



**Ministry of Public Works and Transport
Kingdom of Cambodia**

**GMS: Southern Economic
Corridor Towns Development
Project**

**Loan 2983-CAM(SF), Loan 8265-CAM(SCF)
Grant 0334-CAM (UEIF), Grant 0335-CAM (SCF)**

**Quarterly Report
4th Quarter 2018**

Executing Agency:

**Ministry of Public Works and
Transport (MPWT)
4th Floor Western Building
Corner Norodom Blvd. &
Street #106
Phnom Penh, Cambodia**

Funding Agency:

**Asian Development Bank (ADB)
6 ADB Avenue, Mandaluyong City 1550
Metro Manila, Philippines**

PISCD Consultants:

**NJS Consultants Co. Ltd.
In Joint Venture with
Key Consultants Cambodia, Ltd.
4th Floor, Ministry of Public
Works and Transport
Phnom Penh, Cambodia**



TABLE OF CONTENTS

	<u>Page No.</u>
SECTION 1 INTRODUCTION AND BASIC DATA	1
1.1 PROJECT OVERVIEW	1
1.2 BASIC DATA	2
1.3 REPORTING PERIOD	3
SECTION 2 UTILIZATION OF FUNDS	4
2.1 REVISED PROJECT COST ESTIMATE	4
2.2 LOAN AND GRANT PROCEEDS	4
2.3 CONTRACT AWARDS	5
2.4 DISBURSEMENT	6
2.5 COUNTERPART FUNDS	6
SECTION 3 IMPLEMENTATION PROGRESS	7
3.1 OVERALL PROGRESS	7
3.2 PROCUREMENT	8
3.3 CONSULTING SERVICES	9
3.4 ADOPTION AND IMPLEMENTATION OF THE SLEDP (OUTPUT 1)	12
3.5 IMPLEMENTATION OF PRIORITY URBAN INFRASTRUCTURE INVESTMENTS (OUTPUT 2)	12
3.6 STRENGTHENING OF INSTITUTIONAL CAPACITY	13
SECTION 4 PROJECT PERFORMANCE	15
4.1 GENERAL	15
4.2 ASSESSMENT OF ASSUMPTIONS AND RISKS	15
4.3 PROJECT PERFORMANCE AGAINST THE TARGETS SET OUT IN THE DMF	15
4.4 BASELINE VALUES, PERFORMANCE TARGETS FOR INDICATORS, AND PROJECTED ACHIEVEMENTS	15
SECTION 5 COMPLIANCE WITH SAFEGUARDS AND COVENANTS	16
5.1 ENVIRONMENTAL SAFEGUARDS	16
5.2 RESETTLEMENT	16
5.3 IMPLEMENTATION OF GENDER ACTION PLAN	21
5.4 STATUS OF COMPLIANCE WITH LOAN COVENANTS, AND RISK ASSESSMENT AND RISK MANAGEMENT PLAN	22
SECTION 6 MAJOR PROJECT ISSUES AND PROBLEMS, AND ACTIONS TAKEN	23
SECTION 7 ACTIVITIES FOR THE NEXT STEPS	25



LIST OF APPENDICES

Appendix No.

APPENDIX A	KEY MEMBERS OF PMU AND PIUs
APPENDIX B	REVISED OVERALL PROJECT IMPLEMENTATION PLAN
APPENDIX C	LOANS AND GRANTS UTILIZATION
APPENDIX D	UPDATED PROCUREMENT PLAN
APPENDIX E	LIST OF CAPACITY DEVELOPMENT AND TRAINING CONDUCTED
APPENDIX F	ASSESSMENT OF ASSUMPTIONS AND RISKS
APPENDIX G	DMF TARGETS VS ACHIEVEMENT
APPENDIX H	BASELINE VALUES, PERFORMANCE TARGETS FOR INDICATORS, AND PROJECTED ACHIEVEMENTS
APPENDIX I	PUBLIC INFORMATION BOOKLET
APPENDIX J	GAP IMPLEMENTATION PROGRESS AND PLANS FOR THE NEXT QUARTER
APPENDIX K	STATUS OF COMPLIANCE WITH LOAN COVENANTS
APPENDIX L	RISK ASSESMENT AND RISK MANAGEMENT PLAN (RARMP)
APPENDIX M	SUPPORT DOCUMENTS OF LAND ACQUISITION



LIST OF TABLES

<u>Table No.</u>		<u>Page No.</u>
2.2	Revised Detailed Cost Estimate by Financier (US\$ million)	4
2.2	Consolidated Status of Loan and Grant Proceeds	5
3.1	Completed Contracts, Awarded, Ongoing and Subprojects Changed	8
3.2	Physical and Financial Progress on 31 December, 2018	11
3.3	Dry port and Logistics facility	12
3.4	Ranking of Subprojects, in Order of Priority	12
7.1	WORK PLAN FOR NEXT STEPS (4 th Quarter 2018)	25

LIST OF FIGURES

<u>Figure No.</u>		<u>Page No.</u>
1.1	Location of Three Corridor Towns of CTDP in Cambodia.....	1
2.1	Cumulative Actual Versus Projected Contract Awards	5
2.2	Cumulative Actual Versus Projected Disbursements	6



ABBREVIATIONS AND ACRONYMS

ADB	-	Asian Development Bank
AHs	-	Affect Household
APs	-	Affect People
CS	-	Construction Supervision
CTDP	-	Corridor Towns Development Project
DED	-	Detailed Engineering Design
DMF	-	Design and Monitoring Framework
DMS	-	Detail Measurement Survey
DFEC	-	Declarations of Fraud and Ethical Conduct
EA	-	Executive Agency
EM	-	External Monitoring
EMP	-	Environmental Management Plan
FHH	-	Female Household Head
GAP	-	Gender Action Plan
GDR	-	General Department of Resettlement
GMS	-	Greater Mekong Sub-region
ICB	-	International Competitive Bidding
IEE	-	Initial Environmental Examination
IOL	-	Inventory of Loss
IRC	-	Inter-Ministerial Resettlement Committee
M&E	-	Monitoring and Evaluation
MEF	-	Ministry of Economy and Finance
MPWT	-	Ministry of Public Works and Transport
MRF	-	Material Recovery Facility
NCB	-	National Competitive Bidding
PAHs	-	Project Affect Households
PAP	-	Project-affected People
PISCD	-	Project Implementation Support and Capacity Development
PIU	-	Project Implementation Unit
PMU	-	Project Management Unit
PPMS	-	Project Performance Management System
PPP	-	Public-Private Partnership
PRC	-	Procurement Review Committee
Q	-	Quarter
RGC	-	Royal Government of Cambodia
RP	-	Resettlement Plan
SDR	-	Special Drawing Rights
SEC	-	Southern Economic Corridor
SLEDP	-	Strategic Local Economic Development Plan
URP	-	Update Resettlement Plan
WWT	-	Wastewater Treatment

SECTION 1 INTRODUCTION AND BASIC DATA

1.1 PROJECT OVERVIEW

The Royal Government of Cambodia (RGC) has received loans and grants from the Asian Development Bank (ADB) towards the cost of the Greater Mekong Sub-region (GMS) Southern Economic Corridor Towns Development Project (the Project).

The Project will enhance the competitiveness of towns along the Southern Economic Corridor (SEC). The Project will transform the Cambodian corridor towns of Battambang, Bavet, Neak Loeung, and Poipet (see Figure 1.1) into economic hubs by improving urban-environmental infrastructure and strengthening institutional capacities of provincial and local authorities.

Figure 1.1
Location of Three Corridor Towns of CTDTP in Cambodia



The Project's expected outcome is improved urban infrastructure and enhanced climate resilience in Battambang, Bavet, Neak Loeung and Poipet. The Project will cover ten subprojects comprising: (a) three subprojects in Battambang, i.e. flood protection, wastewater treatment (WWT), and materials recovery facilities (MRF); (b) three in Bavet, i.e. urban roads, WWT, and MRF; (c) one in Neak Loeung, i.e. flood control; and (d) three in Poipet, i.e. WWT, solid waste management, and MRF.



1.2 BASIC DATA

Presented below are the basic Project data.

Project Title:	Greater Mekong Sub-region Southern Economic Corridor Towns Development Project		
Project Number:	43319-033		
Borrower:	Kingdom of Cambodia		
Executing Agency (EA) and Implementing Agencies (IA)	The EA of the Project is the Ministry of Public Works and Transport (MPWT). The EA assumes overall responsibility for the project implementation through the Project Management Unit (PMU). The Provincial Town Governor in each of the four Towns, in cooperation with PMU, has set up the PIUs for the implementation of subproject activities. The key members of the PMU and PIUs are presented in Appendix A .		
Total Project Cost and Financing Plan			
Loan/Grant No.	Source of Funding	Amount (US\$ million)	Share of Total (%)
Loan 2983-CAM (SF)	Asia Development Fund	33.44 ^a	65.3
Loan 8265-CAM (SCF)	Strategic Climate Fund ^b	5.00	9.8
Grant 0335-CAM (SCF)	Strategic Climate Fund ^b	4.40	8.6
Grant 0334-CAM (UEIF)	Urban Environmental Infrastructure Fund Grant under the Urban Financing Partnership Facility ^c	1.50	2.9
	Government of Cambodia	6.87	13.4
	Total Project Cost	51.21	100.0

^a Revised due to the depreciation of the SDR against the US\$.

^b Under the Pilot Program for Climate Resilience financed by the Strategic Climate Fund. The ADB Strategic Climate Fund is administered by the Asian Development Bank.

^c Contributor: the Government of Sweden.

Date of Loan/Grant Approval	10 December 2012
Date of Signing of Agreement	17 January 2013
Date of Effectiveness	08 April 2013
Loan/Grant Closing Date	
Mid-Term Review	31 Dec 2022 (loan period is 9.74 years from date of effectiveness)
Revised	30 June 2021 (loan period is 8.23 years from date of effectiveness)
Original	30 June 2019 (loan period is 6.23 years from date of effectiveness)
Elapsed Loan Period	5.73 years from date of effectiveness (as of 31 December 2018) 59 % of Mid-Term Review revised loan period 70 % of revised loan period 92 % of original loan period
Dates of ADB Review Missions and Mid – Term Review	08 September – 01 October 2014; 01 – 11 December 2015; 09 – 22 August 2016; 18 – 30 October 2017; 21-29 May 2018 and Mid –Term Review 2-30 November 2018



Compared to the original plan, the implementation of the Project has been delayed by about 24 months. This is mainly due to delays in the procurement of detailed engineering design (DED) consultant and the actual preparation of DED and bid documents. Based on this, a proposal for the extension of the loan/grant closing date by 24 months, from 30 June 2019 to 30 June 2021, was prepared by the EA/MEF for approval by ADB.

Following the new priority list and recent experience of each subproject, it is expected that the project will be fully physically completed in 31 December 2022. Based on this, a proposal for the extension of the loan/grant closing date by 18 months, from 30 June 2021 to 31 December 2022, will be prepared by the EA/MEF for approval by ADB. Shown in **Appendix B** is the updated Overall Project Implementation Plan that takes into consideration the 18-month extension of the loan/grant closing date, and the prioritization of subprojects.

1.3 REPORTING PERIOD

This Quarterly Report is for the 4th Quarter of 2018 – October-December 2018 reporting period. It provides a summary of accomplishments during the reporting period, compliance with safeguards and covenants, identifies major issues and concerns and recommends the action required, and lists activities to be carried out in the next quarter.



SECTION 2 UTILIZATION OF FUNDS

2.1 REVISED PROJECT COST ESTIMATE

The Project cost estimate was amended to take into consideration: (i) the reallocation of loan/grant proceeds due to contract awards under some loan categories that already exceeded their allocation, and the prioritization of subprojects such that total cost will be within the available budget; (ii) budget shortfalls arising from the depreciation of the SDR against the US\$; and (iii) extension of loan/grant closing date. **Table 2.1** presents the revised Detailed Cost Estimate by Financier prepared by MEF, and approved by ADB.

Table 2.1
Revised Detailed Cost Estimate by Financier (US\$ million)
Reallocation of Loan and Grant Proceeds as Approved by ADB on 26 January 2017
(Greater Mekong Subregion Southern Economic Corridor Towns Development Project)

No.	Item	ADB Loan *		SCF Loan		SCF Grant		UFPF Grant		RGC				Total
		Amount	%	Amount	%	Amount	%	Amount	%	Nontax	Taxes	Amount	%	
1	Works	25.684	67.2	3.780	9.9	3.270	8.6	1.390	3.6	-	4.097	4.097	10.7	38.221
1A	CW: Wastewater Treatment and Flood Control	16.022	62.2	3.780	14.7	3.270	12.7	-	-	-	2.697	2.697	10.5	25.769
1B	CW: Road and Solid Waste Management	9.662	88.5	-	-	-	-	-	-	-	1.260	1.260	11.5	10.922
	Material Recovery Facilities	-	-	-	-	-	-	1.390	90.8	-	0.140	0.140	9.2	1.530
2	Consulting Services	3.317	69.7	0.739	15.5	0.702	14.8	-	-	-	-	-	-	4.758
2A	Project Implementation Support & CD	1.816	71.1	0.368	14.4	0.371	14.5	-	-	-	-	-	-	2.555
2B	Detailed Engineering Design	0.659	78.0	0.100	11.9	0.085	10.1	-	-	-	-	-	-	0.845
2C	Construction Supervision	0.730	58.6	0.270	21.7	0.246	19.7	-	-	-	-	-	-	1.246
2D	External Monitoring	0.113	100.0	-	-	-	-	-	-	-	-	-	-	0.113
3	Equipment	0.416	100.0	-	-	-	-	-	-	-	-	-	-	0.416
4	Training	0.136	100.0	-	-	-	-	-	-	-	-	-	-	0.136
5	Incremental Administration	0.651	50.7	0.001	0.1	0.001	0.1	-	-	0.630	-	0.630	49.1	1.283
5A	Project Management Unit	0.325	99.2	0.001	0.4	0.001	0.4	-	-	-	-	-	-	0.328
5B	Project Implementation Unit	0.325	100.0	-	-	-	-	-	-	-	-	-	-	0.325
5C	Salary Supplements	-	-	-	-	-	-	-	-	0.630	-	0.630	100.0	0.630
	Land Acquisition and Resettlement	-	-	-	-	-	-	-	-	1.650	-	1.650	100.0	1.650
6	Unallocated	2.427	62.1	0.467	11.9	0.427	10.9	0.110	2.8	0.096	0.385	0.481	12.3	3.910
7	Interest During Construction	0.810	98.4	0.013	1.6	-	-	-	-	-	-	-	-	0.823
	Contingency	-	-	-	-	-	-	-	-	-	-	-	-	-
	Total	33.440	65.3	5.000	9.8	4.400	8.6	1.500	2.9	2.376	4.482	6.858	13.4	51.198

* 1 SDR = 1.392 US\$

2.2 LOAN AND GRANT PROCEEDS

Loans and grants utilization by category, as of 31 December 2018 are indicated in **Appendix C**, and consolidated in **Table 2.2**.



Table 2.2
Consolidated Status of Loan and Grant Proceeds


Loan/Grant No.	US Dollars					
	Allocation	Contracts Awarded	Uncontracted Loan Balance	Contracts Disbursed	Undisbursed Loan Balance	Undisbursed Contract Balance
	A	B	C = A - B	D	E = A - D	F = B - D
Loan 2983	33,452,021	17,872,972	15,579,049	7,350,723	26,101,297	10,522,249
Loan 8265	5,000,000	2,272,945	2,727,055	997,847	4,002,154	1,275,098
Grant 0334	1,500,000	1,500,000	-	1,350,000	150,000	150,000
Grant 0335	4,400,000	2,901,614	1,498,386	1,191,896	3,208,104	1,709,718
Total	44,352,021	24,547,531	19,804,489	10,890,466	33,461,554	13,657,065

2.3 CONTRACT AWARDS

During Q4 2018, no contract awards works were undertaken. As of 31 December 2018, the contracts awarded by PMU amounted to US\$24.55 million, or 55% of total loan and grant amount. **Figure 2.1** shows the S-curves of the cumulative actual contract awards and original and revised projections/targets. The revision of the targets was made based on the approved reallocation of loan/grant proceeds, and updated procurement plan.

According to the Mid-Term Review Mission, the PAM will be updated to reflect the changes specified in the MTR's MOU, including the change of scopes, project implementation schedule, financing and disbursement arrangements, CAD projections, procurement plan and DMF.

Figure 2.1
Cumulative Actual Versus Projected Contract Awards

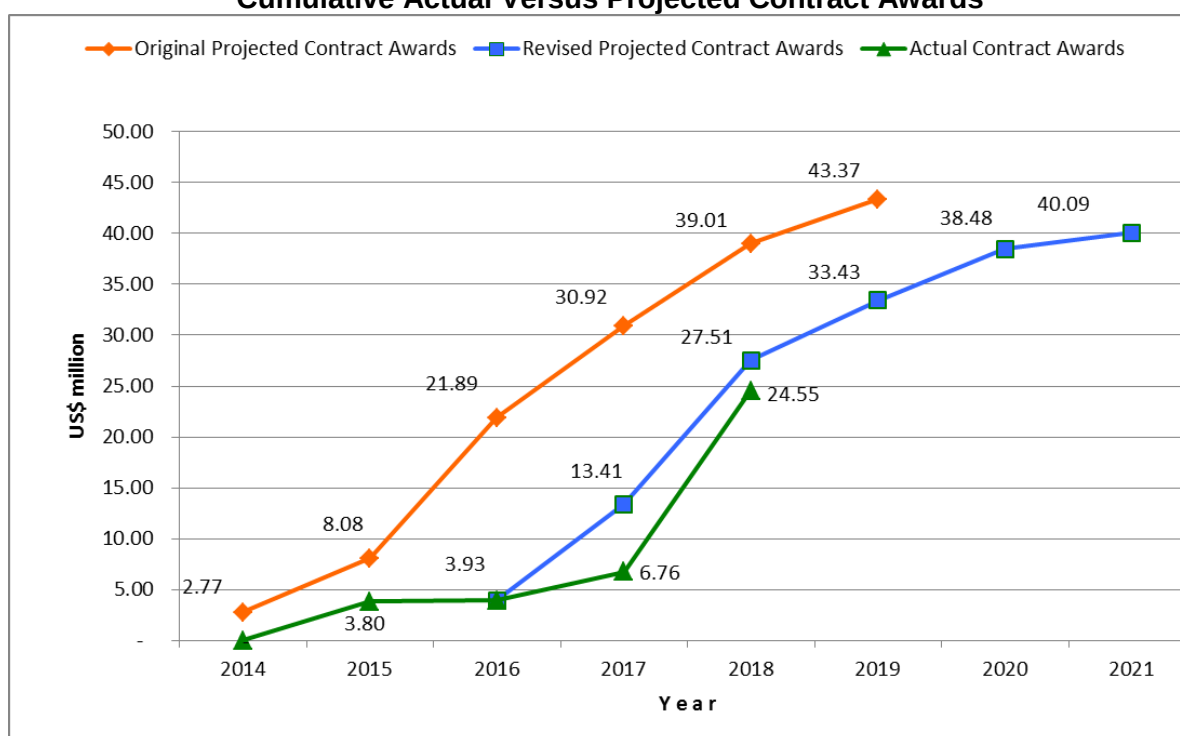




2.4 DISBURSEMENT

Disbursements during Q4 2018 were made through direct payment of PISCD consulting services, construction supervision, Incremental Admin – PMU/PIUs, Material Recovery Facility. So far, a total of US\$10.890 million, or 44% of total contract awards, has been disbursed. This is equivalent to 25% of total loan and grant amount. The S-curves of the cumulative actual disbursements and original and revised projections/targets are shown in **Figure 2.2**. The revision of the targets was made based on the revised projected contract awards and the revised overall project implementation plan.

Figure 2.2
Cumulative Actual Versus Projected Disbursements

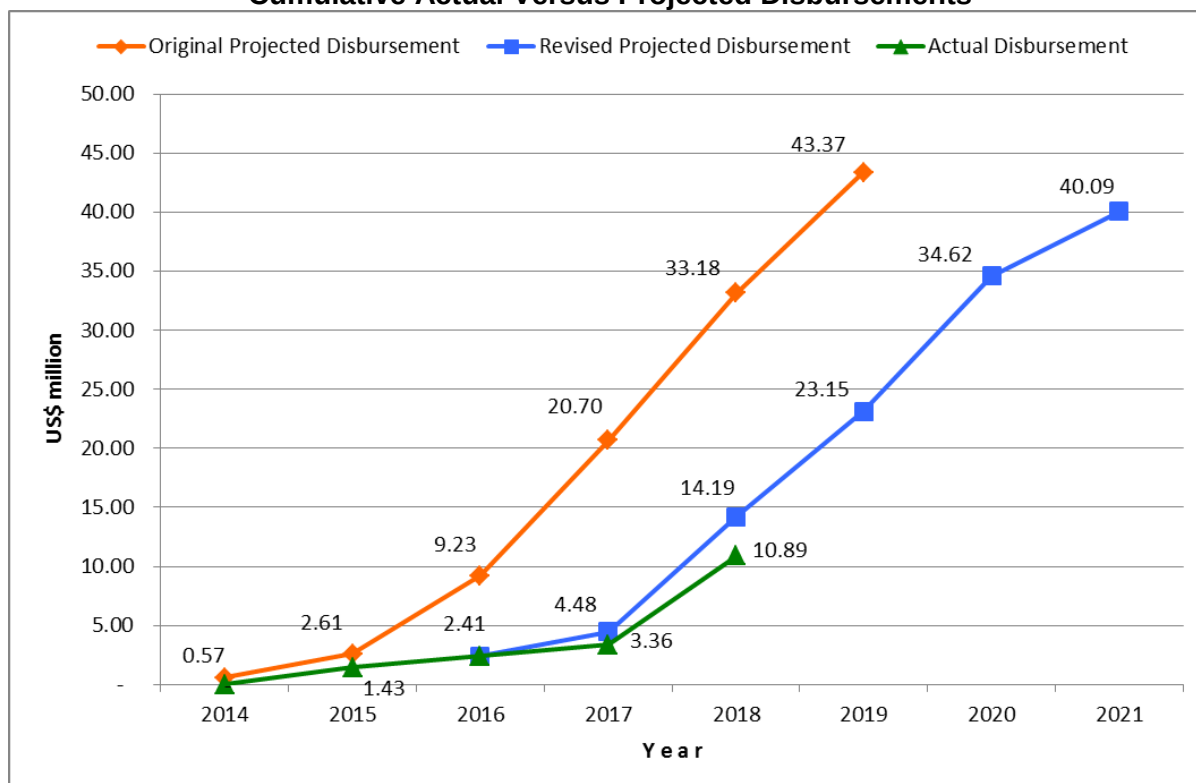

2.5 COUNTERPART FUNDS

The replenishment of RGC counterpart imprest account was made during the reporting period is US\$13,674.65 PMU and PIU staff allowances were paid from the account's balance of the previous quarter. As of 31 December 2018, the total counterpart funds released to the Project was US\$263,432.85 or 4 % of total government contribution.



SECTION 3 IMPLEMENTATION PROGRESS

3.1 OVERALL PROGRESS

As of 31 December 2018, the estimated disbursement of the project is 25% and the estimated physical completion of the Project was about 59%; while the time elapsed from effectiveness date was 59 % of Mid-Term Review revised loan period and 70 % of revised loan period (92% of the original loan period). The physical completion is indicated as a percentage derived from the estimate of the weight contributed by each activity as a percentage of the total project, consistent with the S-curve concept. The S-curve will be updated after update of PAM.

Civil Work:

The construction of material recovery facilities in the three towns has been completed 100%. The constructions of urban road in Bavet town and wastewater treatment (storm drainage) in Battambang are in progress. The estimate of physical progress wastewater treatment storm drainage is 39% and urban road in Bavet is 20%.

Field Activities, Meeting and Other:

Kick-off meeting of ADB Mid-Term Review Mission was conducted at ADB resident on 02 November 2018, with the Executing Agency (EA), Project Implementation Project (PMU), Project Implement Support and Capacity Development (PISCD) and Ministry of Economy and Finance (MEF). The objectives of the Mission were to discuss: (i) overall implementation progress, (ii) change in scopes, (iii) implementation arrangements, revised implementation schedule, loan/grant closing date, (iv) reallocation of loan/grant proceeds, (v) contract awards and disbursements (CAD) projections and Design Monitoring Framework (DMF) updates to reflect the changes, including updated procurement plan, (vi) safeguards impacts reassessment and updates, (vii) Gender Action Plan (GAP) implementation updates, (viii) good governance framework update, (ix) status of compliance with loan covenants, and (x) consultants' performances and other implementation supports to expedite the Project implementation progress to reach the Project objectives.

Wrap-up meeting of ADB Mid-Term Review Mission was conducted at ADB resident on 30 November 2018, with the Executing Agency (EA), Project Implement Support and Capacity Development (PISCD) and GDR/MEF. The wrap-up meeting was discussed all implementation progress and mission findings.

On 5-7 and 12-13 November 2018, the mission team (ADB, EA, PISCD, PMU/PIU and GDR/MEF) visited the completed MRFs at Battambang, Bavet and Poipet, visited urban storm water drainage in Bavet and Poipet and visited urban storm water drainage construction in Battambang and road construction in Bavet. The mission team met with contractors and organized meeting at PIU offices, the meeting discussed on civil work construction, environmental and social safeguards and any finding during visited.

Environmental and Social Safeguard & Gender and Training Program:

Activities of Strengthening of Institutional Capacity (see Subsection 3.6) Environmental Safeguards (see Subsection 5.1), Resettlement (see Subsection 5.2), Implementation of



Gender Action Plan (see Subsection 5.3) and Assessment of Project Performance through PPMS (see Section 4).

3.2 PROCUREMENT

The Project involves the procurement of: (i) civil works with an estimated amount of \$38.22 million; (ii) consulting services, \$4.76 million; (iii) goods and equipment, \$0.42 million; and (iv) training, \$0.14 million.

Material Recovery Facilities (MRFs) in BTB, Bavet and Poipet were completed contracts. The procurement of WWT (storm drainage) in Battambang (CW 06) and urban road in Bavet (CW 05) was signed on 30 January 2018 and 28 February 2018. WWT (storm drainage) in Poipet (CW07) and Bavet (CW8) were awarded contracts or seeking no-objection from ADB to award contract or to draft bidding documents. Neak Loeung Flood Control subproject (CW10) is expected to bid out in Q3 2019.

3.2.1 Awarded and Ongoing, and Completed Contracts

In Q4 2018, some activities were undertaken, as of end of Q4 2018, the status of procurement was as follows:

- Consulting services 7 contracts awarded: (i) PISCD Consultant (ongoing), (ii) DED Consultant (contract expired), (iii) Procurement Specialist (ongoing), (iv) Financial Specialist (ongoing), (v) Construction Supervision (ongoing), (vi) Environmental Specialist (ongoing) and (vii) External Monitoring (ongoing). The recruitment of all consulting services has been completed
- Goods and Works all 6 contracts awarded and completed.
- Civil works

Table 3.1:
Completed Contracts, Awarded, Ongoing and Subprojects Changed

Package Number	Completed Contracts		Remark
CW2 CW3 CW4	MRFs awarded and completed (Battambang, Poipet and Bavet).		
	Ongoing Contracts		
CW05	Urban Road awarded and completed (Bavet).		
CW06	WWT awarded and completed (Storm Water Drainage in Battambang)		
	Contracts Awarded		
	Last Progress (Q3 2018)	Progress to Date (Q4 2018)	
CW07	WWT evaluated bids and submitted to ADB for NOL (Storm Water Drainage in Poipet)	The bids evaluation report (BER) was submitted to the ADB on 30 April 2018	
CW08	WWT bid documents are being prepared and will be advertised during Q4 2018 (Storm Water Drainage in Bavet)	The drafted bidding document was reviewing by the ADB	
CW10	Neak Loeung Flood Control Dike	CW10 is expected to bit out in Q3 2019	



	Subprojects Changed	
CW09a and CW12	WWTP and Sewerage in Poipet Town proposed Multi-tranches Financing Facility (MFF) for the Water Supply and Sanitation Investment Program in 2020.	
CW13	WWTP and Sewerage in Battambang included in the Second Urban Environmental Management in Tonle Sap Basin Project (Loan 3684-CAM).	

3.2.2 Updated Procurement Plan

Due to budget shortfalls resulting from the depreciation of SDR, and underestimation of scope of civil works and cost of construction materials in the feasibility study, the EA and ADB foresee that not all of the subprojects could be covered under the current budget situation. The subprojects were therefore prioritized and an updated procurement plan (**Appendix D**) was prepared and agreed upon by the EA and ADB. During Mid-Term Review Mission Procurement Plan will update 1st quarter 2019.

3.3 CONSULTING SERVICES

To provide support during Project implementation, the following consultants are engaged: (i) Project Implementation Support and Capacity Development (PISCD), (ii) Detailed Engineering (DED) Consultant, (iii) Construction Supervision (CS) Consultant, (iv) External Monitoring (EM) Consultant, (v) Procurement Specialist, and (vi) Financial Specialist.

3.3.1 Project Implementation Support and Capacity Development (PISCD)

Contract No. ICB/MPWT/PMU/CTDP1/001 between the Ministry of Public Works and Transport and NJS Consultants Co., Ltd. in Joint Venture with Key Consultants (Cambodia) Ltd. was signed on August 4, 2014. The consultant began mobilizing the consulting team by August 15, 2014.

Activities of the PISCD Consultant included assisting the PMU with Procurement (see Subsection 3.2), Detailed Engineering Design (see Subsection 3.3.2), Strengthening of Institutional Capacity (see Subsection 3.6) Environmental Safeguards (see Subsection 5.1), Resettlement (see Subsection 5.2), Implementation of Gender Action Plan (see Subsection 5.3) and Assessment of Project Performance through PPMS (see Section 4).

The PISCD Consultants have also assisted PMU in the preparation of this Quarterly Report.

3.3.2 Detailed Engineering Design (DED)

During the reporting period, DED documents of all priority subprojects previously identified such as storm water drainage in Bavet and Poipet were fully completed in Q3 2018. DED document of Neak Loeung Flood Control subproject will procure next year (2019). Flood Control and WWTP/sewerage in BTB, WWTP/sewage in Bavet and solid waste management in Poipet are deferred because of inadequate budget.

3.3.3 Construction Supervision (CS)

CS Consultant started to work in the middle of February 2018, and joint inspection together with project management unit (PMU) officer, contractor representatives and the team leader / construction supervision consultants' beginning of the month March 2018 on construction activity & progress work of contractors that construction of civil works. As of 31 December 2018, construction activity & progress work as follow:

- a) Material Recovery Facility



- Material Recovery Facility – Battambang (CW 02) progress activities is 100%
- Material Recovery Facility – Bavet (CW 03) progress activities is 100%
- Material Recovery Facility – Poipet (CW 04) progress activities is 100%

The constructed and completed MRF Buildings at the above three locations were handed over to the relevant authorities / MPWT by on August 24, 2018.

b) Construction of Wastewater treatment sub project (storm drain) - Battambang

The contractor has mobilized to the site on March 13, 2018 and started to build temporary offices, labour quarters, material yard etc. Construction work is in progress.

Overall Physical Progress 39%

Construction Activity & Progress of work:

1. RC Box Drains along line L1 – 1 & L1 - 4 is in progress
 - Install steel shoring along some box culvert trenches.
 - Excavation and laying of screed concrete for box drains.
 - Installation of rebar / form work / casting of box drains.
 - Casting of pre-cast cover slabs / catch basins and placing at site.
 - Construction of catch basins and manholes.
 - Back filling earth and compaction on excavated trenches.
2. RC Pipes along line L1 – 2, L1 – 3, L1 – 3a & L1 – 4a is in progress.
 - Excavation and laying of screed concrete.
 - Laying of RC pipes.
 - Construction of catch basins and manholes.
 - Back filling earth and compaction on excavated trenches.

c) Construction of Urban Road – Bavet (Pk 2+400 to 8+545 m)

The contractor has mobilized to the site on March 19, 2018. Construction Activity & Progress of work (Only the Free re-settlement Area)

Overall Physical Progress 20%

Construction Activity & Progress of work

- Road way clearing, excavation and remove unsuitable material along the road sections (Pk 2+400 - 4+060 m and Pk 5+470 - 6+800 m).
- Embankment / Sub grade / Sub base material filling / compaction along the road sections (Pk 2+400 - 4+060 m and Pk 5+470 – 6+800 m).
- Laying of RC pipes dia. 600 mm, 800 mm & 1000 mm – 5700 m length is completed.
- Construction of Box Culvert at Pk 2+580 m, 5+510 m, 6+380 m & 7+320 m.
- Casting of pre-cast RC catch basins / manholes.
- Continuing delivery of materials such as embankment filling / ABC material etc. to the site and stock at the site yards.

The Physical & financial progress of subprojects is shown in **Table 3.2:**



Table 3.2:
Physical and Financial Progress on 31 December, 2018

Package No.	Name of the sub project	Date of commencement of work	Contract Amount (USD)	Work Done Amount (USD)	Financial Progress		Physical Progress	
					Target	Actual	Target	Actual
CW 02	Battambang Material Recovery Facility	25-Jul-17	424,991.84	459,617.55	Completed		100%	100%
CW 03	Bavet Material Recovery Facility	25-Jul-17	389,826.64	409,719.29	Completed		100%	100%
CW 04	Poipet Material Recovery Facility	25-Jul-17	359,571.12	630,663.16	Completed		100%	100%
CW 05	Bavet Urban Road Improvement	19-Mar-18	7,674,956.00	1,525,000.00	58.38%	19.87%	50%	20%
CW 06	Battambang Wastewater Treatment	01-Apr-18	9,368,943.03	3,575,000.00	34.00%	38.16%	40%	39%

3.3.4 External Monitoring (EM)

External Monitoring is part of the Safeguards Monitoring for the Project. Environmental and Social Safeguards are to be monitored during the pre-construction, construction and post-construction periods. The MEF has engaged an external monitoring consultant to provide EM for resettlement activities and implementation of the Resettlement Plan (RP). The MPWT has engaged one National Environmental Specialist to provide EM of the implementation of the Environmental Management Plan (EMP). As of 31 December 2018 External Monitoring implemented of the activity as follow:

Semi-annual social safeguards monitoring reports for the project should be submitted as part of the internal monitoring of resettlement activities by the GDR/Department of Internal Monitoring and Data Management (DIMDM). DIMDM will prepare a consolidated report to reflect progress to date and submit it to ADB. The same report will also be shared with the External Monitoring Organization(EMO) for verifying information produced through the project monitoring process and facilitating the carrying out of any verification activities as stated in Schedule 5, para 9 (c) of the loan agreement.

Semi-Annual Environment Safeguards Monitoring Report covering the period July to December 2018 was finalized and will submit to ADB by 15 January 2019.

3.3.5 Financial and Procurement Specialists

The Financial and Procurement Specialists who are directly contracted by the PMU (since 10 June 2016) are responsible for the preparation of quarterly financial management report, and procurement report, respectively.



3.4 ADOPTION AND IMPLEMENTATION OF THE SLEDP (OUTPUT 1)

The SLEDPs for Bavet, Battambang and Poipet, which were all prepared in 2011, were reviewed by relevant Government agencies and provincial authorities, and adopted by these agencies/authorities.

The SLEDPs adopted by these agencies/authorities as following:

1. Battambang adopted on March 2017
2. Bavet adopted on February 2017
3. Poipet adopted on June 2018
4. Neak Loeung December 2014 (District level) and March 2018 (Commune level)

There were activities related to Public-Private Partnership (PPP) Initiatives during the 4th Quarter 2018. The proposed PPP projects include Dry Port and Logistics Facility in Poipet and Bavet. Based on SLEDPs in each town and interviewed with PIUs, dry port and logistics facility are described in the table 3.3 below:

Table 3.3:
Dry port and Logistics facility

No.	Town	PPP	Remark
1	Poipet	3 dry ports, 10 logistic facility and 4 special economic zones	Five years development plan and PIU interview
2	Bavet	4 dry ports, 1 logistic facility and 4 special economic zones	Five years development plan and PIU interview

3.5 IMPLEMENTATION OF PRIORITY URBAN INFRASTRUCTURE INVESTMENTS (OUTPUT 2)

Considering that the priority three MRFs was completed of construction, two priority subprojects was constructed of civil works, three subproject is in processing of procurement and some subprojects are deferred.

It was agreed by the EA and ADB that the criteria for the prioritization of subprojects be based on the importance and urgency of works to be done, and readiness in terms of safeguards requirements and detailed engineering designs. The agreed ranking of subprojects, in order of priority, is shown in **Table 3.4**:

Table 3.4
Ranking of Subprojects, in Order of Priority

Rank	Package	Subproject	Readiness
1	CW02	Battambang Material Recovery Facility	No potential safeguards issues as MRF located adjacent to the existing dumpsite that land belong to Battambang town (which has no potential safeguards issue).



2	CW04	Poipet Material Recovery Facility	The proposed MRF site is located on a public land proposed for the landfill. This land is currently utilized as source of borrow materials and has recently been almost completely excavated. The MRF site therefore was relocated south of the proposed landfill. The PIU has already acquired lands for new site of the MRF. IRC/MEF purchase land from land owner on 03 August 2017 for MRF construction (support document see in Appendix M).
3	CW03	Bavet Material Recovery Facility	The PIU is now in the process of acquiring a land south of National Road no.1 for the new site of the MRF. Reference letter No.013 dated 04 May 2018, Bavet Governor provide land 20 ha for construction of MRF and WWTP (support document see in Appendix M).
4	CW06	Battambang Wastewater Treatment (Drainage)	The construction activity & progress of work only the free re-settlement area. IRC will compensate affected people.
5	CW07	Poipet Wastewater Treatment(Drainage)	Verification DMD's Data for Poipet to reducing Resettlement Cost. IRC will compensate all affected people.
6	CW05	Bavet Urban Roads	The construction activity & progress of work only the free re-settlement area. IRC will compensate affected people.
7	CW09b	Poipet Solid Waste Management	The implementation of this subproject is deferred.
8	CW09a	Poipet Wastewater Treatment(Sewerage)	Sewerage in Poipet Town proposed Multi-tranches Financing Facility (MFF) for the Water Supply and Sanitation Investment Program in 2020. MEF letter No.4755 dated 31 May 2018, MEF purchase land for pumping station construction (Support document see in Appendix M).
9	CW12	Poipet Wastewater Treatment (Mechanical Wastewater Treatment plant)	WWTP in Poipet Town proposed Multi-tranches Financing Facility (MFF) for the Water Supply and Sanitation Investment Program in 2020. MEF letter No.4755 dated 31 May 2018, MEF purchase land for WWTP construction (support document see in Appendix M)
10	CW8	Bavet Wastewater Treatment (Drainage)	The drafted bidding document was reviewing by the ADB

3.6 STRENGTHENING OF INSTITUTIONAL CAPACITY

The capacity development program is intended to ensure smooth implementation of urban infrastructure and to provide sustainable capacity development. During Q4 2018, no capacity development was conducted.



So far, a total of 24 training were conducted by the PISCD Consultant, 434 participants attended in the training program, 78 of them are women, a complete list of which is presented in **Appendix E**.

The training course on Environmental Management and Monitoring Plan was conducted at contractor's campsite in Battambang on 19-20 July 2018. There are 18 participants from PMU, PIUs, CS and contractors from Battambang, Bavet and Poipet attended in training program.



SECTION 4 PROJECT PERFORMANCE

4.1 GENERAL

Project performance M&E includes tracking progress from the baseline situation against the targets and the indicators identified in the DMF, and assessing progress toward achieving the respective result level outputs, outcome and impact.

In this Project, although outputs, outcome and impacts will be achieved only as subprojects are completed (some of the subprojects sooner, others later; some fully, others partly), it is necessary to assess the likelihood or degree of the achievement of outputs, outcome and impact already during implementation. The subjectivity of the judgments involved can be reduced by taking into account the implementation progress and, equally important, by realistically reassessing the assumptions and risks that affect outputs and development objectives.

4.2 ASSESSMENT OF ASSUMPTIONS AND RISKS

Assumptions and risks are the external factors which cannot be controlled by the project manager or the executing agencies, but which influences the success of project implementation. These are identified in the DMF. Assumptions explain important conditions that affect project implementation, while risks are the probability or likelihood that key assumptions may not materialize. The assessment of assumptions and risks is presented in **Appendix F**. The main concern at the present is the low level of female participation in the training conducted so far, as compared to GAP target percentage of women participants in capacity development. Meanwhile, at the present is the low level of participation of participants in the training conducted so far, as compared to the target set in DMF.

4.3 PROJECT PERFORMANCE AGAINST THE TARGETS SET OUT IN THE DMF

M&E of performance indicators involves the tracking and assessment of the degree of attainment and sustainability of Project outputs, outcome and impact by comparing actual performance, as measured by its corresponding indicator, to the baseline and performance target.

The Project's performance against the targets set out in the DMF is reported in **Appendix G**. As of 31 December 2018, assessments of progress toward achieving Outputs 1 and 3 are being carried out since the activities toward attaining these outputs have commenced and are ongoing. Progress toward achieving Output 2, Outcome and Impact, however, can only be assessed upon completion of subprojects and during their operation.

4.4 BASELINE VALUES, PERFORMANCE TARGETS FOR INDICATORS, AND PROJECTED ACHIEVEMENTS

The projected achievements of performance target values for the indicators in the project DMF has updated based on the results of civil work to be conducted in the 3rd, 4th quarters of 2017 and year of 2018. The baseline values and performance targets, and projected achievements that need to be updated, are discussed in **Appendix H**.



SECTION 5 COMPLIANCE WITH SAFEGUARDS AND COVENANTS

5.1 ENVIRONMENTAL SAFEGUARDS

Many environmental works were made during the reporting period. As of 31 December 2018, the environmental works were undertaken the activities as following:

One IEE and three EMPs was Revised many times follow the ADB's comments and submitted to ADB to review and revisions, ADB have no-objection to the three updated EMPs on 4 January 2019 for the implementation of three sub-projects. These EMPs were disclosed on ADB project's website on 2 January 2018.

Final draft of IEIA report of Poipet subprojects (WWTP and Sewerage) was passed EIA department and MOE will organize inter-ministry meeting for adopt IEIA report of Poipet subprojects (WWTP and Sewerage) in 3 January 2019.

Environmental monitoring report was done by contractors (urban road in Bavet and WWT in Battambang) and submits to Construction Supervision (CS) to review.

During Mid-Term Review, the mission visited the completed MRFs at Battambang, Bavet and Poipet. The Mission commended that all sites should have power and water supply, separate toilets for men and women and first aid kits should be provided, all sites should have warning signs on hazards and safety instructions in khmer language, open waste separation areas are roofed to avoid exposure of workers and materials to sun/rain, operations and maintenance manuals and capacity building integrating environmental, health and safety requirements, all commends integrated in EMPs and for the contract variation.

The Mission of environmental team met with Contractors in Bavet, Battambang and Poipet to review progress with implementation of EMP requirements. The Mission acknowledged progress made since the last review mission and special safeguard mission against agreed action and made recommendations for further improvement:

- (i) Traffic management and community safety
- (ii) Construction environmental management plan (CEMP)
- (iii) Clean-up following construction
- (iv) Personal Protective Equipment (PPE)
- (v) Sanitary provisions
- (vi) Battambang wastewater
- (vii) Bavet construction camp

5.2 RESETTLEMENT

During the reporting period (October-December 2018) the Resettlement Specialists were undertaken to prepared resettlement progressed as following activities:

1. Bavet Urban Road (CW-05)

Resettlement Plan and DMS

The Resettlement Plan (RP) for the Bavet Urban Road is finalized by national and international consultants based on the comments received from ADB and submitted to PMU/MPWT and GDR. National and international consultants worked closely with GDR at



GDR's Office, GDR officially submitted the RP to ADB for concurrence and disclosure by end of November 2018. GDR conducted consultations with vulnerable affected households, document the consultations and include the documentation of the consultation process in the RP.

Re-analysis DMS data for urban road in Bavet, Re-analysis affected households along both side of road for verify the data follow comments from GDR.

Vulnerable DPs Consultations:

On 12 November 2018, Governors, GDR, PIU and National Resettlement Consultant conducted consultations with the vulnerable DPs, the objective of consultations meeting with the vulnerable DPs are:

- To identify an appropriate alternative livelihood, occupation for Vulnerable Group affected by Resettlement construction in the Bavet towns.
- To identify for all vulnerable group and disruption during construction stage such Business, Jobs, before, during and after construction.
- Raise their concern about Project, supported, Not supported, at the same and other concerns for the Project

With specific activities as follow:

- Did not affected main structures,
- Did not disturb long time their business, they should shift back and continue business
- RGC represented by GDR will have allowance as cash assistant for all vulnerable Group such as APs their income below 33\$permonth, FHH, Elderly and EM that have no supported, but just more time cash assistant as ADB needed to inform to presented by GDR.

Participants:

Actual participants who are attended the public consultation for Bavet towns are as follows:

Town	Female	Male	Total
Bavet	7	8	15

Feedback from the meeting by Vulnerable Group

- Request to contractor keeping access road into their houses;
- Contractor don't be excavate and keep for long time, such as constructed culvert or Drainage;
- Amount 15 vulnerable Group, there are 12 proposed to construction before received the compensation

2. Battambang Drainage System (CW-06)

Resettlement Plan

The updated Resettlement Plan (RP) for the Battambang drainage is finalized by national and international consultants based on the comments received from ADB. National and international consultants worked closely with GDR at GDR's Office, GDR officially submitted



the RP to ADB for concurrence and disclosure by end of December 2018. GDR conducted consultations with vulnerable affected households, document the consultations and include the documentation of the consultation process in the URP.

Vulnerable DPs Consultations:

On 14 November 2018, Governors, GDR, PIU, Chief Office of Land Urban Management and National Resettlement Consultant conducted consultations with the vulnerable DPs, the objective of consultations meeting with the vulnerable DPs are:

- To identify an appropriate alternative livelihood, occupation for Vulnerable Group affected by Resettlement construction.
- To identify for all vulnerable group and disruption during construction stage such Business, Jobs, before, during and after construction.
- To inform all vulnerable Group for entitlement Matrix to receive cash assistant
- Entitlement Matrix for 5AH Landless AHs
- Raise their concern about Project, supported, not supported, at the same and other concerns for the Project with specific activities as follow:
 - a. If Project affected with structures, the Project will compensated base on category of structures or assets
 - b. If Project affected permanently of their business, the Project will have plan for Training Income Restoration Program to those APs.
 - c. RGC represented by GDR will have allowance as cash assistant for all vulnerable Group such as AHs their income below 33\$permonth, FHH, Elderly that have no supported, The Project will provide one-time cash assistant to vulnerable groups as requirement of the Project.

5 AHs Landless:

IRC-WG, Local authorities and Consultant have meeting with 1 landless AH, her name is Orm Savry to inform as follow:

- a. She lives on the Public Land so Project will not compensation for Public land
- b. She will receive compensation for all property affected by Project, based on category their properties at the same others AHs
- c. Will received cash assistant as vulnerable Group
- d. If lose permanently business, the Project will provide Training Income Restoration Program or cash for Training depending number loss
- e. She will receive Transport allowance for relocated structure



- f. She has right to requested Land concession from local authority, by local authorities help to supported process documents
- g. Should proceed requested land concession from now on from local authorities
- h. Should proceed requested land concession from now on from local authorities, Representation here, they are as a part of Provincial Resettlement Sub-committee, they will to proceed document to speed up your requesting.

Participants

Actual participants who are attend the public consultation for Battambang towns are as follows:

Town	Female	Male	Total
Battambang	4	11	15

Feedback from the meeting by Vulnerable Group

- Request to contractor keeping access road into their houses when construction started
- Contractor don't be excavate and keep for long time when constructed culvert or Drainage
- Request informed to affected household in advance, at list one week, based on category of structure before construction started.

3. Poipet Drainage System (CW-07)

Resettlement Plan and DMS:

The updated Resettlement Plan (RP) for the Poipet drainage is finalized by national and international consultants based on the comments received from ADB. National and international consultants worked closely with GDR at GDR's Office, GDR officially submitted the RP to ADB for concurrence and disclosure by end of December 2018. GDR conducted consultations with vulnerable affected households, document the consultations and include the documentation of the consultation process in the URP.

Re-analysis DMS data for Poipet by re-alignment on line 2, and also review on land document to reducing Resettlement Cost, by resettlement cost is higher than construction cost.

Vulnerable DPs Consultations:

On 15 November 2018, MRF/GDR, PIU, Commune Council, Village chief and National Resettlement Consultant conducted consultations with the vulnerable DPs, the objective of consultations meeting with the vulnerable DPs are:

- To identify an appropriate alternative livelihood, occupation for Vulnerable Group affected by Resettlement construction.



- To identify for all vulnerable group and disruption during construction stage such Business, Jobs, before, during and after construction.
- To inform all vulnerable Group for entitlement Matrix to receive cash assistant
- Entitlement Matrix for 5AH Landless AHs
- Raise their concern about Project, supported, not supported, at the same and other concerns for the Project with specific activities as follow:
 - a. If Project affected with structures, the Project will compensated base on category of structures or assets
 - b. If Project affected permanently of their business, the Project will have plan for Training Income Restoration Program to those APs.
 - c. RGC represented by GDR will have allowance as cash assistant for all vulnerable Group such as AHs their income below 33\$permonth, FHH, Elderly that have no supported, The Project will provide one-time cash assistant to vulnerable groups as requirement of the Project.

1 AH Landless:

IRC-WG, Local authorities and Consultant have meeting with 1 landless AH, her name is Orm Savry to inform as follow

- a. She lives on the Public Land, so Project will not compensation for Public land
- b. She will receive compensation for all property affected by Project, based on category their properties at the same others AHs
- c. Will received cash assistant as vulnerable Group
- d. If lose permanently business, the Project will provide Training Income Restoration Program or cash for Training depending number loss
- e. She will receive Transport allowance for relocated structure
- f. She has right to requested Land concession from local authority, by local authorities help to supported process documents
- g. Should proceed requested land concession from now on from local authorities

Participants

Actual participants who are attended the public consultation for Poipet towns are as follows:

Town	Female	Male	Total
Poipet	3	3	6



Feedback from the meeting by Vulnerable Group:

- Request to contractor keeping access road into their houses
- Contractor don't be excavate and keep for long time, such as constructed culvert or Drainage

5.3 IMPLEMENTATION OF GENDER ACTION PLAN

During the reporting period the Gender Specialist was remobilized, the Gender Specialist accomplished of implementation of Gender Action Plan as following activities:

Accomplishments (Oct.-Dec 2018)

- Conducted Employment Market Assessment (EMA) for Women in Poipet, Battambang, and Bavet through the methodologies are employed to collect information for this EMA including conducting desk review, Conduct online research, Conduct distance and face-to face consultation. The EMA was prepared for the SECTD with three different purposes as follows:
 - 1- Review Cambodian women's existing literacy rates/absorptive capacities of three towns.
 - 2- Assess the current employment market to identify high potential growth sectors and employment trends where quality, sustained, and appropriated employment can be created to support women who are living in project areas.
 - 3- Assess and identify existing institution/NGOs for providing vocational/livelihood training skills in the three towns. The assessment findings will be presented to the relevant NGOs/CSOs to seek for training support as required by the waste pickers and affected female head of households.
- Conduct the Public Consultation on Alternative Livelihood to learn about the alternative livelihood among 184 of affected households and waste pickers of Battambang, Poipet and Bavet Towns. The consultation findings will be presented to the relevant NGOs/CSOs, to seek for training support as required by the waste pickers and affected households.
- Develop TOT activity design on Health and Sanitation Promoter is focused on building concept of hygiene and sanitation; developing communication/facilitation/interpersonal skills for selected health and sanitation promoters, PDWA and PIUs of the 4 towns (Poipet, Battambang, Neak Loeung, and Bavet) is proposed for implementation and will be held in first quarter of 2019.
- Keep monitor how civil work contractors mobilize unskilled women in the construction work. Support civil work to ensure that the gender action targets on 30% women unskilled laborers.
- Support PMU to work with contractor in Battambang to review proposal and negotiated with individual consultant who submitted proposal to conduct training on HIV awareness to construction workers, women and girls in the project area.



GAP Implementation Progress is presented in **Appendix J**

5.4 STATUS OF COMPLIANCE WITH LOAN COVENANTS, AND RISK ASSESSMENT AND RISK MANAGEMENT PLAN

There are 35 key loan covenants, out of which fourteen (28) are complied, two (2) are complied with, three (3) are compliance ongoing, one (1) is partly complied and one (1) is not yet due for compliance. The list of covenants under relevant categories and their status of compliance as of December 31, 2018 is provided in **Appendix K**.

The status of compliance with the Risk Assessment and Risk Management Plan is presented in **Appendix L**.



SECTION 6

MAJOR PROJECT ISSUES AND PROBLEMS, AND ACTIONS TAKEN

The major project issues and problems encountered, and actions taken during Q4 2018 were:

Issues/Problems	Action Taken
1. Budget shortfall due to the depreciation of the SDR against the US\$, and underestimated scope of civil works and cost of construction materials in the feasibility study.	• EA and ADB agreed to the prioritization of subprojects such that total cost will be within the available budget. • EA & ADB agreed to the reallocation of loan/grant proceeds.
2. Compared to the original plan, the implementation of the Project has been delayed by about 42 months. The likelihood is high that civil works may not be completed within the remaining loan period.	• An ADB Mid-Term Review proposed for the extension of the loan/grant closing date by 42 months, from 30 June 2019 to 30 December 2022, will be prepared by the EA/MEF for approval by ADB.
3. Bidding documents of storm water drainage in Bavet and Poipet delayed by safeguard documents is not finalized.	• Environmental and Resettlement specialists will accelerate work activities relate environmental and resettlement documents for approval by ADB, MOE and MEF.
4. The resettlement process not yet completed both WWT sub project at Battambang and Urban road construction project at Bavet. This matter mainly interrupted progress of work at Bavet.	• In this circumstances, both contract period have to be extended depend on the resettlement process completed date.
5. Follow the GAP, the total number per town could not be 500 for organize training for women due lack of the participants and limited budget.	• Propose training for women to better position their entry in the growing employment demand areas arising from project interventions, targeting at least 200 women. The training shall target only vulnerable women who express interest in skill development training with an estimation of 200 women including the entire female waste picker.
6. A target of 90% women for employing existing informal waste pickers in the material recovery facilities (MRFs) funded under the project, including skills upgrade training is high.	• Propose new target of 40% women for employing existing informal waste pickers in the material recovery facilities (MRFs) funded under the project, including skills upgrade training. Because two baseline data of waste picker in dump sites collected in January and October 2018 shows that number of female waste picker varied between 36% and 50%.
7. Ensure that 30% of the overall staff positions and 30% of the management positions in the PMU and PIU to be female.	• Propose new target of 20% overall staff positions and 20% of the management positions in the PMU and PIU to be female.



8. Each MRF is not yet connected to water and power and does not have roof on top of the waste separation area

- These additional works will finance from the savings of other loans. It was agree that MEF will send a letter to ADB requesting for reallocation of loan proceeds to finance additional works of the three subprojects which were originally 100% funded by G0334-CAM.
- Already instructed the contractor to prepare & submit detail drawings and cost estimates for the additional works under MRF
- At presently, the contractor has preparing detail drawings and cost estimates for the additional works which are proposed by the ADB mission team. They will submit within a week time.



SECTION 7 ACTIVITIES FOR THE NEXT STEPS

The work plan for the next steps is presented in **Table 7.1**.

Table 7.1
WORK PLAN FOR NEXT STEPS (4th Quarter 2018)

Main Task	Activities to be Carried out	Responsible	Agreed Due Date
Civil Work	Construction supervision and coordination works for implementation of Battambang, Poipet and Bavet Sub-projects.	PISCD & CS Consultant	Q1 2019
DED	DED of Neak Loeung Flood Control subproject.	PISCD	Q1 2019
Procurement	- Sign contract for Bavet Storm Drain Subproject - Sign contract for Poipet Storm Drain Subproject - Bid document preparation Neak Loeung Flood Control (CW10) - Update procurement plan	Procurement Specialist	Q1 2019
Implementation of Gender Action Plan	- Continues support PMU to work with contractors in Bavet for hire Individual/NGO to conduct training on HIV awareness to construction workers, women and girls in the project area of Bavet. - Finalize the Employment Market Assessment (EMA) for women in Poipet, Battambang, and Bavet. - Preparation and conducting TOT on Health and Sanitation Promoter to selected health and sanitation promoters, PDWA and PIUs of the 4 towns (Poipet, Battambang, Neak Loeung, and Bavet) is proposed for implementation and will be held in March 2019. - Assist PIU to monitor civil work contractors regarding core labor issues and unskilled women in construction.	PISCD Social Safeguards & Gender Specialists	Q1 2019
Resettlement	Revise URP Poipet follow comments from GDR and ADB, and finally URP Poipet will submit	PISCD Resettlement Specialists	Q1 2019



Main Task	Activities to be Carried out	Responsible	Agreed Due Date
	to GDR and ADB - Revise URP Battambang follow comments from GDR and ADB, and finally URP Battambang will submit to GDR and ADB - Updated Resettlement Plan for Bavet, after ADB approved Popet as formatting		
Environmental Safeguards	- Follow up and attend inter-ministry meeting for adopt IEIA report of Poipet subprojects (WWTP and Sewerage). - Updated IEE and EMP Neak Loeung Flood Control subproject - Conduct training to new contractors in Bavet and Poipet - Subproject information disclosure to communities at Bavet and Poipet urban storm water drainage - Reviewed contractor's environmental monitoring report - Prepare second–annual environmental monitoring report covering period July to December 2018	PISCD Environmental Safeguards Specialist	3 January 2019. Q1 2019
PPMS	- Updating of projected accomplishments of performance, baseline and target values. - Data collection/information for prepare draft of 1st quarterly report 2019	PISCD PPMS Specialist	Q1 2019



APPENDIX A

KEY MEMBERS OF PROJECT MANAGEMENT UNIT AND PROJECT IMPLEMENTATION UNITS

A.1 Key Members of Project Management Unit

PMU Member	Project Responsibility	Phone
1. H.E. Vong Pisith	- Project Director	012 833 411
2. Mr. Pou Manith	- Procurement Officer	012 803 203
3. Ms. Thap Solini	- Financial Officer	
4. Mr. Vong Rada	- Technical Officer and Gender Focus Point	012 451545
5. Mr. Vong Litet	- Social & Environmental Affairs	
6. Mr. Chay Vila	- Municipal Development Planning	092 443 434
7. Mr. Sros Sitharith	- Impact Assessment	
8. Mr. Pal Piseth	- General Administrator	
9. Mr. Nuon Sikheng	- Liaison Officer	
10. Mr. Ung Sa Em	- Driver	
11. Mr. Nget Chan Goeun	- Driver	
12. Mr. Mao Chansok	- Driver	
13. Mrs. Srey Chea	- Office Support	

A.2 Key Members of Project Implementation Units

PIU Member	Project Responsibility	Phone
Battambang		
1. Mr. Chan Sambo	- Chief of PIU	092 930 966
2. Mr. Dy Pao	- Deputy Chief of PIU	
3. Mrs. Kem Sokuntheary	- Administrative & Financial Officer	092 818017
4. Mr. Prounh Rith Tha	- Technical Officer	
5. Mr. Song Soeung	- Technical Officer	012 975 250
6. Mr. Nou Chamroeun	- Urban Development Plan	017 339 986
7. Ms. Sok Kinna	- Social & Environmental Officer	012 479 030
8. Mrs. Toun Bopha	- Impact Assessment	
9. Mr. Nou Chhorvivann	- Coordinator and Gender Focus Point	017 260 560





PIU Member	Project Responsibility	Phone
Poipet		
1. Mr. Chea Sovanthoun	- Chief of PIU	012 220 015
2. Mr. Touch Mony	- Deputy Chief of PIU	012 998 998
3. Mr. Chheang Monin	- Technical Officer	
4. Mr. Orn Siphea	- Technical Officer	012 686 196
5. Mr. Sok Penhnane	- Urban Development Plan	
6. Ms. Chhay Vannin	- Administrative & Financial Officer	012 509 158
7. Mr. Sang Sony	- Social & Environmental Officer	077 319 444
8. Ms. Sophal Leaphea	- Impact Assessment and Gender Focus Point	017 622 270
9. Mr. Rinh Bunchhuoy	- Coordinator	
Neak Loeung		
1. Mr. Kry Rathat	- Chief of PIU	012 497 374
2. Mr. Yaem Pheara	- Deputy Chief of PIU	097 249 3342
3. Mr. Nhem Sokheoun	- Technical Officer	
4. Mr. Chheung Choeun	- Urban Development Plan	
5. Mr. Khorn Phy	- Social & Environmental Officer	
6. Mrs. Phat Sreysros	- Gender & Public Campaign Officer	093 427 117
7. Mr. Prak Sareth	- Impact Assessment	
Bavet		
1. Mr. Noun Lihoun	- Chief of PIU	012 707 616
2. Mr. Ung Sa	- Deputy Chief of PIU	
3. Mr. Yun Raksmeay	- Technical Officer	
4. Mr. Sok Sophal	- Administrative & Financial Officer	097 751 6364
5. Mr. Keo Sarang	- Social & Environmental Officer and Gender Focus Point	088 6440544
6. Mr. Kham Rithy	- Urban Development Plan	097 481 1801




APPENDIX B

		OVERALL IMPLEMENTING SCHEDULE																																																							
		2013				2014				2015				2016				2017				2018				2019				2020				2021				2022				2023															
		1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2														
	Loan Signing	■																																																							
	Loan Effectiveness	■																																																							
	RFP for PIS/CD consulting Service			■																																																					
	Proposal due for PIS/CD consulting Service			■																																																					
	Consultant Selection for PIS/CD Consulting Service			■		■																																																			
	Consultant Selection for DED Service					■		■																																																	
	Consultant Selection for Supervision Service							■		■																																															
A	Battambang																																																								
CW02	Materials Recovery Facility																																																								
	1. Preliminary Design Review			■		■																																																			
	2. Detailed Engineering design					■		■																																																	
	3. Land Acquisition and Resettlement							■		■																																															
	- PISCD							■		■																																															
	- GDR Prepare (DDR)											■		■																																											
	- ADB Review and Approval													■		■																																									
	- Monitoring															■		■																																							
	4. Updated IEE/EMP																	■		■																																					
	- PISCD Prepare																	■		■																																					
	- PMU Review																	■		■																																					
	- ADB Review and Approval																	■		■																																					
	- Public Consultation and Information Disclosure																	■		■																																					
	5. Bidding/Contract Award																	■		■																																					
	6. CEMP																	■		■																																					
	- Contractor Prepare																	■		■																																					
	- PISCD Review																	■		■																																					
	- PMU Approve																	■		■																																					
	- Conduct training to contractors' staff																	■		■																																					
	- Monitoring																	■		■																																					
	7. Construction of civil works																	■		■																																					
	8. Procurement of Equipment																	■		■																																					
	9. Construction Supervision																	■		■																																					
	10. DLP																	■		■																																					
	11. Hand Over																	■		■																																					
	12. O&M																	■		■																																					
CW06	Storm Driage (CW06)																																																								
	1. Preliminary Design Review			■		■																																																			
	2. Detailed Engineering design					■		■																																																	
	3. Land Acquisition and Resettlement							■		■																																															
	- PISCD Prepare							■		■																																															
	- GDR Review and Approval											■		■																																											
	- ADB Review and Approval													■		■																																									
	- Public Consultation Meeting Costing													■		■																																									
	- Contract Agreement with APs																	■		■																																					
	- Processing Budget Document																	■		■																																					
	- Pay Compensation to APs																	■		■																																					
	- Move assets outside COI																	■		■																																					
	- Monitoring																	■		■																																					
	4. Updated IEE/EMP																	■		■																																					
	- PISCD Prepare																	■		■																																					
	- PMU Review																	■		■																																					
	- ADB Review and Approval																	■		■																																					
	- Public Consultation and Information Disclosure																	■		■																																					
	5. Bidding/Contract Award																	■		■																																					
	6. CEMP																	■		■																																					
	- Contractor Prepare																	■		■																																					
	- PISCD Review																	■		■																																					
	- PMU Approve																	■		■																																					
	- Conduct training to contractors' staff																	■		■																																					
	- Monitoring																	■		■																																					
	7. Construction of civil works																	■		■																																					
	8. Procurement of Equipment																	■		■																																					
	9. Construction Supervision																	■		■																																					
	10. DLP																	■		■																																					
	11. Hand Over																	■		■																																					
	12. O&M																	■		■																																					

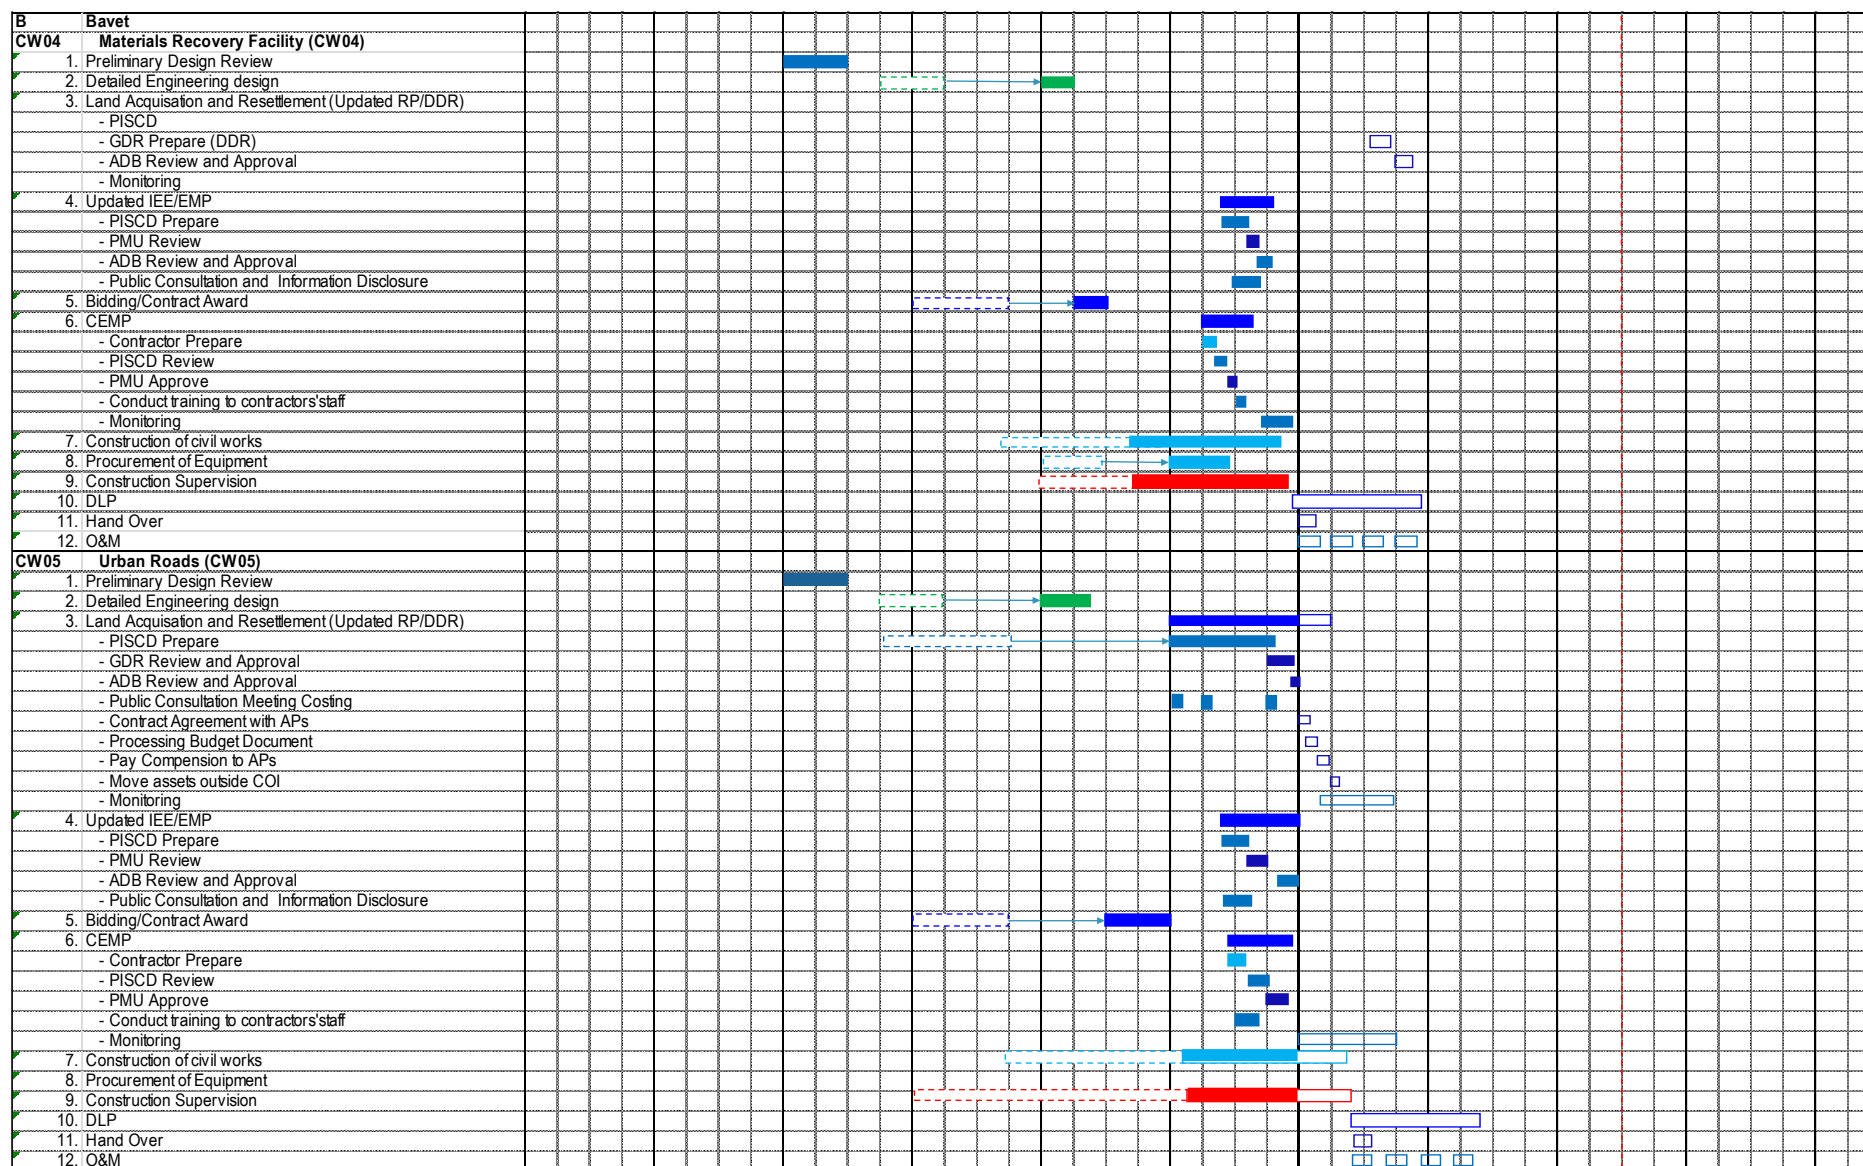

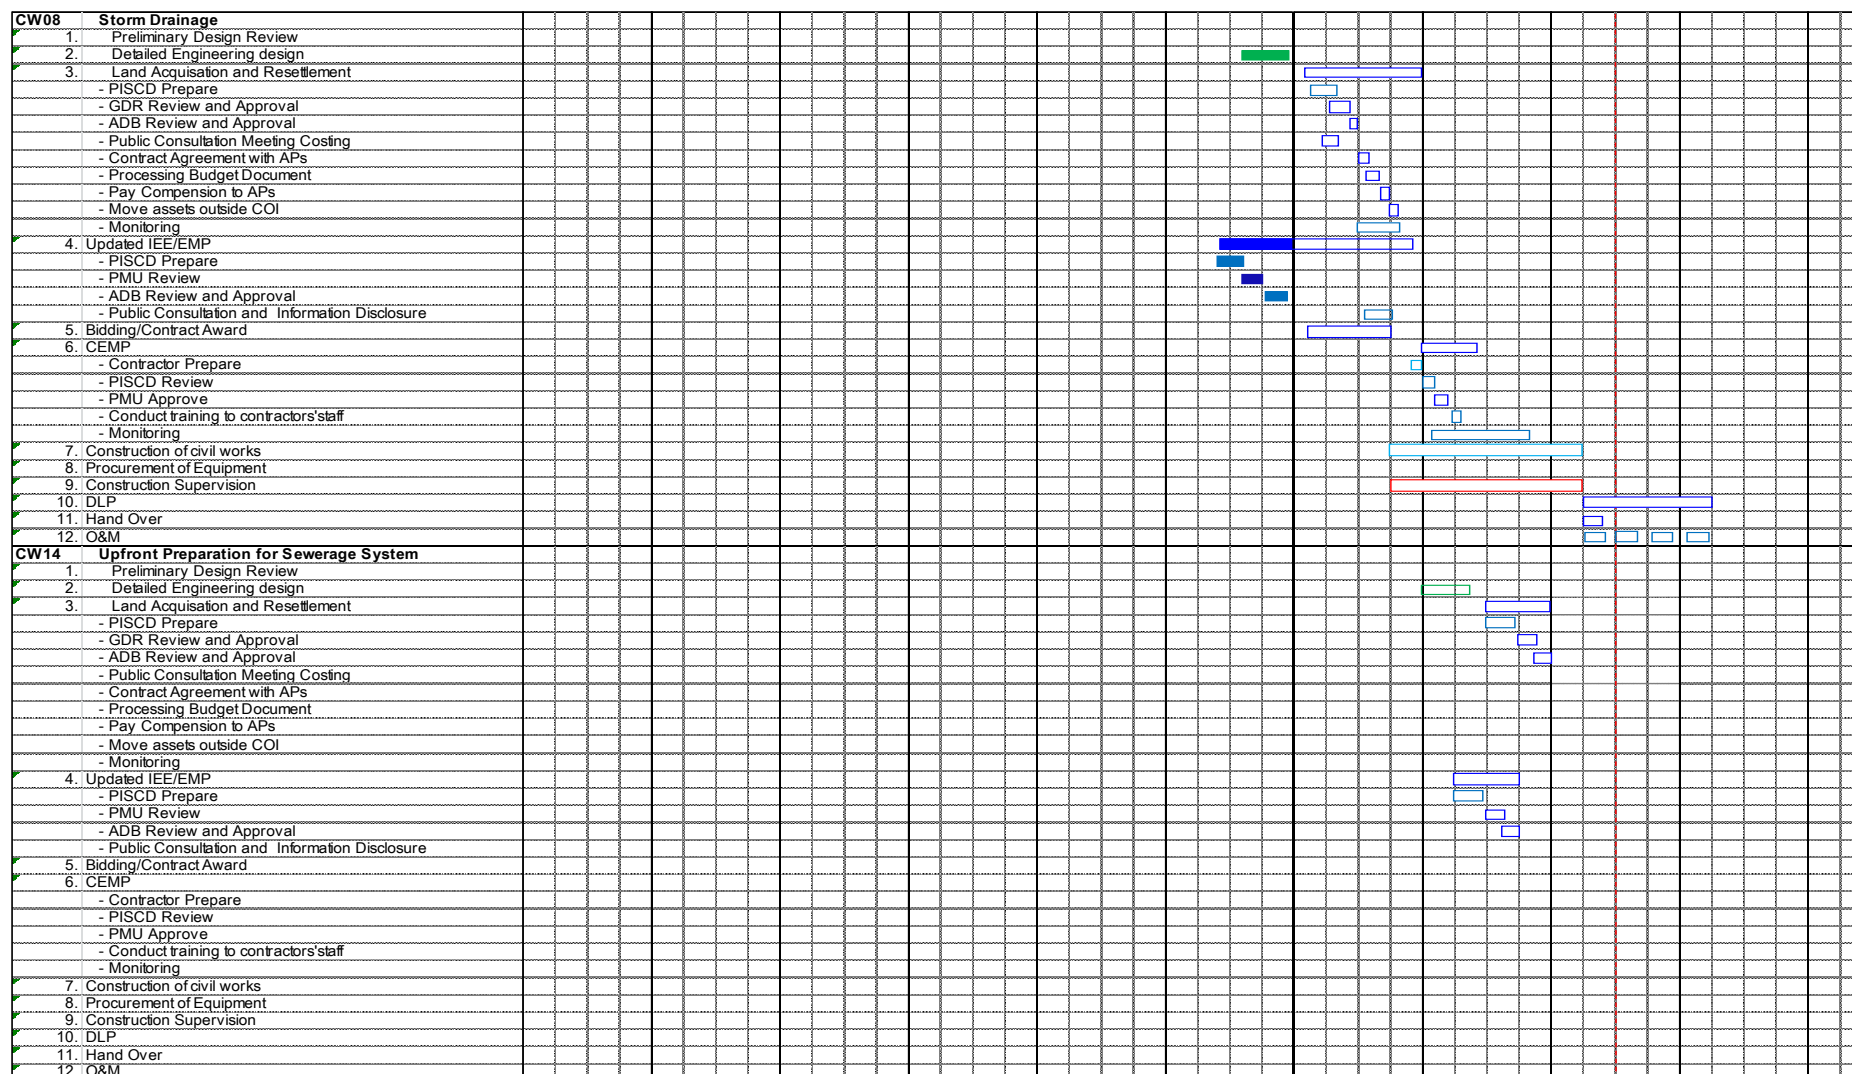

[illegible]

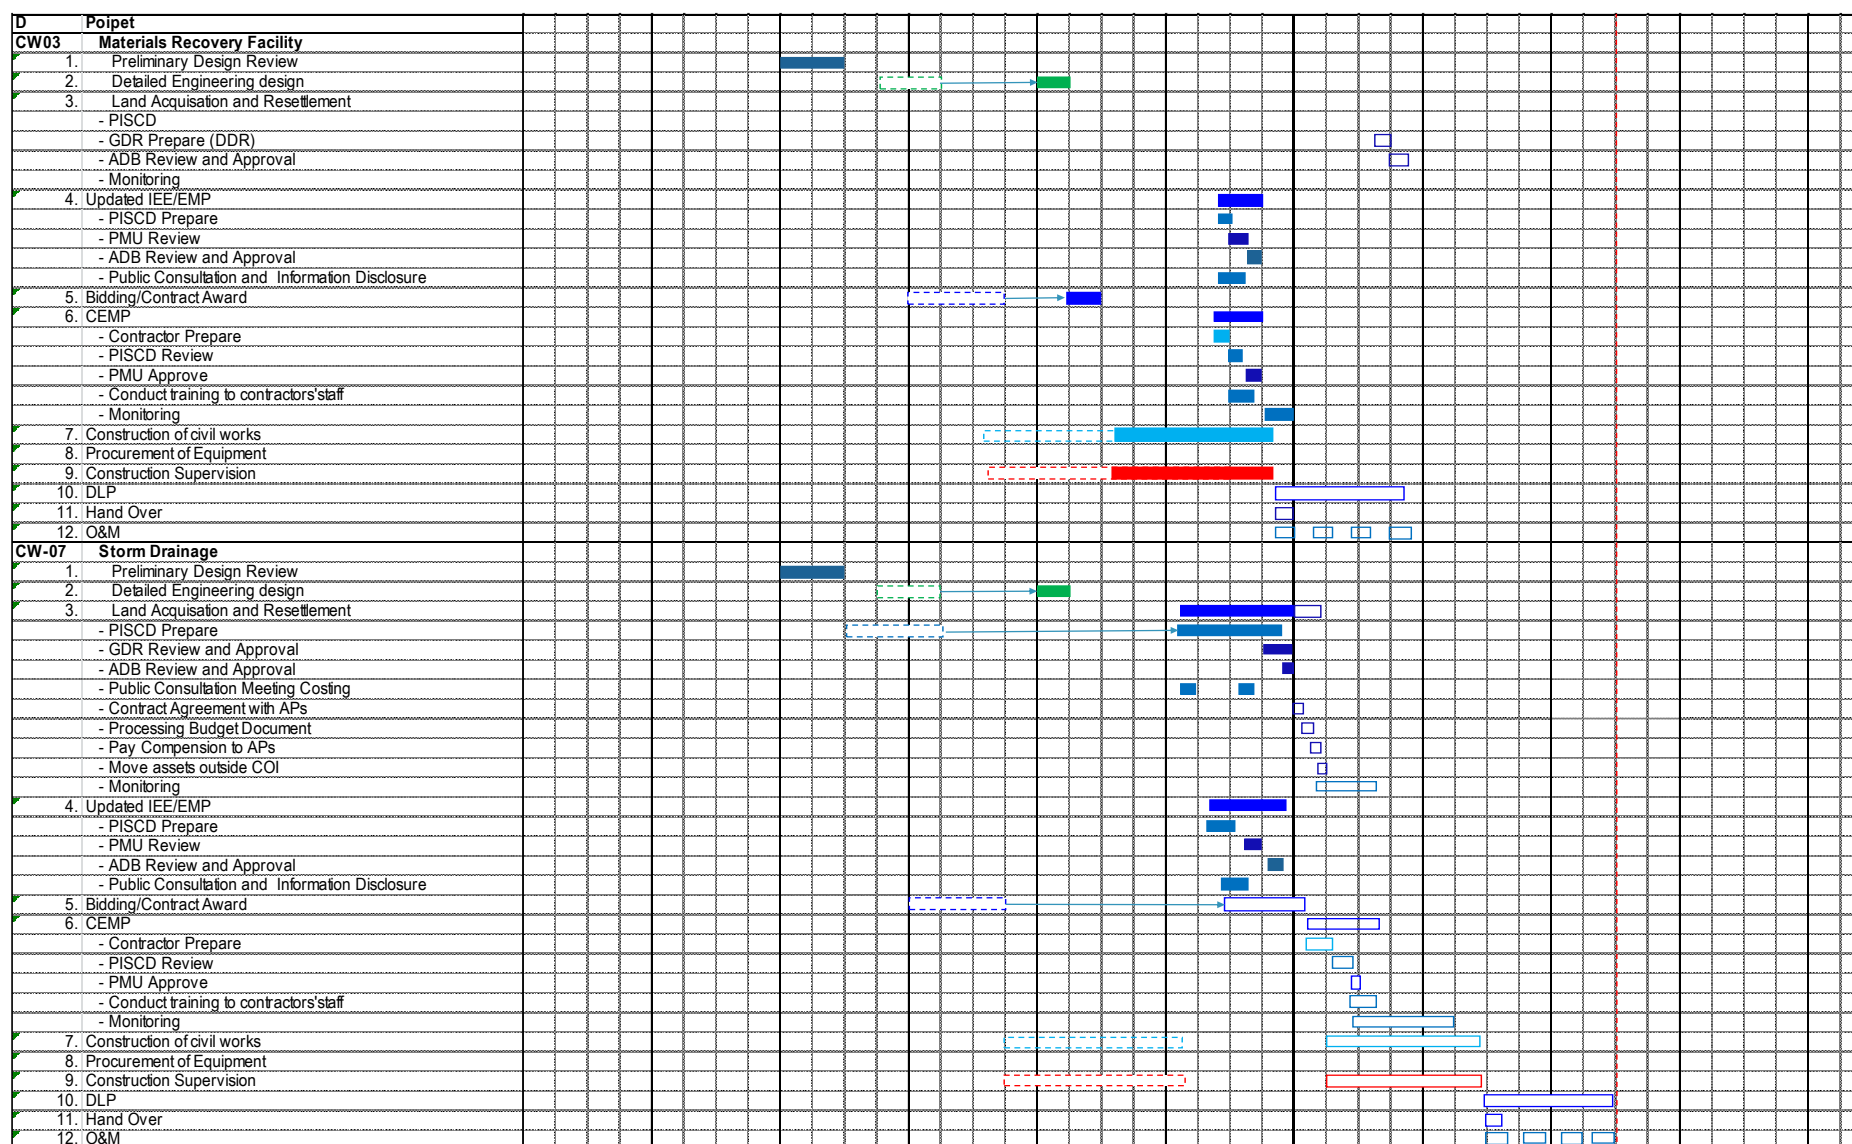



Legends:

Quarterly Report, 4th Quarter 2018



APPENDIX C LOANS AND GRANTS UTILIZATION

Status of Loan Utilization (Loan 2983)

As of 31 Dec 2018							
Cat. Ref.	Category Name	US Dollars					
		Allocation	Contracts Awarded	Uncontracted Loan Balance	Contracts Disbursed	Undisbursed Loan Balance	Undisbursed Contract Balance
		A	B	C = A - B	D	E = A - D	F = B - D
01	Works		-	-	-	-	-
1A	CW- Battambang WWT	16,000,007	5,846,220	10,153,786	1,907,492	14,092,514	3,938,728
1B	CW- Road and Solid Waste M	9,676,986	7,674,956	2,002,030	1,932,407	7,744,578	5,742,549
02A	CS - PISCD	1,842,013	2,071,805	(229,792)	1,799,500	42,513	272,305
02B	CS - DED	659,180	882,448	(223,268)	629,004	30,176	253,444
02C	CS - Construction Supervision	724,815	713,065	11,750	158,388	566,426	554,677
02D	CS - External Monitoring	112,377	-	112,377	-	112,377	-
03	Equipment	418,040	367,305	50,735	367,281	50,759	24
04	Training	135,134	-	135,134	-	135,134	-
05A	Incremental Admin - PMU	329,965	239,952	90,013	156,495	173,470	83,456
05B	Incremental Admin - PIUs	326,141	77,221	248,920	75,783	250,358	1,438
06	Unallocated	2,418,517	-	2,418,517	-	2,418,517	-
07	Interest During Construction	808,138	-	808,138	85,768	722,370	(85,768)
99	Imprest Account	709	-	709	238,605	(237,896)	(238,605)
	Total	33,452,021	17,872,972	15,579,049	7,350,723	26,101,297	10,522,249

Status of Loan Utilization (Loan 8265)

As of 31 Dec 2018							
Cat. Ref.	Category Name	US Dollars					
		Allocation	Contracts Awarded	Uncontracted Loan Balance	Contracts Disbursed	Undisbursed Loan Balance	Undisbursed Contract Balance
		A	B	C = A - B	D	E = A - D	F = B - D
01	Works						
1A	CW- Battambang WWT	3,780,000	1,433,448	2,346,552	467,702	3,312,298	965,746
2A	CS - PISCD	368,163	411,463	(43,300)	343,067	25,096	68,397
2B	CS - DED	100,430	137,598	(37,168)	98,079	2,351	39,519
2C	CS - Construction Sup.	270,435	270,435	-	52,366	218,069	218,069
03	Incremental Administration	1,291	20,000	(18,709)	1,290	1	18,710
04	Service Charge	13,000	-	13,000	1,192	11,808	(1,192)
05	Unallocated	466,681	-			466,681	-
	Imprest Account			-	34,150	(34,150)	(34,150)
	Total	5,000,000	2,272,945	2,260,374	997,847	4,002,154	1,275,098



Status of Grant Utilization (Grant 0334)

As of 31 Dec 2018							
Cat. Ref.	Category Name	US Dollars					
		Allocation	Contracts Awarded	Uncontracted Loan Balance	Contracts Disbursed	Undisbursed Loan Balance	Undisbursed Contract Balance
		A	B	C = A - B	D	E = A - D	F = B - D
01	Works						
01	Material Recovery Facility	1,500,000	1,500,000	-	1,350,000	150,000	150,000
	Total	1,500,000	1,500,000	-	1,350,000	150,000	150,000

Status of Grant Utilization (Grant 0335)

As of 31 Dec 2018							
Cat. Ref.	Category Name	US Dollars					
		Allocation	Contracts Awarded	Uncontracted Loan Balance	Contracts Disbursed	Undisbursed Loan Balance	Undisbursed Contract Balance
		A	B	C = A - B	D	E = A - D	F = B - D
01	Works						
1A	CW- Battambang WWT	3,270,000	2,089,274	1,180,726	681,684	2,588,316	1,407,590
02A	CS - PISCD	370,756	414,361	(43,605)	345,483	25,273	68,878
02B	CS - DED	85,490	117,129	(31,639)	83,489	2,001	33,640
02C	CS - Construction Sup.	245,850	245,850	-	47,605	198,245	198,245
03	Incremental Administration	1,391	30,000	(28,609)	1,391	0	28,609
04	Unallocated	426,513	-	426,513	-	426,513	-
			5,000				5,000
	Imprest Account		-	-	32,245	(32,245)	(32,245)
	Total	4,400,000	2,901,614	1,503,386	1,191,896	3,208,104	1,709,718



APPENDIX D

UPDATED PROCUREMENT PLAN

(Updated as of 30 November 2018)

Basic Data

Project Name: Greater Mekong Subregion Southern Economic Corridor Towns Development Project	
Project Number: 43319-033	Approval Number: 2983/8265/0334/0335
Country: Cambodia	Executing Agency: Ministry of Public Works and
Project Procurement Classification: Category A	
Project Procurement Risk: Low	
Project Financing Amount: US\$ 54,780,000 ADB Financing: US\$ 37,000,000 Cofinancing (ADB Administered): US\$ 10,900,000 Non-ADB Financing: US\$ 6,880,000	Project Closing Date: - Original: 30 June 2019 - Revised: 30 June 2021 - Revised (Mid-Term Review): 31 Dec 2022
Date of First Procurement Plan: 10 December 2012	Date of this Procurement Plan: 06 December 2018

A. Methods, Thresholds, Review and 18-Month Procurement Plan

1. Procurement and Consulting Methods and Thresholds

Except as the Asian Development Bank (ADB) may otherwise agree, the following process thresholds shall apply to procurement of goods and works.

Procurement of Goods and Works		
Method	Threshold	Comments
International Competitive Bidding for Goods	US\$ 1,000,000 and Above	
National Competitive Bidding for Goods	Beneath that stated for ICB, Goods	The first language version of National Competitive Bidding is subject to prior review, thereafter post review.
Shopping for Goods	Below US\$ 100,000	The first language version of shopping is subject to prior review, thereafter post review.
International Competitive Bidding for Works	US\$ 3,000,000 and Above	
National Competitive Bidding (NCB) for Works	Beneath that stated for ICB, Works	The first language version of National Competitive Bidding is subject to prior review, thereafter post review.
Shopping for Works	Below US\$ 100,000	The first language version of shopping is subject to prior review, thereafter post review.



Consulting Services	
Method	Comments
Consultant's Qualification Selection for Consulting Firm	Prior review
Quality- and Cost-Based Selection for Consulting Firm	Prior review
Individual Consultants Selection for Individual Consultant	Prior review

2. Goods and Works Contracts Estimated to Cost \$1 Million or More

The following table lists goods and works contracts for which the procurement activity is either ongoing or expected to commence within the next 18 months.

Package Number	General Description	Estimated Value (US\$)	Number of Contracts	Procurement Method	Review (Prior/ Post)	Bidding Procedure	Advertisement Date (quarter/year)	Comments
CW-07	Poipet Wastewater Treatment Subproject (Drainage)	2,600,000	1	NCB	Prior	1S1E	Q1 / 2018	Prequalification of Bidders: N Domestic Preference Applicable: N Bidding Document: Based on SOP/PM of Cambodia
CW-08	Bavet Wastewater Treatment Subproject (Drainage)	6,900,000	1	ICB	Prior	1S1E	Q2 / 2019	Prequalification of Bidders: N Domestic Preference Applicable: N Bidding Document: Small Works
CW-10	Neak Loeung Flood Control Subproject	8,800,000	1	ICB	Prior	1S1E	Q3 / 2019	Prequalification of Bidders: N Domestic Preference Applicable: N Bidding Document: Small Works

3. Consulting Services Contracts Estimated to Cost \$100,000 or More

The following table lists consulting services contracts for which the recruitment activity is either ongoing or expected to commence within the next 18 months.



Package Number	General Description	Estimated Value	Recruitment Method	Review (Prior/ Post)	Advertisement Date (quarter/year)	Type of Proposal	Comments

4. Goods and Works Contracts Estimated to Cost Less than \$1 Million and Consulting Services Contracts Less than \$100,000 (Smaller Value Contracts)

The following table lists smaller-value goods, works and consulting services contracts for which the activity is either ongoing or expected to commence within the next 18 months.

Goods and Works								
Package Number	General Description	Estimated Value	Number of Contracts	Procurement Method	Review (Prior/ Post)	Bidding Procedure	Advertisement Date (quarter/year)	Comments

Consulting Services							
Package Number	General Description	Estimated Value	Recruitment Method	Review (Prior/ Post)	Advertisement Date (quarter/year)	Type of Proposal	Comments

B. Indicative List of Packages Required Under the Project

The following table provides an indicative list of goods, works and consulting services contracts over the life of the project, other than those mentioned in previous sections (i.e., those expected beyond the current period).

Goods and Works							
Package Number	General Description	Estimated Value (cumulative)	Estimated Number of Contracts	Procurement Method	Review (Prior/Post)	Bidding Procedure	Comments
G-08	Equipment (Rubber wheel backhoe 2 units, Crane mounted truck: 2 units, Vacuum truck: 2 units, High pressure cleaner (jet cleaning machine for sewer/storm drain): 1 unit, Traffic sign: 16 units and Traffic corner: 40 units)	450,000	1	NCB	Prior	1S1E	Subject to the availability of funds
CW-09a	Poipet Wastewater Treatment Subproject (Sewerage)	4,800,000	1	ICB	Prior	1S1E	Subject to the availability of funds



Goods and Works							
Package Number	General Description	Estimated Value (cumulative)	Estimated Number of Contracts	Procurement Method	Review (Prior/Post)	Bidding Procedure	Comments
CW-09b	Poipet Solid Waste Management Sub-project	6,230,000	1	ICB	Prior	1S1E	Subject to the availability of funds
CW-11	Battambang Flood Control Subproject	2,090,000	1	NCB	Prior	1S1E	Subject to the availability of funds
CW-12	Poipet Wastewater Treatment Subproject (Mechanical Plant)	6,000,000	1	ICB	Prior	1S1E	Subject to the availability of funds

Consulting Services							
Package Number	General Description	Estimated Value (cumulative)	Estimated Number of Contracts	Recruitment Method	Review (Prior/Post)	Type of Proposal	Comments
NA							

C. List of Awarded and On-going, and Completed Contracts

The following tables list the awarded and on-going contracts and completed contracts.

1. Awarded and Ongoing Contracts

Goods and Works							
Package Number	General Description	Estimated Value (US\$)	Awarded Contract Value (US\$)	Procurement Method	Advertisement Date (quarter/year)	Date of ADB Approval of Contract Award	Comments
	Battambang Materials Recovery Facility Subproject	480,000	424,991.84	NCB	08-May-2017	07-Jul-17	Taing Cheng Oing Construction & Import Export Co., Ltd (VO1= US\$465,709.30)
	Bavet, Materials Recovery Facility Subproject	420,000	389,826.64	NCB	08-May-2017	07-Jul-17	Taing Cheng Oing Construction & Import Export Co., Ltd (VO1= US\$418,848.05)
	Poipet Materials Recovery Facility Subproject	490,000	359,571.12	NCB	08-May-2017	07-Jul-17	Taing Cheng Oing Construction & Import Export Co., Ltd (VO1= US\$615,442.65)
CW-06	Battambang Wastewater Treatment Subproject	12,000,000	9,368,943.03	ICB	Prior	03-Jan-18	Beijing Urban Construction Group Co., Ltd



Ministry of Public Works and Transport, Kingdom of Cambodia
GMS: Southern Economic Corridor Towns Development Project

Goods and Works							
Package Number	General Description	Estimated Value (US\$)	Awarded Contract Value (US\$)	Procurement Method	Advertisement Date (quarter/year)	Date of ADB Approval of Contract Award	Comments
CW-05	Bavet Urban Roads Subproject	9,900,000	7,674,956.00	ICB	Prior	13-Feb-18	MTA Construction Co., Ltd and Xinjiang Beixin Road and Bridge Group Co. Ltd (JV)

Services							
Package Number	General Description	Estimated Value	Awarded Contract Value	Recruitment Method	Advertisement Date (quarter/year)	Date of ADB Approval of Contract Award	Comments
CS-01	Project Implementation Support and Capacity Development	2,480,000	2,222,490.00	QCBS	Q1 / 2013	31-JUL-14	NJS Consultants Co., Ltd. VO7 =US\$2,59,2690 VO8 =US\$2,897,629.50
CS-03	Construction Supervision Consultants	1,750,000	1,229,250.00	QCBS	Q3/2015	05 Jan 17	Contract with RDC (lot1= US\$ 825,950, & Lot2= US\$297,300)
CS-06	National Environmental Specialist	60,000	40,934.00	ICS	Q1 / 2016	18 Aug 16	Contract with Mr. Bun San
CS-05	National Procurement Specialist	72,000	27,508.00	ICS	Q1 / 2016	9 June 16	Contract with Mr. Pheang Pheourn
CS-04	Financial Management Specialist	72,000	32,660.00	ICS	Q1 / 2016	9 June 16	Contract with Mr. Mao Dor

2. Completed Contracts

Package Number	General Description	Estimated Value	Awarded Contract Value	Procurement Method	Advertisement Date (quarter/year)	Date of ADB Approval of Contract Award	Date of Completion	Comments
G-01	Procurement of Vehicles	200,000	166,800.00	NCB	08-Apr-2015	06 Jul 2015	29-Jan-16	RMA (Cambodia) Co., Ltd
G-02	Procurement of Office Equipment	90,000	94,460.00	Shopping	26-Mar-2015	N/A	30-Nov-15	NEEKA Limited
G-03	Procurement of Office Furniture	35,000	24,945.00	Shopping without advertising	N/A	11-Nov-2015	18-Apr-16	LC Office Furniture Shop



Ministry of Public Works and Transport, Kingdom of Cambodia
GMS: Southern Economic Corridor Towns Development Project

Package Number	General Description	Estimated Value	Awarded Contract Value	Procurement Method	Advertisement Date (quarter/year)	Date of ADB Approval of Contract Award	Date of Completion	Comments
G-04	Bavet Transformer 3 phase-100kva	5,000	11,626.00	Shopping without advertising	NA	NA	31-Aug-15	KROI KOR Electricity Supply
G-05	UAV (Drone)	45,000	78,045.00	Shopping	26- Mar -15	NA	30-Jun-16	ENVOSTAR Co., Ltd.
CW-01/1	PMU Office Renovation	15,000	15,091.31	Shopping without advertising	NA	8-Jan-15	25-Jan-16	TAING CHENG ONG CONSTRUCTION CO. LTD.
CW-01/2	Battambang Office Renovation	9,000	9,344.80	Shopping without advertising	NA	NA	24-Mar-16	Vong Reaksmeay
CW-01/3	Poipet Office Renovation	7,000	7,049.00	Shopping without advertising	NA	NA	25-May-16	T.M.3 Consulting Co., Ltd.
CW-01/4	Neak Loeung Office Renovation	9,000	9,990.00	Shopping without advertising	NA	NA	21-Apr-16	Y.S.B.
CW-01/5	Bavet Office Renovation	5,000	5,760.00	Shopping without advertising	NA	NA	12-Jul-16	Chhun Nary Import Export Co., Ltd. Construction Co. Ltd.
G-06	Accounting Software	3,000	2,595.00	Shopping without advertising	NA	NA	26-Sep-16	BIZDIMNSION CO., LTD
G-07	Supply & Installation of Parts for Ford Ranger Plate No. State 25 2-0607	6,000	6151.33	Shopping without advertising	NA	NA	21-Feb-17	RMA (Cambodia) Co., Ltd.
CS-02	DED consultants for all 10 subprojects	1,151,000	1,137,175.00	QCBS	Q3 / 2014	19-OCT-15	19Jun-17	FCG International Ltd.

D. National Competitive Bidding

A. Regulation and Reference Documents

- The procedures to be followed for national competitive bidding shall be those set forth for the "National Competitive Bidding" method in the Government's Procurement Manual issued under Sub-Decree Number 74 ANKR.BK, updated version dated 22 May 2012 with the clarifications and modifications described in the following paragraphs. These clarifications and modifications are required for compliance with the provisions of the Procurement Guidelines.



2. For the procurement of ADB financed contracts under National Competitive Bidding (NCB) procedures, the use of harmonized national bidding documents (NCB and National Shopping) developed in consultation with development partners including ADB, is mandatory except where the Government and ADB have agreed to amendments to any part of the documents. The Procurement Manual also advises users to check the ADB website from time to time for any update on ADB documents, which form the basis, among others, of the existing harmonized national bidding documents.

B. Procurement Procedures

1. Application

3. Contract packages subject to National Competitive Bidding procedures will be those identified as such in the project Procurement Plan. Any change to the mode of procurement of any procurement package in the Procurement Plan shall be made through updating of the Procurement Plan, and only with prior approval of ADB.

2. Sanctioning

4. Bidders shall not be declared ineligible or prohibited from bidding on the basis of barring procedures or sanction lists, except individuals and firms sanctioned by ADB, without prior approval of ADB.

3. Rejection of all Bids and Rebidding

5. The Borrower shall not reject all bids and solicit new bids without ADB's prior concurrence. Even when only one or a few bids is/are submitted, the bidding process may still be considered valid if the bid was satisfactorily advertised and prices are reasonable in comparison to market values.

4. Advertising

6. Bidding of NCB contracts shall be advertised on the ADB website via the posting of the Procurement Plan. Borrowers have the option of requesting ADB to post specific notices in the ADB website.

C. Bidding Documents

5. Use of Bidding Documents

7. The Standard National Competitive Bidding Documents provided with the Government's Procurement Manual shall be used to the extent possible both for the master bidding documents and the contract-specific bidding documents. The English language version of the procurement documents shall be submitted for ADB review and approval in accordance with agreed review procedures (post and prior review) as indicated in the Procurement Plan. The ADB-approved procurement documents will then be used as a model for all procurement financed by ADB for the project.

6. Bid Evaluation

8. Bidders shall not be eliminated from detailed evaluation on the basis of minor, non-substantial deviations.
9. A bidder shall not be required, as a condition for award of contract, to undertake obligations not specified in the bidding documents or otherwise to modify the bid as originally submitted.

7. Employer's Right to Accept or Reject Any or All Bids

10. The decision of the Employer to accept or reject any or all bids shall be made in a transparent manner and involve an obligation to inform of the grounds for the decision through the bid evaluation report.

8. ADB Policy Clauses



11. A provision shall be included in all NCB works and goods contracts financed by ADB requiring suppliers and contractors to permit ADB to inspect their accounts and records and other documents relating to the bid submission and the performance of the contract, and to have them audited by auditors appointed by ADB.
12. A provision shall be included in all bidding documents for NCB works and goods contracts financed by ADB stating that the Borrower shall reject a proposal for award if it determines that the bidder recommended for award has, directly or through an agent, engaged in corrupt, fraudulent, collusive, or coercive practices in competing for the contract in question.
13. A provision shall be included in all bidding documents for NCB works and goods contracts financed by ADB stating that ADB will declare a firm or individual ineligible, either indefinitely or for a stated period, to be awarded a contract financed by ADB, if it at any time determines that the firm or individual has, directly or through an agent, engaged in corrupt, fraudulent, collusive, coercive or obstructive practices or any integrity violation in competing for, or in executing, ADB-financed contract.



APPENDIX E

LIST OF CAPACITY DEVELOPMENT AND TRAINING CONDUCTED

Module	Title	Date	Venue	Agency	Participants		
					Female	Male	Total
				PMU	1	0	1
				PIU BB	2	1	3
				PIU PP	0	2	2
				PIU NL	0	2	2
				PIU BV	0	2	4
				Total	3	7	10
				PMU	0	0	0
				PIU BB	0	3	3
				PIU PP	0	3	3
				PIU NL	0	3	3
				PIU BV	0	2	2
				Total	0	11	11
				PMU	1	2	3
				PIU BB	2	2	4
				PIU PP	1	3	4
				PIU NL	1	3	4
				PIU BV	-	4	4
				Total	5	14	19
				PMU	1	2	3



Module	Title	Date	Venue	Agency	Participants		
					Female	Male	Total
	Approaches for Safeguards	2017	Poipet Municipality, Banteay Meanchey Province	PIU BB	2	2	4
				PIU PP	1	3	4
				PIU NL	1	3	4
				PIU BV	-	4	4
				Total	5	14	19
				PMU	-	2	2
				PIU BB	2	3	5
				PIU PP	2	2	4
				PIU NL	1	4	5
				PIU BV	-	4	4
				Total	5	15	20
				PMU	-	2	2
				PIU BB	2	3	5
				PIU PP	2	2	4
				PIU NL	1	4	5
				PIU BV	-	4	4
				Total	5	15	20
				PMU	-	-	-
				PIU BB	1	2	3
				PIU PP	-	2	2
				PIU NL	-	2	2
				PIU BV	-	2	2



Module	Title	Date	Venue	Agency	Participants		
					Female	Male	Total
				Total	1	8	9
				PMU	1	2	3
				PIU BB	1	2	3
				PIU PP	-	2	2
				PIU NL	-	2	2
				PIU BV	-	2	2
				Total	2	10	12
				PMU	1	4	5
				PIU BB	2	2	4
				PIU PP	1	3	4
				PIU NL	1	3	4
				PIU BV	-	2	2
				Total	5	14	19
				PMU	-	3	3
				PIU BB	1	1	2
				PIU PP	1	1	2
				PIU NL	-	2	2
				PIU BV	-	2	2
				Total	2	9	11
				PMU	-	1	1
				PIU BB	2	2	4
				PIU PP	-	3	3



Ministry of Public Works and Transport, Kingdom of Cambodia
GMS: Southern Economic Corridor Towns Development Project

Module	Title	Date	Venue	Agency	Participants		
					Female	Male	Total
				PIU NL	-	5	5
				PIU BV	-	4	4
				Total	2	15	17
				PMU	-	3	3
				PIU BB	2	2	4
				PIU PP	-	4	4
				PIU NL	-	6	6
				PIU BV	-	5	5
				Total	2	20	22
				PMU	1	1	2
				PIU BB	2	-	2
				PIU PP	1	3	4
				PIU NL	1	3	4
				PIU BV	-	3	3
				Total	5	10	15
				PMU	1	4	5
				PIU BB	2	2	4
				PIU PP	1	3	4
				PIU BV	-	4	4
				GMAG	1	-	1
				MoWA	1	-	1
				PDWA	3	-	3



Ministry of Public Works and Transport, Kingdom of Cambodia
GMS: Southern Economic Corridor Towns Development Project

Module	Title	Date	Venue	Agency	Participants		
					Female	Male	Total
				PHD	2	-	2
				Contractor	-	3	3
				Total	11	16	27
				PMU	-	2	2
				PIU BB	-	1	1
				PIU PP	-	1	1
				PIU NL	-	1	1
				PIU BV	-	1	1
				Total	0	6	6
				PMU	-	2	2
				PIU BB	2	2	4
				PIU PP	1	3	4
				PIU NL	1	3	4
				PIU BV	-	4	4
				Total	4	14	18
				PMU	1	1	2
				PIU BB	1	2	3
				PIU PP	-	3	3
				PIU NL	-	2	2
				PIU BV	-	2	2
				Total	2	10	12
				PMU	-	3	3



Module	Title	Date	Venue	Agency	Participants		
					Female	Male	Total
	Management and Sanitary Landfill			PIU BB	1	2	3
				PIU PP	-	3	3
				PIU NL	-	2	2
				PIU BV	-	2	2
				Total	1	12	13
				PMU	1	3	4
				PIU BB	2	5	7
				PIU PP	1	8	9
				PIU NL	-	4	4
				PIU BV	-	5	5
				Total	4	25	29
				PMU	1	3	4
				PIU BB	2	5	7
				PIU PP	1	8	9
				PIU NL	-	4	4
				PIU BV	-	5	5
				Total	4	25	29
				PMU	1	3	4
				PIU BB	2	5	7
				PIU PP	1	8	9
				PIU NL	-	4	4
				PIU BV	-	5	5



Module	Title	Date	Venue	Agency	Participants		
					Female	Male	Total
				Total	4	25	29
				PMU	1	3	4
				PIU BB	0	3	3
				PIU PP	0	3	3
				PIU NL	0	3	3
				PIU BV	0	3	3
				Total	1	15	16
				PMU	1	3	4
				PIU BB	-	3	3
				PIU PP	-	3	3
				PIU NL	-	3	3
				PIU BV	-	3	3
				Total	1	15	16
				PMU	-	2	2
				PIU BB	1	1	2
				PIU PP	-	2	2
				PIU NL	-	2	2
				PIU BV	-	2	2
				Total	1	9	10
				PMU	-	3	3
				PIU BB	3	3	6
				PIU PP	-	6	6



Module	Title	Date	Venue	Agency	Participants		
					Female	Male	Total
				PIU NL	-	5	5
				PIU BV	-	5	5
				Total	3	22	25
24 Modules				Grand Total	78	356	434



APPENDIX F ASSESSMENT OF ASSUMPTIONS AND RISKS

MONITORING AND EVALUATION OF ASSUMPTION AND RISKS
GMS: Southern Economic Towns Development Project

M&E Form no. 7A
Version: June 2015

Reporting Date: 31 December 2018 Prepared by: PMU/PIUs assisted by Nat'l. M&E Specialist
[Quarterly] [PMU/PIUs]

Assumption / Risk for Outputs		Rating (HS,S,PS,U)	Assessment of Current Status
Assumptions:			
1.	Local authorities endorse the SLEDPs and associated budgets	S	Adopted SLEDPs by Battambang adopted on March 2017 Bavet adopted on February 2017 Poipet adopted on June 2018 Neak Loeung on March 2018
2.	Women's participation in SLEDP preparation increased, women's needs identified through participatory processes and reflected in the SLEDPs	S	SLEDPs were adopted by 2017 and 2018 when women's participation will be encouraged.
3.	Environmental and social risks can be mitigated	S	EMPs and RPs and was addressed in DED & adequately considered in the bid documents.
4.	Priority infrastructure will promote gender equality and/or women's empowerment by improving women's access to, and use of opportunities, services, resources, and assets; and contribute to increased participation in decision making	S	GAP will be addressed in the DED and adequately considered in the bid documents.
5.	Capacity development activities take gender balance into account	PS	20% of women participated in CD activities
6.	Specific training on gender aspects & issues provided to all staff of executing & implementing agencies & project implementing units	S	Specific training on Gender Action Plan & Gender sensitization and awareness provided to all staff, 44 staffs of PMU&PIUs attended in training, 9 out of them are women.
Risks:			
1.	Local authorities do not recognize the need for continued capacity development	Y	Satisfactory attendance in training



Risks:	Mitigated (Y/N)	Rating (HS,S,PS,U)	Assessment of Current Status
2. Required budgets for sustaining operations are not allocated	-	-	Not due yet as subprojects are in construction and DED phase.
3. Delayed or incomplete settlement of land acquisition and resettlement entitlements	Y	S	Resettlement activities to start in Q1 2017 and ongoing.
4. Lack of municipal quality control and performance evaluation	Y	HS	Construction works to start Q3 2017. CS started activities on Q1 2018

a/ HS = Highly Satisfactory; S = Satisfactory; PS = Progressing Satisfactorily; U = Unsatisfactory

MONITORING AND EVALUATION OF ASSUMPTION AND RISKS
GMS: Southern Economic Towns Development Project

M&E Form no. 7B
June 2015

Reporting Date: 31 December 2018 Prepared by: PMU/PIUs assisted by Nat'l. M&E Specialist
[Quarterly] [PMU/PIUs]

Assumption / Risk for Outcome and Impact		Rating (HS,S,PS,U)	Assessment of Current Status
Outcome: Urban infrastructure improved and climate resilience enhanced in Battambang, Bavet, Neak Loeung, and Poipet - from 2018 to 2020			
Assumptions:			
The government remains committed to sustainable management of urban infrastructure as a national development priority		HS	There is strong support from National and provincial governments.
Risks:	Mitigated (Y/N)	Rating (HS,S,PS,U)	Assessment of Current Status
Government regulations do not fully support sustainable decentralized operation and maintenance of urban infrastructure	-	-	O&M of infrastructure to start by Q2 2019.
Impact: The towns of Battambang, Bavet, Neak Loeung & Poipet will become centers of economic activity in the Southern Economic Corridor - by 2025			
Assumptions:		Rating (HS,S,PS,U)	Assessment of Current Status
Government remains fully committed to the Project			
Risks:	Mitigated (Y/N)	Rating (HS,S,PS,U)	Assessment of Current Status
Corridor towns unable to collect revenue for wastewater treatment plants, sanitary landfill, and solid waste management	-	-	The implementation of these subprojects is deferred and change to new project start in 2020.

a/ HS = Highly Satisfactory; S = Satisfactory; PS = Progressing Satisfactorily; U = Unsatisfactory



APPENDIX G DMF TARGETS VS ACHIEVEMENTS

PROJECT PERFORMANCE MONITORING AND EVALUATION
GMS: Southern Economic Towns Development Project

M&E Form no. 8A
June 2015

Reporting Date: 31 December 2018 [Quarterly]

Prepared by: PMU/PIUs assisted by Nat'l. M&E Specialist
[PMU/PIU member in-charge of M&E/Impact Assessment]

Indicators (with Baseline and Performance Targets)	Baseline	Achievements/Status (as of end of reporting period)	Assessment of Current Progress/ Status & Reason for any Negative Variance
Output 1: SLEDPs adopted and implemented in Battambang, Bavet, Neak Loeung, and Poipet - by 2018			
1.1 SLEDPs with sex-specific and climate-resilience measures incorporated, adopted, & disclosed; updated as required. [Validation with PIUs and corridor towns in Q2 2015 for adoption and Q4 2018 for updating] [Updates on September 2018 from FDP and from gender specialist]	SLEDP of each town prepared in 2011	SLEDPs Adopted by Battambang adopted on March 2017 Bavet adopted on February 2017 Poipet adopted on June 2018 Neak Loeung on March 2018 SLEDPs of the 4 towns include sections on gender issues and measures to address these. Gender issues cited in the SLEDPs: Women are discriminated in the labor sector where	



Indicators (with Baseline and Performance Targets)	Baseline	Achievements/Status (as of end of reporting period)	Assessment of Current Progress/ Status & Reason for any Negative Variance
		they have lower wages than men; exposed to poor working conditions; Women particularly the female heads of households are not economically empowered and are not involved in decision-making in the community; because of low education; and much time spent in housework performing both tasks of men and women Women, especially young girls are at risk to human trafficking and the core labor issues; Women do not occupy leadership positions in the community	
1.2 Gender awareness and sensitization training conducted for 30 executing and implementing agency staff. [Updates from Training Implementation Consultant (TIC) upon completion of training in Q3 2016] [Updates from Training on Gender Action Planning on 4-5 January 2017 and Refresher course on GAP on 8-9 August 2018.]	Nil as of 2014	As per the attached training completion report, this training activity was already conducted by the PISCD last September, 2016. Total participants were 36 out of which 31 (86%) men and 5 (14%) women.	



Indicators (with Baseline and Performance Targets)	Baseline	Achievements/Status (as of end of reporting period)	Assessment of Current Progress/ Status & Reason for any Negative Variance
		A training on Gender Action Planning conducted on 4-5 January, 2017. Total number of participants was 14, 9 men (65%) and 5 (35%) women. Refresher course on GAP was conducted on 8-9 August 2018. A total 27 (11 female) participants attended the refresher course.	
Output 2: Priority urban infrastructure investments implemented - Priority infrastructure operational - by 2020			
30% of construction workers hired under the project are female [Updates from CS Consultant from Q3 2017 to Q4 2020]	Nil, as construction starts Q3 2017	Total of 37 construction workers in the MRFs in 3 towns, 10 are women (27%) and 27 (72%) are men. Total unskilled construction workers in the storm drainage sub-component of the waste water treatment subproject of Battambang and urban road subproject of Poipet is 144; 49 (34%) are women.	PIU to regularly monitor manpower status with civil works contractors. PMU and PIU to compel civil works contractors to hire more women unskilled laborers.
Battambang			
Wastewater treatment (PPCR)			
2.1 52,000 residents serviced by new and rehabilitated	31,000 residents currently	-	Assessment to start upon



Indicators (with Baseline and Performance Targets)		Baseline	Achievements/Status (as of end of reporting period)	Assessment of Current Progress/ Status & Reason for any Negative Variance
wastewater treatment plants (capacity 2,800 cu m/day) by 2020. Flood events of facility reduced (based on 50-year flood frequency). <i>[Updates from CS Consultant upon completion of infrastructure in Q4 2020, and from infrastructure operator during operation from Q1 2021 onward]</i>		connected to existing sewerage system		completion of construction of storm water drainage canal and upgrade of existing WWTP western part is deferred.
Flood control (PPCR)				
2.2	Flood events of city center, near river, reduced (based on 50-year flood frequency), benefiting 15,120 persons by 2018.	"Before-project" number of persons affected by floods is ____ ^{a/}	-	The implementation of this flood control subproject is deferred.
Material recovery facility				
2.3	30 cu m of recyclables per day segregated benefiting 128,000 residents by 2018. <i>[Updates from CS Consultant upon completion of infrastructure in Q1 2019, and from infrastructure operator during operation from Q2 2019 onward]</i>	Nil, as the MRF is a new facility	-	Assessment to start upon completion of construction of MRF in Q1 2019 onwards.
Bavet				
Wastewater treatment (PPCR)				
2.4	29,000 residents serviced by wastewater treatment plant (capacity 255 cu m/day) by 2019. Flood events of facility reduced (based on 50-year flood frequency).	Nil as Bavet has no existing WWT	-	The implementation of this WWT subproject is deferred.
Urban roads				
2.5	6,14 km of main urban road upgraded with drainage structures, benefiting 37,100 residents by 2019. <i>[Updates based on local authorities' statistical data, and on-site verification, from Q2 2020 onward]</i>	"Before-project" number of persons that has access to existing road to be upgraded is ____ ^{a/}	-	Assessment to start upon completion of urban road upgrading in Q2 2020 onwards.



Indicators (with Baseline and Performance Targets)		Baseline	Achievements/Status (as of end of reporting period)	Assessment of Current Progress/ Status & Reason for any Negative Variance
Material recovery facility				
2.6	30 cu m of recyclables per day segregated, benefiting 24,000 residents by 2018. <i>[Updates from CS Consultant upon completion of infrastructure in Q1 2019, and from infrastructure operator during operation from Q2 2019 onward]</i>	Nil as the MRF is a new facility	-	Assessment to start upon completion of construction of MRF in Q1 2019 onwards.
Neak Loeung				
Flood protection (PPCR)				
2.7	5.4 km flood protection dike constructed; 363 ha of residential and commercial areas protected from annual flooding (based on 50-year flood frequency), benefiting 24,700 residents by 2019.	“Before-project” number of persons residing within the subproject area is ____ ^{a/} .	-	The implementation of this flood protection subproject is under study.
Poipet				
Wastewater treatment (PPCR)				
2.8	65,000 residents serviced by wastewater treatment plant (capacity 16,400 cu m/day) by 2019. Flood events of facility reduced (based on 50-year flood frequency). <i>[Updates from CS Consultant upon completion of infrastructure in Q3 2020, and from infrastructure operator during operation from Q4 2020 onward]</i>	Nil as Poipet has no existing WWTP	-	Assessment to start upon completion of construction of WWTP in Q3 2020 onwards.
Solid waste management				
2.9	20 tons/day of solid waste deposited in sanitary landfill, benefiting 58,600 residents by 2019	Nil since the sanitary landfill is a new facility	-	The implementation of this subprojects is deferred.
Material recovery facility				
2.10	30 cu m of recyclables per day segregated, benefiting 58,600 residents by 2018. <i>[Updates from CS Consultant upon completion of infrastructure in Q1</i>	Nil as the MRF is a new facility	-	Assessment to start upon completion of construction of MRF in Q1 2019



Indicators (with Baseline and Performance Targets)	Baseline	Achievements/Status (as of end of reporting period)	Assessment of Current Progress/ Status & Reason for any Negative Variance
2019, and from infrastructure operator during operation from Q2 2019 onward]			onwards.
Output 3: Institutional capacity strengthened - by 2020			
3.1 2,000 people trained in project management and implementation, financial management, procurement, and social and environment safeguards; [Updates from TIC [TBD] 4/ from Q3 2015 to Q2 2020] Gender targets achieved: staff quota of 30% women in the PMU and PIU with increased role in decision making. • Updates from PMU/PIUs from Q3 2015 onward] • [Updates from Gender Specialist during discussed refresher course on August 2018]	Nil as of 2014 as training starts Q3 2016 Nil	434 PMU and PIUs staffs trained, of which 78 (18%) are woman Total PMU staffs are 10; 8 (80%) men and 2 women (20%) women. Even, this issue was already discussed during the Refresher Course on GAP in August 2018; PMU so far couldn't solve the issue on gender balance in the PMU and PIUs.	As of 30 Sep. 2018, 25 training modules conducted for PMU and PIUs. Gender action target may not be realized because the PMU has already existing staffs already in place even before start of project implementation. This issue will be addressed during the MTR; with support document to justify its re-targeting
Gender targets achieved: staff quota of 20% women in the PMU and PIU with increased role in decision making. [Updates from Mid-Term Review Mission 2-30 Nov 2018]	Nil	- 2 staffs (or 20%) of 10 PMU staffs are women - 7 staffs (22%) of 31 PIUs staffs are women. - All PMUs and PIUs staffs received gender sensitization training.	
3.2 Memorandum of agreement signed between implementing agencies and district and corridor town authorities on subproject O&M and climate resilience measures [Validation with PIUs and district and corridor towns, Q3 2017 onward]	As of 2015, no MOA signed as construction starts Q3 2017		Assessment to start upon completion of construction onwards.
3.3 Women hold 30% of overall staff positions and 30% of the management positions in the PMU and PIU.	Nil	As of Q3 2018, women hold 20% of overall staff positions in PMU & 20%	



Indicators (with Baseline and Performance Targets)	Baseline	Achievements/Status (as of end of reporting period)	Assessment of Current Progress/ Status & Reason for any Negative Variance
<i>[Updates from PMU/PIUs from Q3 2015 onward]</i>		PIUs	
Women hold 20% of overall staff positions and 20% of the management positions in the PMU and PIU. <i>[Updates from Mid-Term Review Mission 2-30 Nov 2018]</i>	Nil	- 2 staffs (or 20%) of 10 PMU staffs are women - 7 staffs (22%) of 31 PIUs staffs are women.	

a/ To be determined/updated during the preliminary design review to be undertaken by the DED Consultant.

PROJECT PERFORMANCE MONITORING AND EVALUATION
GMS: Southern Economic Towns Development Project

M&E Form no. 8B
June 2015

Reporting Date: _____ 31 December 2018 _____ *[Quarterly]*

Prepared by: _____ PMU/PIUs assisted by Nat'l. M&E Specialist
[PMU/PIU member in-charge of M&E/Impact Assessment]

Indicators (with Baseline and Performance Targets)	Baseline	Achievements/Status (during reporting period)	Assessment of Current Progress/ Status & Reason for any Negative Variance
Outcome: Urban infrastructure improved and climate resilience enhanced in Battambang, Bavet, Neak Loeung, and Poipet - from 2018 to 2020			
1. Improved access to urban infrastructure affects 558,220 inhabitants (cumulative figure) in four project towns.	In 2015, _____ a/ persons have access to existing infrastructure	-	Assessment to start upon completion of construction of infrastructure in four project town, onwards.
2. Annual economic impact of poor sanitation, accounting for a loss of \$33 in 2005 per capita per year, reduced by 40%.	Value of loss due to poor sanitation was \$32 in 2005	-	Assessment to start upon completion of construction of WWT subprojects, onwards.
3. Urban areas affected by perennial flooding reduced by 30%.	"Before- Project" total urban area affected by perennial flooding in Battambang and Neak	-	Assessment to start upon completion of construction of flood control/protection subprojects, onwards.



Indicators (with Baseline and Performance Targets)	Baseline	Achievements/Status (during reporting period)	Assessment of Current Progress/ Status & Reason for any Negative Variance
	Loeung is ____ ^{a/} ha.		
Impact: The towns of Battambang, Bavet, Neak Loeung & Poipet will become centers of economic activity in the Southern Economic Corridor - by 2025			
1. In project towns (represented by provincial data): (i) trade services increased from 8.4% of GDP in 2007 to 18.4%; (ii) transport and communication services increased from 6.9% of GDP in 2007 to 16.9%; (iii) hotels & restaurant services increased from 4.3% of GDP in 2007 to 14.3%	Growth rates of subsectors in 2012 7.2% 7.6% 16.2%	-	Evaluation will be carried out by 2025 The implementation of this subprojects is deferred. The implementation of this subprojects is deferred. The implementation of this subprojects is deferred.
2. Employment opportunities for women (This refers to female employment in economic growth opportunities generated by the project, including construction, market trading, solid waste management, and recycling.) increased from 52% in 2012 to 53.5% (nationally).	Employment opportunities for women in the service sector was 47.8% in 2013	-	Evaluation will be carried out by 2025
3. Flood-affected population in Battambang and Neak Loeung reduced by 30% of regularly affected population (50,400 in 2012).	“Before-project” flood-affected population is ____ ^{a/} in 2015	-	Evaluation will be carried out by 2025

^{a/} To be determined/updated during the preliminary design review to be undertaken by the DED Consultant.



APPENDIX H

BASELINE VALUES, PERFORMANCE TARGETS FOR INDICATORS, AND PROJECTED ACHIEVEMENTS

Output 1: SLEDPs adopted & implemented

Indicator 1.1: Baseline: The SLEDPs for Battambang, Bavet, Neak Loeung and Poipet are currently available. These were all prepared in 2011.

Target: SLEDPs with sex-specific and climate-resilience measures incorporated, adopted, & disclosed; updated as required.

Projected Achievement: SLEDPs with sex-specific and climate-resilience measures incorporated, adopted, & disclosed by 2014; and updated by 2018.

Indicator 1.2: Baseline: As of 2014, no gender awareness and sensitization training has been conducted for executing and implementing agency staff.

Target: Gender awareness and sensitization training conducted for 30 executing and implementing agency staff.

Projected Achievement: Gender awareness and sensitization training conducted for 30 executing and implementing agency staff by 3rd quarter 2016.

Output 2: Priority urban infrastructure investment implemented

Battambang

Baseline: Battambang has an existing wastewater treatment plant (WWTP) in Chamkar Samraong serving the west part of the town. The WWTP has a capacity of 2,800 cu.m./day, built in 1994. Since 2014, the system is not functioning due to broken pump facilities and blocked conduits.

Target: 52,000 residents serviced by new and rehabilitated wastewater treatment plants (capacity 2,800 cu m/day) by 2020. Flood events of facility reduced (based on 50-year flood frequency).

Projected Achievement:

- 33,350 residents serviced by new wastewater treatment plant by 2020.
- The capacity of the new WWTP is 7,470 cu.m./day (Stage 1, design year is 2030).
- The new WWTP (completion of infrastructure in June 2020) will be servicing the following in the east part of the town by 2020:

Particular	Sangkat		Total
	Prek Preah Sdech	Rattanak	
Residents/Population	15,900	17,450	33,350
Commercial/Tourism Facilities	15	57	72
Public Facilities	2	4	6
Wastewater Generation (cu.m./day)	2,376	3,110	5,486

Source: PISCD, Battambang Wastewater Treatment Subproject Technical Assessment and Preliminary Design Report, July 2015.

- The rehabilitated WWTP (capacity 2,800 cu.m./day) will be servicing 18,650 residents, in the west part of the town, currently connected to the



existing sewerage system.

- Flood events of facility reduced (based on 50-year flood frequency).

Indicator 2.2: **Flood Control** Baseline: The extent of flooding in the subproject area in Battambang Municipality is as follows:

Sangkat	Total Area (ha)	Affected by Flood During Wet Season		
		% of Total Area	Area (ha)	Population
1. Svay Por	199	25	50	1,516
2. Preah Preah Sdach	294	50	147	7,444
3. Rottanak	505	40	202	8,072
Total			399	17,032

Source: Consolidated Sangkat Report on Flooding in Battambang. 2013

Validated with Chief of Commune Council of each Sangkat on 24 February 2016.

The projected year 2018 total population within the flood-prone areas in the three Sangkats is 18,800.

Target: Flood events of city center, near river, reduced (based on 50-year flood frequency), benefiting 15,120 persons by 2018.

Projected Achievement: Flood events of city center, near river, reduced (based on 50-year flood frequency), benefiting _____* persons by 2018.

The implementation of this Flood Control Subproject has been deferred.

* The reduction of flood events due to the subproject, and the number of persons benefited will be updated/determined during the preliminary design review and detailed engineering design to be undertaken by the DED Consultant.

Indicator 2.3: **Material Recovery Facility** Baseline: The baseline value for the indicator is “nil” since subproject is construction of new MRF.

CINTRI is contracted, since 2010, to provide waste collection and disposal services in the town. A total of 7,249 households are served in 8 out of 11 sangkats. The present tonnage of solid waste that is collected daily is estimated to be 80-90 tons.

Source: Mr. To Thanarith, Operations Manager, CINTRI, Battambang, 24 February 2016.

Target: 30 cu m of recyclables per day segregated benefiting 128,000 residents by 2018.

It is noted that the target of 30 cu m of recyclables per day in the DMF is inconsistent with the value in the Feasibility Study of 60 cu m of recyclable per day.

Projected Achievement: 60 m³ or eight (8) tons of dry, source segregated and non-biodegradable waste processed per day.

Bavet

Baseline: Bavet has no existing WWTP, hence the baseline value for the indicator is “nil”.



Treatment Target: 29,000 residents serviced by wastewater treatment plant (capacity 255 cu m/day) by 2019. Flood events of facility reduced (based on 50-year flood frequency).

Projected Achievement: 22,990 residents serviced by wastewater treatment plant (capacity 3,950 cu.m./day) by 2019. Flood events of facility reduced (based on 50-year flood frequency).

The new WWTP (completion of infrastructure in December 2018) will be servicing the following in Sangkat Bavet by 2019:

- 22,990 residents/population
- 27 commercial facilities, and
- 10 public buildings

The capacity of the new WWTP is 3,950 cu.m./day (Stage 1, design year is 2025).

Source: PISCD, Bavet Wastewater Treatment Subproject Technical Assessment and Preliminary Design Report, July 2015.

Indicator 2.5: Urban Road Baseline: The subproject will benefit not only the residents of Bavet but also the traffic between Cambodia and Viet Nam.

The projected population of Bavet by 2019 (year of completion of construction) is 40,600.

Source: Subproject Feasibility Study, Bavet Urban Road, ADB TA 7644-REG, May 2012.

Number of persons/year entering Cambodia from Vietnam (2010 to 2015)

2010	2011	2012	2013	2014	2015
547,565	621,010	673,830	680,723	738,441	751,811

Number of persons/year exiting Cambodia to Vietnam (2010 to 2015)

2010	2011	2012	2013	2014	2015
559,074	644,208	725,104	733,451	749,568	775,432

Source: Immigration Office at Bavet Border Check Point. Collected by Mr. Keo Sarorng, Social & Environment Officer, Bavet PIU.

Target: 6, 14 km of main urban road upgraded with drainage structures, benefiting 37,100 residents by 2019.

Note: 37,100 is the population of Bavet in 2010.

Projected Achievement: 6, 14 km of main urban road upgraded with drainage structures, benefiting 40,600 residents by 2019.

Indicator 2.6: Material Recovery Facility Baseline: The baseline value for the indicator is “nil” since subproject is construction of new MRF.

Hybrid Garbage Co. Ltd. (HGCL) is contracted, since 18 September 2015, to provide waste collection and disposal services in the town. A total of 34,884 residents are served in 4 out of 5 sangkats. The present tonnage of solid waste that is collected daily is estimated to be 20-30 tons. The company collects waste from casinos, hotels, guesthouses, market, households, restaurants, commercial establishments and institutions at the urban sector of Bavet on daily basis (Monday through Sunday).

Source: Mr. Yen Chham, Administration Manager, Hybrid Garbage Co. Ltd, Bavet, 15 February 2016.

Target: 30 cu m of recyclables per day segregated, benefiting 24,000 residents by 2018.



Projected Achievement: 30 m³ or four (4) tons of dry, source segregated and non-biodegradable waste processed per day benefiting ____* residents by 2018.

Source: Subproject Feasibility Study, Bavet Material Recovery Facility, ADB TA 7644-REG.

* The original target value will be validated/updated during the preliminary design review and detailed engineering design to be undertaken by the DED Consultant.

Neak Loeung

Baseline: The current population within the subproject area is 9,338 residents, as follows:

No. of Households	No. of Families	Population	Within the Flood Protection Area			
			Percentage	No. of Households	No. of Families	Population
Neak Loeung Commune						
1,538	1,781	8,864	60%	923	1,069	5,318
Prek Khsay Khor Commune						
2,282	2,351	11,485	35%	799	823	4,020
Total						
3,820	4,132	20,349		1,722	1,891	9,338

Source: Mr. Phum Samphorn, Deputy Governor, Peam Ror District, 16 February 2016.

Target: 5.4 km flood protection dike constructed; 363 ha of residential and commercial areas protected from annual flooding (based on 50-year flood frequency), benefiting 24,700 residents by 2019.

Projected Achievement: 3.9 km flood protection dike constructed by 2019; benefiting ____* residents and protecting 355 ha from annual flooding (based on 50-year flood frequency) for development into residential and commercial areas.

The implementation of this Flood Protection Subproject has been deferred.

* The length of the flood protection dike, and the number of residents and the hectareage of the area that will be protected will be updated/determined during the detailed engineering design to be undertaken by the DED Consultant.

Poipet

Baseline: Poipet has no existing WWTP, hence the baseline value for the indicator is “nil”.

Target: 65,000 residents serviced by wastewater treatment plant (capacity 16,400 cu m/day) by 2019. Flood events of facility reduced (based on 50-year flood frequency).

Projected Achievement: 45,790 residents serviced by wastewater treatment plant (capacity 7,660 cu m/day) by 2019. Flood events of facility reduced (based on 50-year flood frequency).

The new WWTP (completion of infrastructure in December 2018) will be servicing the following in Sangkat Poipet by 2019:

- 45,790 residents/population, and
- 29 commercial facilities

The capacity of the new WWTP is 7,660 cu m/day (Stage 1, design year is



2020).

Source: PISCD, Poipet Wastewater Treatment Subproject Technical Assessment and Preliminary Design Report, July 2015.

Indicator 2.9: **Solid Waste Management** Baseline: The baseline value for the indicator is “nil” since the sanitary landfill is a new facility.

Poipet Cleaner is contracted, since 2008, to provide waste collection and disposal services in the town. A total of 2,200 households are served in 2 out of 3 sangkats. The present tonnage of solid waste that is collected daily is estimated to be 50-65 tons. Of which, an average of about 28 tons/day are collected from hotels/casino and other business and institutional establishments, and an average of about 35 tons/day are collected from households.

Source: Ms. Sareoung Sophea, Poipet Cleaner, 25 February 2016.

Target: 20 tons/day of solid waste deposited in sanitary landfill, benefiting 58,600 residents by 2019

Projected Accomplishment: ____* tons/day of solid waste deposited in sanitary landfill, benefiting ____* residents by 2019

The implementation of this Solid Waste Management Subproject has been deferred.

* The original targets will be verified/updated during the preliminary design review and detailed engineering design to be undertaken by the DED Consultant.

Baseline: The baseline value for the indicator is “nil” since subproject is construction of new MRF.

Target: 30 cu m of recyclables per day segregated, benefiting 58,600 residents by 2018.

Projected Achievement: 60 m³ or eight (8) tons of dry, source segregated and non-biodegradable waste processed per day benefiting ____* residents by 2018.

Source: Subproject Feasibility Study, Poipet Material Recovery Facility, ADB TA 7644-REG, June 2012.

* The original target value will be validated/updated during the preliminary design review detailed engineering design to be undertaken by the DED Consultant.

Output 3: Institutional capacity strengthened

Indicators 3.1, 3.2 & 3.3: Baseline: The SECTDP is considered as the first major urban sector development assistance of the ADB in the GMS that integrates urban environment improvement and economic infrastructure with institutional capacity development for sustained economic growth. Hence the baseline value for these indicators is “nil”.

Target: The performance targets of these indicators are as specified in the DMF.

Outcome: Urban infrastructure improved and climate resilience enhanced in Battambang, Bavet, Neak Loeung, and Poipet

Indicator 1: Baseline: The “before-project” number of inhabitants/individuals that have access to existing urban infrastructure that are to be rehabilitated/upgraded in the subprojects is the total of the baseline values of Output 2 Indicators 2.1 and 2.5, as follows:

Particular	Value
Residents presently connected to existing sewerage system and	18,650



WWTP that will be rehabilitated in Battambang.	
Present traffic volume (residents/individuals) of main urban road to be upgraded in Bavet.	_____ *
Total number of inhabitants/individuals that have access to existing urban infrastructure	_____ *

* To be determined/updated during the preliminary design review and detailed engineering design to be undertaken by the DED Consultant.

Target: Improved access to urban infrastructure affects 558,220 inhabitants (cumulative figure) in four project towns.

Projected Accomplishment: Improved access to urban infrastructure affects _____ inhabitants (cumulative figure) in four project towns.

This is the total of the target number of residents/individuals benefiting from the urban infrastructure subprojects, i.e. total of targets for Indicators 2.1 to 2.10, as follows:

Town/ Indicator no.	Indicator	Updated Target
Battambang		
2.1	No. of residents serviced by new & rehabilitated WWTP	52,000
2.2	No. of persons benefiting from flood control	_____ *
2.3	No. of residents benefiting from MRF	_____ *
Bavet		
2.4	No. of residents serviced by WWTP	22,990
2.5	No. of residents/individuals benefiting from upgraded urban road	_____ *
2.6	No. of residents benefiting from MRF	_____ *
Neak Loeung		
2.7	No. of persons benefiting from flood protection	_____ *
Poipet		
2.8	No. of residents serviced by WWTP	45,790
2.9	No. of residents benefiting from sanitary landfill	_____ *
2.10	No. of residents benefiting from MRF	_____ *
Total inhabitants having improves access to urban infrastructure		_____ *

* To be determined/updated during the preliminary design review and detailed engineering design to be undertaken by the DED Consultant.

Indicator 2: **Baseline:** Economic loss due to poor sanitation was \$32 per capita in year 2005.

Source: *Economic Impacts of Sanitation in Cambodia, Summary. Water and Sanitation Program – East Asia and the Pacific (WSP-EAP). World Bank. 2008*

Target: Annual economic impact of poor sanitation, accounting for a loss of \$33 in 2005 per capita per year, reduced by 40%.

Projected Accomplishment: Annual economic impact of poor sanitation, accounting for a loss of \$32 in 2005 per capita per year, reduced by 40%.

Indicator 3: **Baseline:** The “before-project” total hectarage of urban areas affected by perennial flooding in Battambang and Neak Loeung, is as follows:



Town	Urban areas presently affected by perennial flooding, hectares
Battambang.	_____*
Neak Loeung	335
Total	_____*

* To be determined/updated during the preliminary design review & detailed engineering design to be undertaken by DED Consultant.

Target: Urban areas affected by perennial flooding reduced by 30%.

This is the total of the target hectareage of urban areas (i) benefiting from reduction of flood events, due to the flood control subproject in Battambang; and (ii) protected from annual flooding, due to the flood protection subproject in Neak Loeung. This is expressed as a percentage of the baseline value.

Town/ Indicator no.	“Before-project” (baseline) urban areas affected by perennial flooding Hectare	Urban areas protected from flooding due to flood control/protection subprojects	
		Hectare	% **
Battambang / 2.2	_____*	_____*	_____**
Neak Loeung / 2.7	335	335	100
Total	_____*	_____*	_____**

* To be determined/updated during the preliminary design review and detailed engineering design to be undertaken by the DED Consultant.

** Urban areas protected from flooding due to flood control/protection subprojects as a percentage of “before-project” (baseline) urban areas affected by perennial flooding.



APPENDIX I PUBLIC INFORMATION BOOKLET



KINGDOM OF CAMBODIA



**Ministry of Public
Works and Transport**



Asian Development Bank

Project Information Disclosure

GMS: Southern Economic Corridor Towns Development Project

Project Location: Poipet, Battambang and Bavet

June 2018

A. PROJECT OVERVIEW

The Royal Government of Cambodia (RGC) has received loans and grants from the Asian Development Bank (ADB) towards the cost of the Greater Mekong Sub-region (GMS) Southern Economic Corridor Towns Development Project (the Project).

The Project will enhance the competitiveness of towns along the Southern Economic Corridor (SEC). The Project will transform the Cambodian corridor towns of Poipet Battambang and Bavet into economic hubs by improving urban-environmental infrastructure and strengthening institutional capacities of provincial and local authorities.

The Project's expected outcome is improved urban infrastructure and enhanced climate resilience in Battambang, Bavet and Poipet. The Project will cover eight subprojects comprising:

a) Poipet:

1. Construction of separate sewage interceptor, collection and haulage canals (Detail design by NJS, ongoing)
2. Upgrading of existing storm water drainage canals (2km, cover the area of Sangkat Poipet and Pshakandal of Poipet town)
3. Installation of new WWTP (68mx68m, 4000m³/day)
4. Material Recovery Facility (800m², 60m³/day)

b) Battambang:

1. Construction of storm water drainage canal (13.50 km)
2. Material Recovery Facility (800m², 60m³/day)

c) Bavet:

1. Improvement and widening of main urban road and construction of drainage structure on both roadsides (6.14km)
2. Material Recovery Facility (800m², 60m³/day)





B. PROJECT BENEFITCIARY

The project construction of separate sewage, drainage, urban road and material recovery facility,, significant benefits that will be generated from the project including:

- Public health as well as city environment
- Supported existing future tourism development
- Provided more employment and livelihoods opportunities
- Improving the water quality of the river and stream water
- improved and supported the ongoing sustainable development
- Trade services will increase
- Transport and communication services will increase



MRF will be construct

C. ENVIRONMENTAL IMPACT and MITIGATION MUSURE

During pre-construction, construction and post- construction, the environmental impact will happenn such as water supply and electric or cables facility, no bypass, no road access, noise, air and water quality; soil quality and economic losses due to construction, mitigation measures will be taken into account in order to minimize negative impacts in which result from the construction and operation stage.

Impact		Mitigation Measures
Preconstruction Phase		
1. Confirmation of no required resettlement relocation and compensation		Affected persons well informed well ahead of subproject implementation



Impact	Mitigation Measures
2. Disclosure and engagement of community (community impacts)	Initiate Information Disclosure and Grievance process of IEE
3. UXO survey and removal (injured worker or public)	Ensure Government is consulted for UXO, and clears areas where necessary
4. Recruitment of workers (Spread of sexually transmitted)	Use local workers as much as possible thereby reducing number of migrant worker
5. Water supply facility	Design engineer will inform, cooperate, and discuss with local authority as well as with water supply authority/owners on the location of the water supply system in order to ensure that this system is properly prevented. In case of damage, the project owner should pay compensate or repairing for such damage.
6. Existing sewer line/telephone line/electric cable and traffic signboard	Design engineer will inform, cooperate, and discuss with local authority as well as with authority/owners on the location of the sewer line/telephone line/electric cable in order to ensure that this system is properly prevented. In case of damage, the project owner should pay compensate or repairing for such damage.
Construction Phase	
8. Increase in dust emissions from site construction	• Regularly apply wetting agents to exposed soil • Cover or keep moist all stockpiles of construction aggregates, and all truckloads of aggregates. • Minimize time that excavations and exposed soil are left open/exposed. • Stored construction materials well away from all human activity and resettlements, and cultural (e.g., schools, hospitals)
9. Noise arising from construction of the site facilities	• As much as possible restrict working time between 07:00 and 17:00. Maintain equipment in proper working order. • Replace unnecessarily noisy vehicles and machinery • Vehicles and machinery to be turned off when not in use • Provide temporary noise barriers around excessively noisy activity areas where possible such as trees.
10. Air pollution	• Construction materials should be properly covered during transport it in and out of the project sites. • Regularly, spray water on the earth road and construction site in dry period in order to minimize dust generation as much as possible, especially on exposed surface.
11. No bypass or access road	• Temporary wooden bridge will provide or detour road will construct
12. Leaks and spills of hazardous material	• The fuel storage must be far from watercourse or drain channel. • Contractor must provide precaution sign and security equipment for protection when the problem happens. • Be careful in loading and unloading fuel



Impact	Mitigation Measures
13. Contamination of land and surface water from excavated soil, concrete and construction waste	• Uncontaminated soil, concrete and construction waste to be disposed of in Government designated sites, which must never be in or adjacent surface waters. Designated sites must be clearly marked and identified. • Soil, concrete and construction waste must not be disposed of on sloped land, near cultural property or values, ecologically important areas, or on/near any other culturally or ecologically sensitive feature. • Where possible soil should be used at other construction sites, or disposed in spent quarries or borrow pits. • A record of type, estimated volume, and source of disposed soil must be recorded. • Contaminated soil disposal must follow Government regulations including handling. Transport, treatment(if necessary).
14. Land erosion	• Berms and plastic sheet fencing should be placed around all excavations and earthwork area. • Earthwork should be conducted during dry periods. • Maintain a stockpile of topsoil for immediate site restoration following backfilling. • Re-vegetate all soil exposure area immediately after work is completed.
15. Traffic disruption, accidents and public injury	• Schedule construction vehicle activity during light traffic periods. Create adequate traffic detour, and sufficient signage and warning lights. • Post speed limits, and create dedicated construction vehicle road • Demarcate additional location where pedestrians can develop road crossings away from construction area. • Avoiding construction/installation sewer pipes and transportation construction material in and out of the construction sites in busy time. • Traffic facilitator/traffic police shall be provided in construction sites where heavy traffic always happened in the road
16. Worker camp (Pollution and Social Problem)	• Locate worker camps away from human settlements. • Ensure adequate housing and waste disposal facilities including pit latrines and garbage cans. • A solid waste collection program must be established and implemented that maintains a clean worker camps. • Locate separate pit latrines for male and female workers away from worker living and eating areas. • A clean-out or infill schedule for pit latrines must be established and implemented to ensure working latrines are available at all times.



Impact	Mitigation Measures
	• Worker camps must have adequate drainage. • Local food should be provided to worker camps. Guns and weapons not allowed in camps. • Transient workers should not be allowed to interact with the local community. HIV/Aids education should be given to workers.
17. Working condition of workers (occupational safety, security, accidents, risks)	• Proper fencing, protective barriers, and buffer zones should be provided around construction sites. • Sufficient signage and information disclosure, and site supervisors and night guards should be placed at all sites. • Worker and public safety guidelines RGC should be followed. • Standing water suitable for disease vector breeding should be filled in. • Worker education and awareness seminars for construction hazards should be given. • A construction site safety program should be developed and distributed to workers. • Appropriate safety clothing and footwear should be mandatory for all construction workers. • Adequate medical services must be on site or nearby all construction sites. • Pit latrine must be provided at worker camp and construction sites. • Drinking water must be provided at all construction sites. • Sufficient lighting used during necessary night work. • All construction sites should be examined daily to ensure unsafe conditions are removed.
Post Construction Operational Phase	
18. Odors	• Implementation of best-practice operating procedures to minimize the odors generated by the plant, including properly control on the sludge in ponds. • Mechanical ventilation facilities or chemical odor control shall be provided. • Planting vegetation around WWTP and pumping station site also one method to reduce smell spread out to the nearby households. • Provide education and awareness program to residents and others in the vicinity of the WWTP avoiding disposal solid waste/rubbish into the WWTP.
19. Noise disturbance	• Planting vegetation around WWTP and pumping station site also one method to reduce smell spread out to the nearby households. • Noise reducing buffer shall be provided.



Impact	Mitigation Measures
20. Operation of Drains(Periodic back up and local flooding)	Improved drains must be regularly cleaned and surface to maintain design capacity flows


D. GRIEVANCE REDRESS MECHANISM

People who may be affected by the subprojects or concerned about their environmental impacts are entitled to lodge complaints regarding any aspect of the preparation and implementation of the subproject.

The objective of the grievance redress mechanism is to resolve complaints as quickly as possible and at the local level through a process of conciliation; and, if that is not possible, to provide clear and transparent procedures for appeal.

A well-defined grievance redress and resolution mechanism will be established to resolve grievances and complaints in a timely and satisfactory manner. All affected persons will be made fully aware of their rights, and the detailed grievance redress procedures will be publicized through an effective public information campaign. The grievance redress process applies to environmental issues and includes three steps of which three are followed before complaints may be elevated to a court of law as a last resort, as follows:

- (i) 1st step: Complaints and grievances will be provided verbally or in writing to the village chief, commune chief, or to contractor. The receiving agent will provide immediate written confirmation of receiving the complaint. If after 15 days the complainant does not hear from the contractor, village and commune chiefs or if he/she is not satisfied with the decision taken in the first stage, the complaint may be brought to the District Office or Project Implementation Unit (PIU).
- (ii) 2nd step: The District Office in cooperation with Project Implementation Unit (PIU) has 15 days within which to resolve the complaint to the satisfaction of all concerned. If the complaint cannot be solved at this stage, the District Office or Project Implementation Unit (PIU) will bring the case to the Provincial Grievance Redress Committee (PGRC) or Project Management Unit (PMU) and has to inform the complainant.
- (iii) 3rd step: The PGRC or Project Management Unit (PMU) meets with the aggrieved party and tries to resolve the situation. Within 30 days of the submission of the grievance, the Committee or PMU will make a written decision and submit copies to Provincial Court.

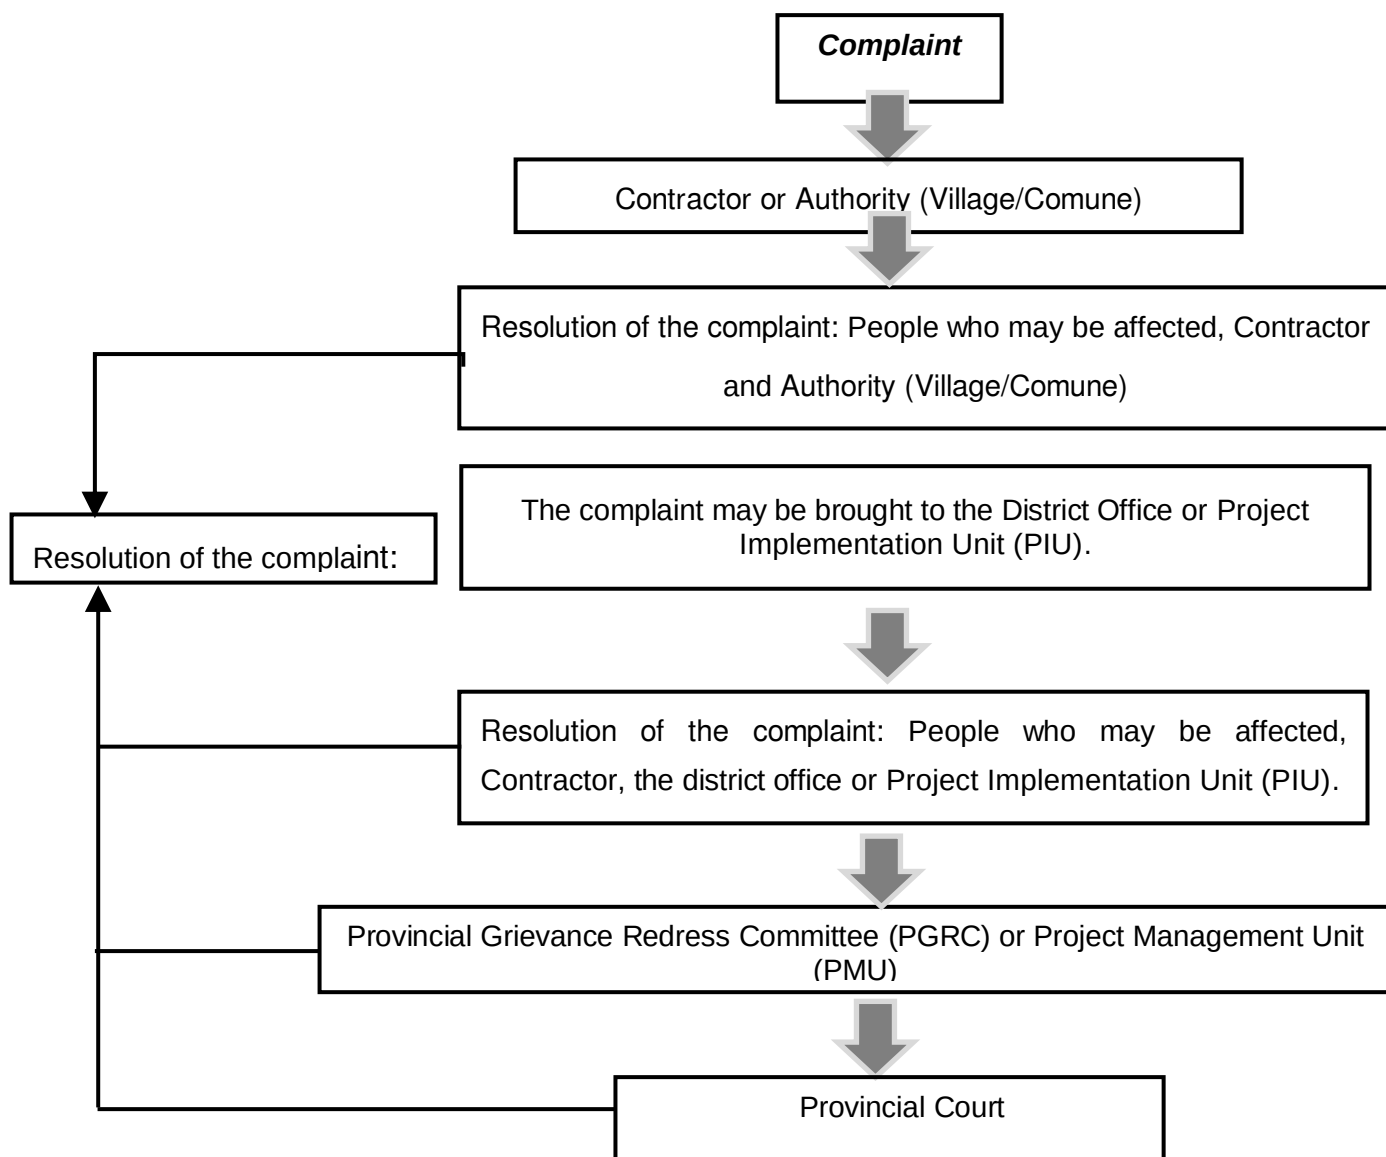



Telephone Number Contact

Bavet Town:

- Road improvement Contractor 077 258 224
- MRF Contractor 012 202 266 or 089 852 588
- Project Implementation Unit (PIU). 012 707 616 or 088 644 0544

Battambang Town:

- Storm drainage Contractor 096 916 6190
- MRF Contractor 012 202 266 or 089 852 588
- Project Implementation Unit (PIU) 092 930 966 or 012 479 030

Poipet Town:

- MRF Contractor 012 202 266 or 089 852 588
- Project Implementation Unit (PIU). 012 220 015 or 077 319 444

Envirenmental Spesialists of Project 012 916 545 or 012 863 994

Project Management Unit (PMU)



APPENDIX J
GENDER ACTION PLAN (GAP) MONITORING TABLE
Date of Update: 1 October- 31 December 2018

Project Title:	Greater Mekong Sub-region Southern Economic Corridor Towns Development Project ¹
Country:	Cambodia
Project No.	43319-033
Type of Project (Loan/Grant/TA):	Loan 2983
Approval and Timeline:	Approval 10 December 2012
Gender Category:	Effective Gender Mainstreaming (EGM)
Project Officer:	Mr. Ratha Sann
Project Impact:	The towns of Battambang, Bavet, Neak Loeung, and Poipet will become centers of economic activity in the Southern Economic Corridor
Project Outcome:	Urban infrastructure improved and climate resilience enhanced in Battambang, Bavet, Neak Loeung, and Poipet

Document 1: Progress of Gender Action Plan Implementation
Document 2: Status of Compliance with DMF

¹ The project was approved by the board on 10 December 2012, the effective date is on 08 April 2013 and estimated loan closing date on 30 June 2019. The total investment cost is estimated at \$ 54.78 million. Four corridor towns along the Southern Economic Corridor (SEC) were selected as project areas based on their economic potential, infrastructure constraints, and expressed commitment: Battambang, Bavet, Neak Leung, and Poipet.



1) Progress of Gender Action Plan Implementation

Gender Action Plan (GAP Activities, Indicators and Targets, Timeframe and Responsibility)	Progress to Date This should include information on period of actual implementation, sex-disaggregated quantitative updates (e.g. number of participating women, women beneficiaries of services, etc.), and qualitative information. However, some would be on-going - so explain what has happened so far towards meeting the target.	Issues and Challenges Please include reasons why an activity was not fully implemented, or if targets fall short, or reasons for delay, etc., and provide recommendations on ways to address issues and challenges
Output 1 (GAP): Strategic Local Economic Development Plan (SLEDP) adopted and implemented		
1.1. GAP Component 1 - Institutional Strengthening for Gender and Development (funded under capacity development and training)		
Gender issues reflected and mainstreamed in planning documents including socio-economic development plans and master plans Responsibility: Reviewed by Kol Prapey, Social Safeguard/Gender Specialist Time: October 2018 Revised by Hor Sakphea, Social Safeguard/Gender Specialist Time: December 2018 Action1: Achieved	SLEDPs of the 4 towns include sections on gender issues and measures to address these. Gender issues cited in the SLEDPs: • School dropped out for poor girls to find job to support family; • Gender-based violence; • Women particularly the female heads of households are not economically empowered and are not involved in decision-making in the community; because of low education; and much time spent in housework performing both tasks of men and women; • Women, especially young girls are at risk to human trafficking and the core labor issues; • Women do not occupy leadership positions in the community;	



	- Rural pregnant women have low knowledge on maternity health. Action in SLEDP: - Disseminating information on preventive anthelmintic treatment; - Disseminating law on gender-based violence; - Disseminating and promoting women and children’s right; - Disseminating law on human trafficking; - Provide food nutrition to women and children; - Promote gender equality, women empowerment and provide legal assistance for women and girls; - Promote women’s decision making in politics and public work.																														
PIS consultant’s gender specialists will collect sex-disaggregated data on EA/IAs staffing and technical designation as baseline and monitoring of gender targets for overall staff and management positions to refine the gender awareness training inputs Responsibility: Reviewed by Hor Sakphea, Social Safeguard/Gender Specialist Time: 31 December 2018 Action 2: On-track	- As of December 2018, 2 women (or 20%) of the 10 PMU staffs are female 7 women (22%) of the 32 PIU staffs in the four towns are women Table 1: Sex-disaggregated data of project staffs at PMU and PIUs by year <table> <tr> <th rowspan="2">Year</th> <th colspan="2">PMU</th> <th colspan="2">PIUs</th> </tr> <tr> <th>Male</th> <th>Female</th> <th>Male</th> <th>Female</th> </tr> <tr> <td>2015</td> <td>8</td> <td>2</td> <td>36</td> <td>8</td> </tr> <tr> <td>2016</td> <td>8</td> <td>2</td> <td>36</td> <td>8</td> </tr> <tr> <td>2017</td> <td>8</td> <td>2</td> <td>26</td> <td>5</td> </tr> <tr> <td>2018</td> <td>8</td> <td>2</td> <td>25</td> <td>7</td> </tr> </table>	Year	PMU		PIUs		Male	Female	Male	Female	2015	8	2	36	8	2016	8	2	36	8	2017	8	2	26	5	2018	8	2	25	7	
Year	PMU		PIUs																												
	Male	Female	Male	Female																											
2015	8	2	36	8																											
2016	8	2	36	8																											
2017	8	2	26	5																											
2018	8	2	25	7																											
Provide gender awareness and sensitization	98 participants including 21 women (21%) from																														



training for 30 EA/IA staff (each province); gender awareness training for managers and staff to increase sensitivity to different needs of women and men. Responsibility: Updated by Hor Sakphea, Social Safeguard/Gender Specialist Time: 30 June 2018 Action 3: Achieved	PMU, PIU, provincial department of women's affairs and contractors received gender sensitization including GAP orientation. As of October 2018, the project conducted three gender sensitization trainings. The training contents included: (i) gender mainstreaming policy in Cambodia, (ii) ADB gender policy and requirement, (iii) GAP orientation, (iv) Developing or integrating gender into work plan, (v) roles and responsibilities of project staffs in GAP implementation, (vi) collecting sex-disaggregated data and (vii) challenges and solution to GAP implementation.	
Output 2 (DMF & GAP output is the same): Priority urban infrastructure investments implemented		
GAP Component 2 - Empowerment for Women in Urban Community Development and Skills Training (funded under capacity development and training)		
Market assessment survey undertaken indicating current demand and economic growth areas in towns. Responsibility: Updated by Hor Sakphea, Social Safeguard/Gender Specialist Time: 30 September 2018 Target 1: Achieved	Conducted Market Assessment on Livelihood for Women in Poipet, Battambang, and Bavet through the methodologies are employed to collect information for this Assessment including conducting desk review, Conduct online research, Conduct distance and face-to face consultation. The market assessment was prepared for the SECTD with three different purposes as follows: 1- Review Cambodian women's existing literacy rates/absorptive capacities of three towns. 2- Assess the current employment market to identify high potential growth sectors and employment trends where quality, sustained, and appropriated employment can be created to support women who are living in project areas.	



	3- Assess and identify existing institution/NGOs for providing vocational/livelihood training skills in the three towns.												
Training for women to better position their entry in the growing employment demand areas arising from project interventions, targeting at least 150 women per town. Responsibility: Updated by Hor Sakphea, Social Safeguard/Gender Specialist Time: 30 September 2018 Target 2: Not yet due	The Market Assessment findings on Livelihood for Women will be presented to the relevant NGOs/CSOs to seek for training support as required by the waste pickers and affected female head of households.	Training for women will be conducted in early 2019											
A target of 40% women for employing existing informal waste pickers in the material recovery facilities (MRFs) funded under the project, including skills upgrade training. Responsibility: Prepared Hor Sakphea, Social Safeguard/Gender Specialist Time: March, 2018 Target 3: Not yet due	- All MRFs construction were fully completed, it is not yet operated. Currently, it is in the process to handover to municipality to manage the operation. - PMU agreed that all existing workers in current dumping size will be employed in MRFs. The condition to employ all existing waste pickers will be included in the term ad agreement of MRFs handover.												
Construction phase employment, construction workers will be 30% female; contractor records to be sex disaggregated for monitoring purposes. Responsibility: Updated by Hor Sakphea, Social Safeguard/Gender Specialist Time: 30 September 2018	- Sex-disaggregated labor monitoring sheet was developed and use by contractors. The contractor also provided on jobs training to women including bending and installing rebar. Person-Labor Day list is shown by month as follows: <table><tr><td>Month/Year</td><td colspan="2">Unskilled labor</td><td rowspan="2">% of female</td></tr><tr><td></td><td>Male</td><td>Female</td></tr><tr><td></td><td></td><td></td><td></td></tr></table>	Month/Year	Unskilled labor		% of female		Male	Female					
Month/Year	Unskilled labor		% of female										
	Male	Female											



Target 4: On-track	<table><tr><td>Mar-18</td><td>150</td><td>9</td><td>6%</td></tr><tr><td>Apr-18</td><td>540</td><td>180</td><td>25%</td></tr><tr><td>May-18</td><td>829</td><td>250</td><td>23%</td></tr><tr><td>Jun-18</td><td>2,095</td><td>767</td><td>27%</td></tr><tr><td>Jul-18</td><td>2,574</td><td>1.221</td><td>32%</td></tr><tr><td>Aug-18</td><td>3,042</td><td>1.413</td><td>32%</td></tr><tr><td>Sep-18</td><td>3,444</td><td>1.630</td><td>32%</td></tr><tr><td>Oct-18</td><td>2,556</td><td>955</td><td>27%</td></tr><tr><td>Nov-18</td><td>2,944</td><td>1.180</td><td>29%</td></tr><tr><td>Dec-18</td><td>2,390</td><td>1.169</td><td>33%</td></tr></table> - Type of activities performance by women included: (i) bending bar, (ii) cleaning the road, (iii) deliver brick and mixed cement and (iv) flag person and etc... - There is no child labor employed in the construction. - Women unskilled labor received equal pay (\$7/day) for equal work.	Mar-18	150	9	6%	Apr-18	540	180	25%	May-18	829	250	23%	Jun-18	2,095	767	27%	Jul-18	2,574	1.221	32%	Aug-18	3,042	1.413	32%	Sep-18	3,444	1.630	32%	Oct-18	2,556	955	27%	Nov-18	2,944	1.180	29%	Dec-18	2,390	1.169	33%	
Mar-18	150	9	6%																																							
Apr-18	540	180	25%																																							
May-18	829	250	23%																																							
Jun-18	2,095	767	27%																																							
Jul-18	2,574	1.221	32%																																							
Aug-18	3,042	1.413	32%																																							
Sep-18	3,444	1.630	32%																																							
Oct-18	2,556	955	27%																																							
Nov-18	2,944	1.180	29%																																							
Dec-18	2,390	1.169	33%																																							
GAP component 3 - HIV awareness and prevention (funded by construction companies)																																										
Awareness training provided by external HIV organizations and/or NGOs subcontracted by contractors during workforce mobilization for laborers and community surrounding construction locales Responsibility: Prepared and revised by Hor Sakphea, Social Safeguard/Gender Specialist Time: 30 September 2018 Action 4: On-track	- TOR for was prepared and included in contractor's contract. - An individual consultant is selected by contractor of Battambang (BUCG BEIJING URBAN CONSTRUCTION GROUP CO., LTD). Proposal on HIV/AIDS awareness is prepared by individual consultant and submitted to contractor. This proposal is reviewed and finalized by EA and will conduct training in January 2019.																																									
GAP component 4 - sanitation, health and hygiene Program (funded under capacity development and training)																																										



Training 2 health and sanitation promoters (male and female) in each town through a training of trainers (TOT) program Establish and train 2 MoWA staff as facilitators for IEC completion in each town. Responsibility: Updated by Hor Sakphea, Social Safeguard/Gender Specialist Time: 31 December 2018 Target 5: Not yet due	- TOT activity design on Health and Sanitation Promoter is developed by focusing on building concept of hygiene and sanitation; developing communication/facilitation/interpersonal skills for selected health and sanitation promoters, PDWA and PIUs of the 4 towns (Poipet, Battambang, Neak Loeung, and Bavet). - Two PDWA staffs were identified.	This activity will be implemented in first quarter 2019.
GAP component 5 - road safety campaign (funded under capacity development and training)		
Target girls as well as boys in school awareness campaigns Responsibility: Updated by Hor Sakphea, Social Safeguard/Gender Specialist Time: 30 June 2018 Action 5: On-track	- TOR for the road safety awareness campaign in Bavet prepared and included in contractor's contract.	This activity shall be implemented as soon as road construction commencing.
Output 3 (DMF & GAP output is the same): Institutional capacity strengthened		
GAP component 6 - institutional strengthening for gender and development (cost included in project output 1)		



Ensure that 20% of the overall staff positions and 20% of the management positions in the Project Management Units and Project Support Units to be female

Responsibility: Prepared by Hor Sakphea, Social Safeguard/Gender Specialist

Time: 31 December 2018

Target 6: Achieved

- 2 staffs (or 20%) of 10 PMU staffs are women. 1 woman is in management position and another woman is in support office.
- 7 staffs (22%) of 31 PIUs staffs are women.

Table 2: Number of project staffs at PIUs

PIUs	Male	Female	Total staff	% female
Battambang	6	3	9	33%
Piopet	7	2	9	22%
Neak Loeung	6	1	7	14%
Bavet	6	1	7	14%
Total	25	7	32	22%

Note: All position at PIUs are technical level with some are at decision-making level.



2) Status of Compliance with Design and Monitoring Framework (DMF)

Design Summary	Performance Targets and Indicators	Progress to Date This should include information on period of actual implementation, sex-disaggregated quantitative updates (e.g. number of participating women, women beneficiaries of services, etc.), and qualitative information. However, some would be on-going - so explain what has happened so far towards meeting the target.
Output 1: SLEDPs adopted and implemented in Poipet, Battambang, Bavet, and Neak Loeung	GAP implementation focuses on the SLEDPs thrusts on poverty, gender and ethnicity; more attention is given to the employment and livelihood issues of female heads of households; also, on the social issues confronting young girls along education, employment in the tourism and service sectors.	Gender action targets in the GAP are continuously implemented and monitored using gender performance monitoring tools.
Output 2. Priority urban infrastructure Investments implemented	30% of construction workers hired as unskilled laborers are women.	To date, 33% of total construction workers are women;
	2,000 people trained in project management and implementation, financial management, procurement, and social and environment safeguards, gender target achieve: Staff quota of 20% women in the PMU	Total 407 people trained and 67 (16%) women in the PMU and PIU with increased role in decision making.



Design Summary	Performance Targets and Indicators	Progress to Date
		This should include information on period of actual implementation, sex-disaggregated quantitative updates (e.g. number of participating women, women beneficiaries of services, etc.), and qualitative information. However, some would be on-going - so explain what has happened so far towards meeting the target.
	and PIU with increased role in decision making	
	Women hold 20% of overall staff positions and 20% of the management positions in the PMU and PIU	A total 10 members with 8 men and 2 women (20% women) as staff of PMU. A total 32 PIU staffs of the four towns, and 7 are women which is 22% of the management position.

Comments/ Remarks (conclusion of status of GAP implementation and suggestion/recommendation for improvement):

Accomplished by: Hor Sakphea, Social Safeguard/ Gender Specialist

Date Accomplished: 31 December 2018



APPENDIX K

STATUS OF COMPLIANCE WITH LOAN COVENANTS

No.	Covenant	Reference in LA	Status of Compliance
1.	Implementation Arrangements The Borrower shall ensure that the Project is implemented in accordance with the detailed arrangements set forth in the PAM. Any subsequent change to the PAM shall become effective only after approval of such change by the Borrower and ADB. In the event of any discrepancy between the PAM and this Loan Agreement, the provisions of this Loan Agreement shall prevail.	Schedule 5, Para. 1	Complied
2.	Environment The Borrower shall ensure, and cause MPWT to ensure, that the preparation, design, construction, implementation, operation and decommissioning of the Project comply with: (a) all applicable laws and regulations of the Borrower relating to environment, health and safety; (b) the Environmental Safeguards; and (c) all measures and requirements set forth in the IEEs, the EMPs and any corrective or preventative actions set forth in a Safeguards Monitoring Report. The Borrower shall ensure, and cause MPWT to ensure, that the foregoing is applied and implemented for all Parts of the Project, regardless of the financing source.	Schedule 5, Para. 2	Ongoing
3.	The Borrower shall ensure that Bavet and Poipet municipalities pass regulation requiring that no untreated waste water is discharged by industrial companies within 36 months of the Effective Date.	Schedule 5, Para. 3	Complied
4.	Land Acquisition and Involuntary Resettlement The Borrower shall ensure, and cause each Project province to ensure, that all land and all rights-of-way required for the Project are made available to the Works contractor in accordance with the schedule agreed under the related Works contract and all land acquisition and resettlement activities are implemented in compliance with: (a) all applicable laws and regulations of the Borrower relating to land acquisition and involuntary resettlement; (b) the Involuntary Resettlement Safeguards; and (c) all measures and requirements set forth in the RPs, and any corrective or preventative actions set forth in the Safeguards Monitoring Report. Without limiting the generality of the foregoing, the Borrower shall ensure, and cause each Project province to ensure, that prior to the commencement of Works a clear land title (which is free of any kind of encumbrance) shall be provided for the implementation of Parts 3, 6 and 10 of the Project.	Schedule 5, Para. 4	Ongoing
5.	Without limiting the application of the Involuntary Resettlement Safeguards or the RPs, the Borrower shall cause MPWT to ensure that no physical or economic displacement takes place in connection with the Project until: (a) compensation and other entitlements have been provided to affected people in accordance with the RPs; and	Schedule 5, Para. 5	



No.	Covenant	Reference in LA	Status of Compliance
	(b) a comprehensive income and livelihood restoration program has been established in accordance with the RPs.		people.
6.	Indigenous Peoples No impact on indigenous people is expected for the Project. In the event that there is any such impact, the Borrower shall cause MPWT to ensure that it adheres to applicable laws and regulations of the Borrower and the SPS.	Schedule 5, Para. 6	Complied
7.	Human and Financial Resources to Implement Safeguards Requirements The Borrower shall make available, and cause MPWT to make available, necessary budgetary and human resources to fully implement the EMPs and the RPs.	Schedule 5, Para. 7	Complied. Budget has been allocated
8.	Safeguards – Related Provisions in Bidding Documents and Works Contracts The Borrower shall ensure, and cause MPWT to ensure, that all bidding documents and contracts for Works contain provisions that require contractors to: (a) comply with the measures relevant to the contractor set forth in the IEEs, the EMPs and the RPs (to the extent they concern impacts on affected people during construction), and any corrective or preventative actions set forth in a Safeguards Monitoring Report; (b) make available a budget for all such environmental and social measures; and (c) provide the Borrower with a written notice of any unanticipated environmental, resettlement or indigenous peoples risks or impacts that arise during construction, implementation or operation of the Project that were not considered in the IEEs, the EMPs and the RPs.	Schedule 5, Para. 8	Complied. a. Complied. Bidding documents contains IEE&EMPs has been updated b. Complied. c. Complied.
9.	Safeguards Monitoring and Reporting The Borrower shall do the following: (a) submit semiannual Safeguards Monitoring Reports to ADB and disclose relevant information from such reports to affected persons promptly upon submission; (b) if any unanticipated environmental and/or social risks and impacts arise during construction, implementation or operation of the Project that were not considered in the IEEs, the EMPs and the RPs, promptly inform ADB of the occurrence of such risks or impacts, with detailed description of the event and proposed corrective action plan;		



No.	Covenant	Reference in LA	Status of Compliance
	under terms of references acceptable to the Borrower and ADB, to verify information produced through the Project monitoring process and facilitate the carrying out of any verification activities; and report any actual or potential breach of compliance with the measures and requirements set forth in the EMPs and the RPs promptly after becoming aware of the breach.		(EMO) has been engaged. The EMO inception report has been reviewed, comments provided and the final version pending submission. The next safeguards report is pending submission
10.	Prohibited List of Investments The Borrower shall ensure that no proceeds of the Loan are used to finance any activity included in the list of prohibited investment activities provided in Appendix 5 of the SPS.	Schedule 5, Para. 10	Complied
11.	Labor Standards and Health The Borrower shall ensure, and cause MPWT to ensure that, all Works contractors: (a) comply with all applicable labor laws of the Borrower; (b) use their best efforts to employ women and local people, including disadvantaged people, living in the vicinity of the Project; (c) disseminate information at worksites on health safety for those employed during construction; (d) provide equal pay to men and women for work of equal type; (e) provide safe working conditions and separate culturally appropriate facilities for male and female workers; and (f) abstain from child labor.	Schedule 5, Para. 11	Complied
12.	Gender and Development The Borrower shall ensure, and cause MPWT to ensure, that: (a) the gender action plan developed for the Project is implemented in accordance with its terms; (b) the bidding documents include relevant provisions for contractors to comply with the measures set forth in this plan; (c) adequate resources are allocated for the implementation of this plan; and (d) key gender outcome and output targets (notably: (i) gender awareness and sensitisation training to be carried out for 30 staff from MPWT and the implementing agencies; (ii) 30 percent of the construction workers hired by the Works contractors should be female; (iii) 30 percent of the total staff in the project management unit and the project implementation units of the Project shall be female; and (iv) within 24 months of the Effective Date, 20 percent of the total management positions in the project management unit and the project implementation units of the Project shall be occupied by female) are monitored regularly and achieved.	Schedule 5, Para. 12	Complied
13.	The Borrower shall ensure, and cause MPWT to ensure that, the stakeholder communication strategy developed for the	Schedule 5, Para. 13	Ongoing



No.	Covenant	Reference in LA	Status of Compliance
	Project is implemented in a timely manner.		
14.	Sector Development The Borrower shall cause MPWT to: (a) adopt a business plan for achieving full cost recovery (to cover operation and maintenance expenditures) of the facilities developed under Parts 1, 4 and 8 of the Project prior to their physical completion; and (b) commit to making up shortfall through budget allocations to cover operation and maintenance expenditures.	Schedule 5, Para. 14	Not yet due
15.	Governance and Anticorruption The Borrower shall: (a) comply with ADB's Anticorruption Policy (1998, as amended to date) and acknowledge that ADB reserves the right to investigate directly, or through its agents, any alleged corrupt, fraudulent, collusive or coercive practice relating to the Project; and (b) cooperate with any such investigation and extend all necessary assistance for satisfactory completion of such investigation.	Schedule 5, Para. 15	Complied
16.	The Borrower shall ensure, and cause MPWT to ensure, that the anticorruption provisions acceptable to ADB are included in all bidding documents and contracts, including provisions specifying the right of ADB to audit and examine the records and accounts of the executing and implementing agencies and all contractors, suppliers, consultants, and other service providers as they relate to the Project.	Schedule 5, Para. 16	Complied
17.	The Borrower shall cause MPWT to prepare and effectively implement a good governance framework, in a form and substance acceptable to ADB during Project implementation.	Schedule 5, Para. 17	Complied
18.	The Borrower shall: (i) maintain separate accounts and records for the Project; (ii) prepare annual financial statements for the Project in accordance with accounting principles acceptable to ADB; (iii) have such financial statements audited annually by independent auditors whose qualifications, experience and terms of reference are acceptable to ADB, in accordance with international standards for auditing or the national equivalent acceptable to ADB; (iv) as part of each such audit, have the auditors prepare a report (which includes the auditors' opinion on the use of the Loan proceeds and compliance with the financial covenants of this Loan Agreement as well as on the use of the procedures for imprest fund and statement of expenditures) and a management letter (which sets out the deficiencies in the internal control of the Project that were identified in the course of the audit, if any); and (v) furnish to ADB, no later than 6 months after the end of each related fiscal year, copies of such audited financial statements, audit report and management letter, all in the English language, and such other information concerning these documents and the audit thereof as ADB shall from time to time reasonably request.	Article IV, Section 4.02 (a)	Complied
19.	ADB shall disclose the annual audited financial statements for the Project and the opinion of the auditors on the financial statements within 30 days of the date of their receipt by posting them on ADB's website.	Article IV, Section 4.02 (b)	Complied with
20.	The Borrower shall enable ADB, upon ADB's request, to	Article IV,	Complied with



No.	Covenant	Reference in LA	Status of Compliance
	discuss the financial statements for the Project and the Borrower's financial affairs where they relate to the Project with the auditors appointed pursuant to subsection (a)(iii) hereinabove, and shall authorize and require any representative of such auditors to participate in any such discussions requested by ADB. This is provided that such discussions shall be conducted only in the presence of an authorized officer of the Borrower unless the Borrower shall otherwise agree.	Section 4.02 (c)	
21.	The Borrower shall enable ADB's representatives to inspect the Project, the Goods and Works, and any relevant records and documents.	Article IV, Section 4.03	Complied
Mid-Term Review Mission 2-30 November 2018			
22.	General The procurement of Goods, Works and Consulting Services shall be subject to and governed by the procurement Guidelines, and the consulting Guidelines, respectively.	Schedule 4, Para. 1	Complied
23.	All terms, used in this schedule and not otherwise defined in this loan agreement have the meanings provided in the Procurement Guidelines and/or the Consulting Guidelines, as applicable.	Schedule 4, Para. 2	Complied
24.	Goods and Works Except as ADB may otherwise agree, Goods and works shall only be procured on the basis of the methods of procurement set forth below: (a) International Competitive Bidding; and (b) National Competitive Bidding	Schedule 4, Para. 3	Complied
25.	The methods of procurement are subject to, among other things, the detailed arrangements and threshold values set forth in the Procurement Plan. The Borrower may only modify the methods of procurement or threshold values with the prior agreement of ADB, and modifications must be set out in updates to the Procurement Plan.	Schedule 4, Para. 4	Complied
26.	Domestic Preference The Borrower may grant a margin of preference in the evaluation of bids under international competitive bidding in accordance with paragraphs 2.55(a) and 2.56 of the Procurement Guidelines for domestically manufactured Goods, and paragraphs 2.55(b) and 2.56 of the Procurement Guidelines for domestic Works.	Schedule 4, Para. 5	Complied
27.	National Competitive Bidding The Borrower and ADB shall ensure that, prior to the commencement of any procurement activities under national competitive bidding, the Borrower's national competitive bidding procedures are consistent with the Procurement Guidelines. Any modifications or clarifications to such procedures agreed between the Borrower and ADB shall be set out in the Procurement Plan. Any subsequent change to the agreed modifications and clarifications shall become effective only after approval of such change by the Borrower and ADB.	Schedule 4, Para. 6	Complied



No.	Covenant	Reference in LA	Status of Compliance
28.	Conditions for Award of Contract The Borrower shall not award any Works contract which involves environmental impacts until MPWT has: (a) Obtained the final approval of the IEE from the appropriate authority of the Borrower; and (b) Incorporated the relevant provisions from the EMP into the Works contract.	Schedule 4, Para. 7	Complied
29.	The Borrower shall not award any Works contract which involves involuntary resettlement impacts, until the Borrower has prepared and submitted to ADB the final RP based on the detailed design, and obtained ADB's clearance of such RP.	Schedule 4, Para. 8	Complied
30.	Consulting Services Except as ADB may otherwise agree, the Borrower shall apply quality- and cost-based selection for selecting and engaging Consulting Services.	Schedule 4, Para. 9	Complied
31.	The Borrower shall apply the following method for selecting and engaging the specified Consulting Services, in accordance with among other things the procedures set forth in the Procurement Plan: Consultant Qualification Selection for (a) detailed design and construction supervision; and (b) independent monitoring.	Schedule 4, Para. 10	Complied
32.	The Borrower shall recruit the individual consultants for such services as agreed with ADB in accordance with procedures acceptable to ADB for recruiting individual consultant.	Schedule 4, Para. 11	Complied
33.	Industrial or Intellectual Property Rights (a) The Borrower shall ensure that all Goods and Works procured (including without limitation all computer hardware, software and systems, whether separately procured or incorporated with other goods and services procured) do not violate or infringe any industrial property or intellectual property right or claim of any third party. (b) The Borrower shall ensure that all contracts for the procurement of Goods and Works contain appropriate representations, warranties and, if appropriate, indemnities from the contractor or supplier with respect to the matters referred to in subparagraph (a) of this paragraph.	Schedule 4, Para. 12	Complied
34.	The Borrower shall ensure that all ADB-financed contracts with consultants contain appropriate representation, warranties and, if appropriate, indemnities from the consultants to ensure that Consulting Services provided do not violate or infringe any industrial property or intellectual property right or claim of any third party.	Schedule 4, Para. 13	Complied
35.	ADB's Review of Procurement Decisions Contracts procured under international competitive bidding procedures and contracts for Consulting Services shall be subject to prior review by ADB, unless otherwise agreed between the Borrower and ADB and set forth in the Procurement Plan.	Schedule 4, Para. 14	Complied



APPENDIX L

RISK ASSESSMENT AND RISK MANAGEMENT PLAN (RARMP)

No.	Risk/Issue	Assessment without Mitigation	Action to Mitigated Risk	Responsibility	Target/Monitoring	Status as at (Dec 2018)	Supporting Evidence
Element 1: Procurement							
1.a	Irregularities relating to leaking prior or post procurement information before the contract award, collusion during the bidding process, and bid evaluation.	High	EA/IAs to establish PRC under the project in accordance with SOP/PM which are in line with ADB guidelines. EA/IAs shall ensure that the Declarations of Fraud and Ethical Conduct (DFEC) for PRC members and bidders (contractors, suppliers and consultants) are signed for each transaction. A copy of the declarations of winning bidders shall be part of the awarded contracts.	EA/IAs	All procurement transactions. EA/IA to monitor, ADB to verify during review missions, prior reviews and post reviews	PRC established on 22 November 2014. DFEC signed for each transaction, and copies of DFEC of winning bidders made part of awarded contracts.	PRC minutes of meetings. DFEC in awarded contracts.
1.b	Insufficient compliance with procedures	High	EA/ IAs are to adhere strictly to the procedures and guidelines set forth in the Loan Agreement, ADB's Procurement Guidelines, and SOP/PM that also cover ICB, NCB and shopping.	EA/IAs MEF monitors compliance with LA, ADB Procurement Guidelines and SOP/PM	All procurement transactions. EA/IA to monitor, ADB to verify during review missions, prior reviews and post reviews	Sufficient adherence/ compliance to procurement procedures and guidelines by EA/IAs, as monitored by MEF.	Bid Evaluation Committee (BEC) / Consultant Evaluation Committee (CEC) Reports & Recommendation. PRC minutes of meetings.
1.c	Weak procurement capacity.	High	EA/ IAs will receive continued hands-on training and technical assistance from consultants recruited under the project. SOP/PM will be used under the project.	ADB	Throughout Project duration	Training conducted by ADB in Dec. 2016. Inquiries on procurement can be directly made through ADB's procurement clinic.	PMU/ADB records.



No.	Risk/Issue	Assessment without Mitigation	Action to Mitigated Risk	Responsibility	Target/Monitoring	Status as at (Dec 2018)	Supporting Evidence
			Recruitment of a well-experienced procurement officer and website officer in PMU to avoid procurement and eventual implementation delays	EA/IAs	Throughout Project duration	Procurement Specialist contracted in Aug 2014 by PISCD and in June 2016 by PMU. Website officer is a PMU member.	Copies of contracts with PMU.
			Closely monitor and review procurement conduct, and where necessary, take measures to improve procedures based on lessons learnt from each successive procurement activity.	EA, MEF and ADB	Throughout Project duration	EA/MEF monitoring and reviewing the conduct of procurements.	BEC and CEC reports. PRC minutes of meetings.
			EA/IAs will recruit additional national and/or national procurement staff if required.	EA/IAs		No additional procurement staff required.	-
1.d	Delayed execution of schedules in the Procurement Plans and failure to track to procurement transactions.	High	Preparation of realistic annual Procurement Plan, tied to annual work plan and budget. EA/IAs will maintain Procurement Monitoring and Tracking Forms as defined in the SOP/PM, and take actions to address delays through additional consultant inputs, if necessary.	EA/IAs to prepare updated procurement plans and procurement tracking form.	Update procurement plan and monitor procurement tracking form during review missions as required	Procurement plan updated in 23 April 2018. Procurement Monitoring & Tracking Forms maintained.	Updated Procurement Plan. Filled out Procurement Monitoring & Tracking Forms.
1.e	Informal payments by contractors, suppliers and consultants	High	All contractors, suppliers and consultants – firms or individuals, national and international – bidding for contracts under the project shall sign the Declaration on Ethical Conduct and Fraud and Corruption in the SOP/ procurement manual.	EA/IAs and MEF	Throughout Project duration	Signed DFECs included in bids.	Signed DFECs.
Element 2: Financial Management							
2.a	Weak internal controls	High	EA/IAs to follow the financial management procedures specified in: (i) the Project Financing Agreement; (ii) the government's SOP and FMM.	EA/IAs; MEF to ensure compliance with SOP/ FMM, Loan	Throughout Project duration	Specified fin'l. management procedures followed since 31	Quarterly Report and PMU reports to MEF and ADB.



No.	Risk/Issue	Assessment without Mitigation	Action to Mitigated Risk	Responsibility	Target/Monitoring	Status as at (Dec 2018)	Supporting Evidence
				Agreement and ADB's Anticorruption Policy		Dec 2015 and ongoing.	
2.b	Weak financial management capacity	High	EA/IAs to receive continued hands-on training from consultants recruited under the project. The SOP/FMM will be used under the project, as well as relevant provisions of the Loan Agreement and ADB's guidelines on procurement and consulting services. Project to closely monitor and review financial management conduct and make necessary improvements as required.	EA and IAs and ADB EA and IAs	Throughout Project duration, conducted as a part of capacity building activities in the project	Hands-on-training ongoing. CapDev training scheduled. Monitoring & review since Dec 2015 and ongoing	CapDev Plan and training modules. Supported by Financial Management Specialist
2.c	Minimize cash transactions	High	Project to make all progress payments to contractors, suppliers and consultants – firms, individuals, national and international – by check or transfer to bank accounts, and retain evidence for audit and donor supervision missions.	MEF, EA and IAs	Throughout Project duration	Payments by check or bank transfer complied and ongoing.	Project Financial Statements
2.d	Delayed or non-existent reconciliation of advances for operating costs and expenses	High	Project to reconcile advances for operating expenses to staff or field offices within one week of the end of each month. No further advances to be paid until previous advance reconciled and cleared against documentary evidence.	EA and IAs	Throughout Project duration Project director to monitor and ADB to verify during review missions.	Reconciliation of advances complied and ongoing.	Project Financial Statements
Element 3 : Disclosure							
3.a	Possible conflict of interest among Project staff	Extremely High	Project staff to disclose private and public affiliations or personal interest before becoming involved in any project-related transaction, such as contract award. EA to prepare a declaration statement for staff's signature.	EA/IAs to ensure all Project staff sign the disclosures	Throughout Project duration Project director to ensure all project staff signs the disclosures.	Internal rules of the project updated and provided for avoidance of conflict of interest. Written disclosure is retained on file.	Internal rules of project for project staffs (PMU and PIUs)



No.	Risk/Issue	Assessment without Mitigation	Action to Mitigated Risk	Responsibility	Target/Monitoring	Status as at (Dec 2018)	Supporting Evidence
3.b	Inadequate transparency and disclosure	High	Project to agree information to be disclosed on the project and EA/IA websites biannually, with hard copies available for public inspection on request. At a minimum, the Project will disclose the information required by the Loan Agreement.	EA and ADB to agree the final list. Project director to arrange disclosure	Throughout Project duration.	Development of project website to be completed in February 2017. Information will then be uploaded to the website. Project information and grievance redress mechanism disclosed in target towns on 19, 21 and 22 June 2018 Bid documents was advertised by Phnom Penh Post newspaper and Project website	Project website. EMPs report and quarterly report Bid Evaluation Report (BER)
Element 4: Complaints and Remedies Mechanism							
5.a	Inadequate complaints and remedies mechanisms		Project to build well-defined complaints and remedies mechanism into project documents. Complaints procedures regarding procurement to follow process set out in Loan Agreement and SOP/PM. Following established publication of evaluation and awards, debriefing mechanism is also necessary not only to enhance transparency but also for the losing bidders to know their weak points.	EA/IAs EA and IAs in consultation with ADB	At effectiveness	To be complied with. PMU provides all bidders with copies of the evaluation and awards through email.	- Copies of emails from PMU
Element 5: Code of Ethical Conduct							
6.a	Poor enforcement of the Code of		Project to provide copies of the relevant laws and articles on Code of Conducts for civil	EA and IAs	Throughout Project duration	The Department of Human	Signed receipts available with the



No.	Risk/Issue	Assessment without Mitigation	Action to Mitigated Risk	Responsibility	Target/Monitoring	Status as at (Dec 2018)	Supporting Evidence
	Conduct for civil servants		servants to all project staff, including contracted staff. Project will maintain signed declaration of receipt of these documents by all project staff, including contracted staff. Similarly, all members of the procurement committee undertaking the evaluation shall sign the Declaration on Ethical Conduct.			Resources provides copies of Code of Conducts for Civil Servants to Ministry personnel upon employment.	Department of Human Resources.
Element 6: Sanctions							
7.a	Inadequate sanctions for fraudulent and corrupt activity by Project staff, contractors, suppliers and consultants		The Project to identify and apply sanctions available under current law and regulations of Cambodia, ADB's Loan Regulations, the Loan Agreement, and ADB's Procurement Guidelines and Consulting Guidelines. Sanctions for individuals may include transfer of duties, retraining, suspension, dismissal, re-grading, and prosecution under Cambodian Law. Sanctions for firms may include: termination of contract, debarment or blacklisting under ADB's Procurement Guidelines and Consulting Guidelines, or prosecution under Cambodian Law	EA and IAs, and in consultation with ADB	Effectiveness	Sanctions for firms included in termination of contract	Bidding document
Element 7: Project Specific Elements							
7.a	Poor enforcement of contract terms and need to conduct contractors performance evaluation		EA to ensure that contract terms are strictly enforced and the loan consultant will be a party to ensuring quality control of contract outputs, include acceptance of completion of works and services.	EA and IAs	Throughout Project duration	Contract terms for previous DED Consultant enforced, with the assistance of PISCD.	Evaluation of DED Consultant's output.
7.b	Poor quality of design and works construction		EA and IAs to ensure that approved infrastructure's design standards and specification developed by the respective agencies are utilized for the design of	EA and IAs, and with ADB NOL	Throughout Project duration	DED to be carried out by PISCD and CS Consultants.	DED reports and bid documents.



No.	Risk/Issue	Assessment without Mitigation	Action to Mitigated Risk	Responsibility	Target/Monitoring	Status as at (Dec 2018)	Supporting Evidence
			structures under the project. Project to recruit experienced detailed design consultant on a timely basis to assist the project.		Contract signed immediately after effectiveness	DED to be carried out by PISCD and CS Consultants.	V.O. no. 6 to PISCD contract, and CS contract.
7.c	Risk of low quality construction and supervision		Project to recruit experienced site supervision consultants to assist EA/IAs.. Regular technical audit is to be undertaken with any adverse findings to be acted upon immediately. Project to evaluate contractors' performance with poor performing contractors declared ineligible to bid for at least one year.	EA and IAs, and with ADB NOL EA and IAs EA and IAs, and with ADB NOL	Prior to award of first works contract. Throughout Project duration. Annually	Construction Supervision Consultant recruited To be complied during construction. To be complied during construction.	CS contract document. - -



APPENDIX M
SUPPORT DOCUMENTS OF LAND ACQUISITION



ព្រះរាជាណាចក្រកម្ពុជា
ជាតិ សាសនា ព្រះមហាក្សត្រ

ក្រសួងសេដ្ឋកិច្ច និង ហិរញ្ញវត្ថុ

លេខ ៤៧/២០១៥ សហវ. ០១១៩

ថ្ងៃពុធ ១២ ខែ ឧសភា ឆ្នាំ ២០១៥ សំរឹទ្ធិស័ក ព.ស. ២៥៥៩

រាជធានីភ្នំពេញ, ថ្ងៃទី ៣១ ខែ ឧសភា ឆ្នាំ ២០១៥

សូមគោរពជូន

ឯកឧត្តមនាយករដ្ឋមន្ត្រី រដ្ឋមន្ត្រីក្រសួងសាធារណការ និងដឹកជញ្ជូន

កម្មវត្ថុ៖ ការប្រគល់ទីតាំងដីដែលគណៈកម្មការអន្តរក្រសួងបានធ្វើលទ្ធកម្មរួច សម្រាប់គម្រោងអភិវឌ្ឍន៍ក្រុងរបៀង
ខាងត្បូងដែលបានទទួលហិរញ្ញប្បទានសហប្រតិបត្តិការពីធនាគារអភិវឌ្ឍន៍អាស៊ី (ADB)។

យោង៖ លិខិតលេខ ១៨៧៩ សក/អក ចុះថ្ងៃទី ២៨ ខែ ឧសភា ឆ្នាំ ២០១៥ របស់ក្រសួងសាធារណការ និងដឹកជញ្ជូន
- លិខិតលេខ ២០៤២ សក ចុះថ្ងៃទី ១០ ខែ មិថុនា ឆ្នាំ ២០១៣ របស់ក្រសួងសាធារណការ និងដឹកជញ្ជូន។

សេចក្តីដូចមានចែងក្នុងកម្មវត្ថុ និងយោងខាងលើ ខ្ញុំសូមគោរពជម្រាបជូនឧត្តមនាយករដ្ឋមន្ត្រី មេត្តាជ្រាបដ៏
ខ្ពង់ខ្ពស់ថា៖ តាមសំណើរបស់ក្រសួងសាធារណការ និងដឹកជញ្ជូន គណៈកម្មការអន្តរក្រសួងដោះស្រាយផលប៉ះពាល់
សហការជាមួយក្រសួងសាធារណការ និងដឹកជញ្ជូន និងអនុគណៈកម្មការខេត្តស្វាយរៀង, ខេត្តបាត់ដំបង និងខេត្ត
បន្ទាយមានជ័យ បានចុះពិនិត្យ ពិគ្រោះយោបល់ និងធ្វើលទ្ធកម្មដីសម្រាប់សាងសង់អាងប្រព្រឹត្តិកម្ម និងស្ថានីយបូមប្រោះ
សម្អាតទឹកកខ្វក់ នៃគម្រោងខាងលើរួចរាល់ហើយ។

ហេតុដូច្នេះនេះ គណៈកម្មការអន្តរក្រសួងដោះស្រាយផលប៉ះពាល់ សូមប្រគល់ទីតាំងដីដែលបានធ្វើលទ្ធកម្មរួច
ជូនក្រសួងសាធារណការ និងដឹកជញ្ជូន ដើម្បីផ្តល់លទ្ធភាពឱ្យក្រុមហ៊ុនសាងសង់ដំណើរការការងារវិស្វកម្មតាមផែនការ
និងបន្តគ្រប់គ្រងនិងប្រើប្រាស់ទីតាំងដីទាំងនេះស្របតាមច្បាប់ និងលិខិតបទដ្ឋានគតិយុត្តជាធរមាន ចាប់ពីថ្ងៃប្រគល់-
ទទួលឯកសារនេះតទៅ។

ទីតាំងដីដែលបានធ្វើលទ្ធកម្មរួច រួមមានដូចខាងក្រោម៖

ល.រ	ខេត្ត/ ក្រុង	បរិយាយ	ទំហំដី	ទីតាំងភូមិសាស្ត្រ	លិខិតផ្ទេរសិទ្ធិកាន់កាប់ប្រើប្រាស់ ដីធ្លី និងប័ណ្ណសម្គាល់សិទ្ធិកាន់ កាប់អចលនវត្ថុ
១	ខេត្តបាត់ដំបង	អាងប្រព្រឹត្តិកម្ម	១០១ ៥៦៩ ម ^២	- ឃុំនា ស្រុកសង្កែ - ឃុំនា ស្រុកសង្កែ - ឃុំនា ស្រុកសង្កែ - ឃុំនា ស្រុកសង្កែ	- ក្បាលដីលេខ÷Bx 0074 - ក្បាលដីលេខ÷Bx 0075 - ក្បាលដីលេខ÷Bx 0108 - ក្បាលដីលេខ÷Bx 0110 ចុះថ្ងៃទី ១២- ឧសភា- ២០១៥

ទំព័រទី១នៃ២



២			១ ៧៤០ ម ^២	-ភូមិបេង, ឃុំអន្លង់វិល, ស្រុកសង្កែ	-ក្បាលដីលេខ÷០០៦ យអវ ចុះថ្ងៃទី ០៤-មករា-២០១៧
៣	ខេត្តបាត់ដំបង	ស្ថានីយបូមប្រោះទឹកកខ្វក់	២ ៤៦៦ ម ^២	-ភូមិរំចេក២, សង្កាត់ រតនៈ, ក្រុងបាត់ដំបង	-ក្បាលដីលេខ÷ 541 ចុះថ្ងៃទី ២៦-កុម្ភៈ-២០១៦
៤		អាងប្រព្រឹត្តិកម្ម	១០០ ០៦០ ម ^២	-ភូមិកូនដំរី, សង្កាត់និមិត្ត, ក្រុងប៉ោយប៉ែត	-ក្បាលដីលេខ÷៩៣២ កបប ចុះថ្ងៃទី ១១-មីនា-២០១៤
៥	ក្រុងឈ្មោយប៉ែត	ស្ថានីយបូមប្រោះទឹកកខ្វក់	១ ៣៥៨ ម ^២	-សង្កាត់ផ្សារកណ្តាល, ក្រុងប៉ោយប៉ែត	-ក្បាលដីលេខ÷ I 0682 ចុះថ្ងៃទី ២៧-កក្កដា-២០១៧
៦	ក្រុងបាត់ដំបង	ស្ថានីយបូមប្រោះទឹកកខ្វក់	១ ៤៥៦ ម ^២	-ភូមិច្រកលាវ, សង្កាត់បារិត	-ក្បាលដីលេខ÷០៨៨/១៧ ចុះថ្ងៃទី ១៧-កុម្ភៈ-២០១៧

អាស្រ័យដ្ឋានបានគោរពជម្រាបជូនខាងលើ សូមឯកឧត្តមទេសរដ្ឋមន្ត្រី មេត្តាជ្រាប និងចាត់ចែង តាមការគួរ។
សូមឯកឧត្តមទេសរដ្ឋមន្ត្រី មេត្តាទទួលនូវការគោរពដ៏ខ្ពង់ខ្ពស់ ពីខ្ញុំ

អនុរដ្ឋលេខាធិការក្រសួងសេដ្ឋកិច្ច និងហិរញ្ញវត្ថុ
និងជាប្រធានគណៈកម្មការក្រសួងដោះស្រាយផលប៉ះពាល់
ដោយគោរពប្រោសអភិវឌ្ឍន៍

ហ៊ុន សែន

បម្រុងជូន៖

- អគ្គនាយកដ្ឋានទ្រព្យសម្បត្តិរដ្ឋ និង
ចំណូលមិនមែនសារពើពន្ធ កសហវ
- ឯកសារ-កាលប្បវត្តិ

ទំព័រទី២នៃ២

h-v



ព្រះរាជាណាចក្រកម្ពុជា
ជាតិ សាសនា ព្រះមហាក្សត្រ

គំនូសបង្ហាញ
ទីតាំង កន្លែងបែងចែកសំរាម

ក្បាលដីទ្រូតលេខ៖ ...៦៨៥...សង្កាត់ ចុះថ្ងៃទី ១០ ខែមេសា ឆ្នាំ២០១៨ ស្ថិតនៅភូមិ ទួលពង្រ សង្កាត់ផ្សារកណ្តាល ក្រុងប៉ោយប៉ែត





1. ប្រតិភូគណៈកម្មាធិការប្រតិបត្តិការស្រាវជ្រាវ 11.603.47 គម្រោង
(ប្រតិភូគណៈកម្មាធិការប្រតិបត្តិការស្រាវជ្រាវស្រាវជ្រាវស្រាវជ្រាវស្រាវជ្រាវ)

ថ្ងៃចុះហត្ថលេខា: ០៣.០៨.២០១៧.

ប្រតិភូគណៈកម្មាធិការប្រតិបត្តិការស្រាវជ្រាវ
ស្រាវជ្រាវ
ស្រាវជ្រាវ
ស្រាវជ្រាវ
ស្រាវជ្រាវ

2. ប្រតិភូគណៈកម្មាធិការប្រតិបត្តិការស្រាវជ្រាវ 11.603.47 (ប្រតិភូគណៈកម្មាធិការប្រតិបត្តិការស្រាវជ្រាវស្រាវជ្រាវស្រាវជ្រាវស្រាវជ្រាវ)

ថ្ងៃចុះហត្ថលេខា: ០១.០៩.២០១៧.

ប្រតិភូគណៈកម្មាធិការប្រតិបត្តិការស្រាវជ្រាវ
ស្រាវជ្រាវ
ស្រាវជ្រាវ
ស្រាវជ្រាវ
ស្រាវជ្រាវ



ព្រះរាជាណាចក្រកម្ពុជា
ជាតិ សាសនា ព្រះមហាក្សត្រ

ខេត្តស្វាយរៀង
រដ្ឋបាលក្រុងបាទីធ្លា
លេខ ០១០១ រ.បក

ថ្ងៃសុក្រ ៥ រោច ខែពិសាខ ឆ្នាំច សំរឹទ្ធស័ក ព.ស ២៥៦២
បាវិត, ថ្ងៃទី ០៤ ខែឧសភា ឆ្នាំ ២០១៨

សូមគោរពជូន

ឯកឧត្តម ចៀង ពិសិដ្ឋ អគ្គនាយករង នៃអគ្គនាយកដ្ឋានសាធារណការ
និង ជា នាយក គម្រោងអភិវឌ្ឍន៍សេដ្ឋកិច្ចក្រុងរៀងខាងត្បូង
នៃក្រសួងសាធារណការ

កម្មវត្ថុ៖ ករណី ២០ ហិកតា សម្រាប់គម្រោងអភិវឌ្ឍន៍សេដ្ឋកិច្ចក្រុងរៀងខាងត្បូង ស្ថិត
នៅភូមិត្រពាំងផ្លុង សង្កាត់បាទី ក្រុងបាវិត ។

តាមកម្មវត្ថុខាងលើ ខ្ញុំសូមគោរពជម្រាបជូន ឯកឧត្តម នាយកគម្រោង មេត្តា
ជ្រាបថា ចំពោះដីទំហំ ២០ ហិកតា សម្រាប់ផ្តល់ជូនក្នុងការអភិវឌ្ឍន៍គម្រោងអភិវឌ្ឍន៍សេដ្ឋកិច្ច
ក្រុងរៀងខាងត្បូង របស់ក្រុងបាវិត សម្រាប់កន្លែងទីតាំងប្រតិបត្តិការ និង កន្លែងធ្វើអាង
ប្រតិកម្មទឹកស្អុយ ស្ថិតនៅភូមិត្រពាំងផ្លុង សង្កាត់បាទី ក្រុងបាវិត ខេត្តស្វាយរៀង ពិតជាដី
របស់រដ្ឋប្រគល់ឲ្យខេត្ត សម្រាប់អនុវត្តគម្រោងកន្លែងទីតាំងប្រតិបត្តិការ និង កន្លែងធ្វើអាង
ប្រតិកម្មទឹកស្អុយ ។

សេចក្តីដូចបានគោរពជម្រាបជូនខាងលើ សូម ឯកឧត្តម នាយកគម្រោង មេត្តា
ជ្រាបដឹងខ្ពង់ខ្ពស់ ។

សូម ឯកឧត្តម ទទួលនូវការគោរពរាប់អានដ៏ស្មោះអំពីខ្ញុំ ។

រដ្ឋបាលក្រុងបាទីធ្លា
លេខ ០១០១ រ.បក
លីម សៀងហេង
