




Ministry of Public Works and Transport
The Kingdom of Cambodia

**Fourth Greater Mekong Subregion
Corridor Towns Development Project**
ADB L3686/G0592/G0593 CAM

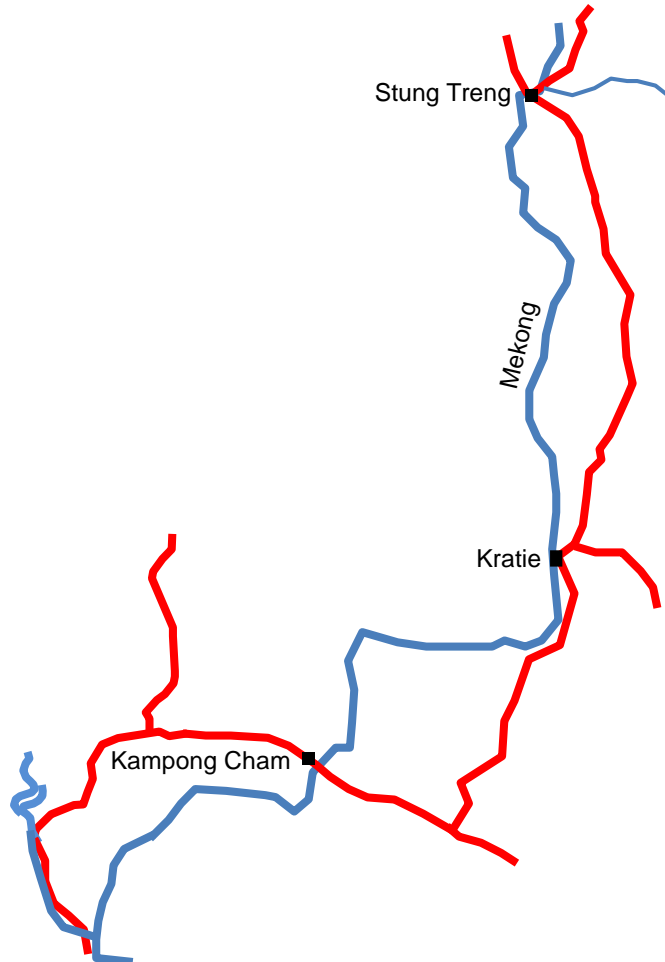

Quarterly Report
Quarter 4, 2021
October to December



Document Control Sheet

I				
Type of Document		Quarterly report		
Description		CTDP4 Q4-2021		
Version	Prepared by	Date	Checked by	Date
0	René van Doorn	24/01/2022	Pau Pat Busquets	25/01/2022

Contents

1	Introduction and Basic Data	1
1.1	Introduction	1
1.2	Basic Data	1
1.3	Cost Estimates and Financing Plan	1
1.3.1	CTDP4 Cost Estimates and Financing Plan	1
2	Utilisation of Funds	2
2.1	Contract Awards and Disbursements.	2
3	Project Scope and Purpose	4
3.1	Project Impact, Outcome and Outputs	4
3.2	Sub-Projects	4
3.3	Safeguards	5
3.3.1	Resettlement	5
3.3.2	Environment	5
3.4	Gender Action Plan	10
4	Implementation Progress	10
4.1	Project Organisation and Management	10
4.1.1	Contract Variations	10
4.2	Progress Monitoring	11
4.3	Implementation Activities	14
4.3.1	Consultant Team	14
4.3.2	General Activities	14
4.3.3	Activities by Output	14
4.3.4	Meetings	15
4.4	Project Costs	15
4.5	Procurement	16
4.5.1	Procurement Plan	16
4.5.2	Procurement of Civil Works and Equipment	16
4.6	Provincial Planning and Municipality Planning	18
4.6.1	General Activities	18
4.6.2	Activities by Output	18
5	Compliance with Covenants	18
6	Project Implementation Issues.	18
6.1	Issues Affecting Project Implementation Progress	18
6.1.1	Covid 19	18
6.1.2	Kampong Cham Landfill	18
6.1.3	Stung Treng Landfill	19
6.1.4	Kratie Landfill	19
6.1.5	Kampong Cham Wastewater.	19
6.1.6	Stung Treng Wastewater.	19
6.1.7	Kratie Wastewater	19
6.1.8	Kratie Town Centre Enhancements	20
6.1.9	Stung Treng Town Centre Enhancements	20
6.2	Other Issues	20
6.2.1	IESIAs	20
7	Work Plan	20

Annexes

Annex A	Design and Monitoring Framework
Annex B	List of Key Meetings during the Quarter
Annex C	Project Progress Monitoring (PPMS)
Annex D	Work Plan
Annex E	Consultant Inputs
Annex F	Gender Action Plan
Annex G	Procurement Plan
Annex H	Compliance with Loan and Grant Covenants
Annex I	Financial Management Action Plan

List of Tables

Table 1.1 Basic Data – CTDP4	1
Table 1.2 CTDP4 Summary Cost Estimates by Output (\$ million)	2
Table 1.3 CTDP4 Financing Plan	2
Table 2.1 Summary Contract Awards and Disbursements (US\$)	2
Table 2.2 Consolidated Awards and Disbursements, Loan 3686 and Grants 0592 and 0593	3
Table 2.3 Awards and Disbursements Status, Loan 3686	3
Table 2.4 Awards and Disbursements Status, Grant 0592	3
Table 2.5 Awards and Disbursements Status, Grant 0593	3
Table 3.1 Proposed Civil Works Sub-Projects	4
Table 3.2 Resettlement Documentation and Next Steps.	5
Table 3.3 Status of Resettlement Safeguards.	6
Table 3.4 Status of IEIA Preparation.	7
Table 3.5 Status of IEEs and EMPs.	9
Table 4.1 Contract Variations, Current and Previous Quarters	10
Table 4.2 Status of Sub-projects and other Project Activities.	12
Table 4.3 International and National Consultants Active during the Quarter	14
Table 4.4 Key Implementation Activities by Output During the Reporting Period	15
Table 4.5 Current Estimates of Sub-project Costs	15
Table 4.6 Status of Civil Works and Equipment Contracts.	17
Table 4.7 Key Implementation Activities by Output	18
Table 7.1 Key Activities Planned for Next Quarter	20

List of Figures

Figure 1.1 Location of Project Towns	1
Figure 3.1 CTDP4 Impact, Outcome and Outputs	4

Abbreviations


ADB	Asian Development Bank
CBO	Community-Based Organization
COI	Corridor-of-Impact
CPP	Community Procurement Procedures
CPS	Country Partnership Strategy
CSO	Civil Society Organizations
DC	Development Committee
DDR	Due Diligence Report
DRP	Detailed Resettlement Plan
DRM	Disaster Risk Management
EA	Executing Agency
EMP	Environmental Management Plan
FGD	Focus Group Discussion
GAP	Gender Action Plan
GDR	General Department of Resettlement (MEF)
GRC	Grievance Redress Committee
GRM	Grievance Redress Mechanism
IA	Implementing Agency
IEE	Initial Environmental Examination
IP(s)	Indigenous People(s)
IR	involuntary resettlement (IR)
MEF	Ministry of Economics and Finance
NCB	National Competitive Bidding
NGO	Non-Government Organisation
PIU	Project Implementation Unit
PMC	Project Management Consultant Team
PMU	Project Management Unit
ROW	Right of Way
SWM	Solid Waste Management
TA	Technical Assistance
TNA	Training Needs Assessment
TOR	Terms of Reference
USD	United States Dollar

1 Introduction and Basic Data

1.1 Introduction

- 1 The Government of The Royal Government of Cambodia has obtained a loan and grant from the Asian Development Bank (ADB) towards the cost of the Fourth Greater Mekong Subregion (GMS) Corridor Towns Development Project (hereinafter referred to as CTDP4). The location of the project towns is shown in Figure 1.1.
- 2 This is the Quarterly Report for Quarter 4, 2021 (October 1 to December 31).

Figure 1.1 Location of Project Towns

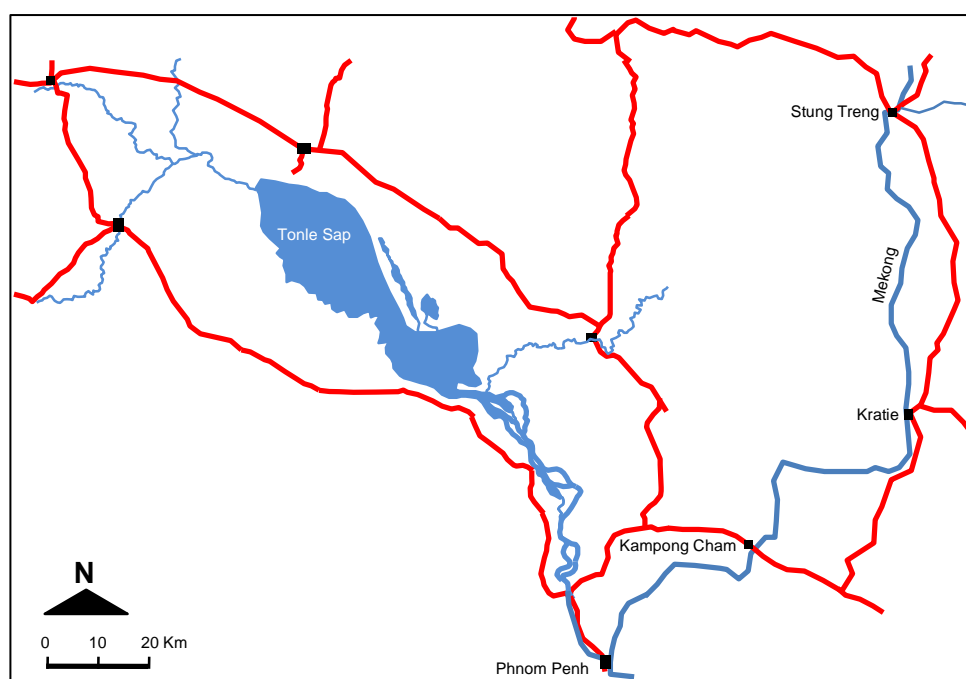

1.2 Basic Data

- 3 The key data for the project is shown in Table 1.1 below.

Table 1.1 Basic Data – CTDP4

ADB Project number:	Loan 3686, Grants G0592 & G0593
Project Title:	Fourth Greater Mekong Subregion Corridor Towns Development Project
Beneficiary:	Kingdom of Cambodia
Executing Agency:	Ministry of Public Works and Transport
Implementing Agency:	Provincial Governments of Kampong Cham, Kratie, Stung Treng
Date of Effectiveness:	14 December 2018
Closing Date:	30 June 2024
Date of Last ADB Mission:	May 2021 (VC)

1.3 Cost Estimates and Financing Plan

1.3.1 CTDP4 Cost Estimates and Financing Plan

- 4 The total cost of the project is estimated at US\$88.5m including contingencies. The breakdown of cost estimates is given in Table 1.2.

Table 1.2 CTDP4 Summary Cost Estimates by Output (\$ million)

Item	Amount
A. Base Cost	
1. Urban environmental infrastructure improved	66.87
2. Institutional effectiveness improved, and policy and planning environment for regional economic connectivity enhanced	9.67
Sub-Total (A)	76.54
B. Contingencies	9.70
C. Financial Charges During Implementation	2.26
Total (A+B+C)	88.50

Source: Asian Development Bank estimates.

5 The summary of the financing plan for CTDP4 is shown in Table 1.3.

Table 1.3 CTDP4 Financing Plan

Source	Amount (\$ million)	Share of Total (%)
Asian Development Bank		
Ordinary capital resources (concessional loan)	77.00	87.0
Special Funds resources (ADF grants)*	3.00	3.4
Korea EAKPF	0.50	0.6
Government	8.00	9.0
Total	88.5	100.0

* Including \$1.5m from Disaster Risk Reduction Fund (DRRF)

Source: Asian Development Bank estimates.

2 Utilisation of Funds

2.1 Contract Awards and Disbursements.

6 A summary of the total cumulative contract awards and disbursements is shown in Table 2.1. As of 31st December 2021, the contract awards amount to a total of **\$8,153,273** and to date disbursements total **\$3,693,350**.

Table 2.1 Summary Contract Awards and Disbursements (US\$)

Fund	Allocation	Contracts Awarded	Uncontracted Loan/Grant Balance	Contracts Disbursed	Undisbursed Loan/Grant Balance	Undisbursed Contract Balance
	A	B	C = A-B	D	E = A-D	F = B-D
Loan 3686	78,500,000	6,531,443	71,968,557	2,865,196	75,634,804	3,666,247
Grant 0592	1,500,000	996,838	503,162	600,000	900,000	396,838
Grant 0593	500,000	496,838	3,162	100,000	400,000	396,838
Government	8,700,000	128,154	8,571,846	128,154	8,571,846	-
Total	89,200,000	8,153,273	81,046,727	3,693,350	85,506,650	4,459,923

Table 2.2 Consolidated Awards and Disbursements, Loan 3686 and Grants 0592 and 0593

Fund	Allocation	Contracts Awarded	Uncontracted Loan/Grant Balance	Contracts Disbursed	Undisbursed Loan/Grant Balance	Undisbursed Contract Balance	Contracts Awarded %	Contracts Disbursed %
	A	B	C = A-B	D	E = A-D	F = B-D	B/A	D/A
Civil works	59,115,000	-	59,115,000	-	59,115,000	-	0	0
Goods & equipment	1,350,000	116,000	1,234,000	116,000	1,234,000	-	9	9
Consulting services	7,097,000	7,717,119	(620,119)	2,698,544	4,398,456	5,018,575	109	38
Incre. Adm. Cost	981,000	192,000	789,000	75,838	905,162	116,162	20	8
Interest charge	2,256,000	-	2,256,000	24,814	2,231,186	(24,814)	0	1
Unallocated	9,701,000	-	9,701,000	-	9,701,000	-	0	0
Advance Account				650,000	(650,000)	(650,000)		
Total	80,500,000	8,025,119	72,474,881	3,565,196	76,934,804	4,459,923	10	4

Table 2.3 Awards and Disbursements Status, Loan 3686

Fund	Allocation	Contracts Awarded	Uncontracted Loan/Grant Balance	Contracts Disbursed	Undisbursed Loan/Grant Balance	Undisbursed Contract Balance
	A	B	C = A-B	D	E = A-D	F = B-D
Civil works	58,615,000	-	58,615,000	-	58,615,000	-
Goods & equipment	1,350,000	116,000	1,234,000	116,000	1,234,000	-
Consulting services	5,597,000	6,223,443	(626,443)	2,198,544	3,398,456	4,024,899
Incre. Adm. Cost	981,000	192,000	789,000	75,838	905,162	116,162
Interest charge	2,256,000	-	2,256,000	24,814	2,231,186	-
Unallocated	9,701,000	-	9,701,000	-	9,701,000	-
Advance Account	-	-	-	450,000	(450,000)	-
Total	78,500,000	6,531,443	71,968,557	2,865,196	75,634,804	4,141,061

Table 2.4 Awards and Disbursements Status, Grant 0592

Fund	Allocation	Contracts Awarded	Uncontracted Loan/Grant Balance	Contracts Disbursed	Undisbursed Loan/Grant Balance	Undisbursed Contract Balance
	A	B	C = A-B	D	E = A-D	F = B-D
Works	500,000	-	500,000	-	500,000	-
Cons Svcs Proj Mgt	500,000	500,000	-	500,000	-	-
Cons Svcs ITC	500,000	496,838	3,162	-	500,000	496,838
Advance Account				100,000	(100,000)	(100,000)
Total	1,500,000	996,838	503,162	600,000	900,000	396,838

Table 2.5 Awards and Disbursements Status, Grant 0593


Fund	Allocation	Contracts Awarded	Uncontracted Loan/Grant Balance	Contracts Disbursed	Undisbursed Loan/Grant Balance	Undisbursed Contract Balance
	A	B	C = A-B	D	E = A-D	F = B-D
Cons Svcs ITC	500,000	496,838	3,162	-	500,000	496,838
Advance Account	-	-	-	100,000	(100,000)	(100,000)
Total	500,000	496,838	3,162	100,000	400,000	396,838

3 Project Scope and Purpose

3.1 Project Impact, Outcome and Outputs

- 7 The CTDP4 will improve urban services and enhance regional economic connectivity in provincial capital towns of Kampong Cham, Kratie, and Stung Treng along the Greater Mekong Subregion (GMS) Central Corridor in Cambodia. The project will finance key urban environmental infrastructure and enhance institutional effectiveness with a focus on private sector engagement and information and communication technology (ICT)-based public management systems, and the policy and planning environment for regional economic connectivity. The project will also improve institutional effectiveness to provide sustainable services and support an improved policy and planning environment for wastewater and solid waste management.
- 8 The Design and Monitoring Framework (DMF) is included in Annex A. The key elements of the DMF are summarised in Figure 3.1 below.

Figure 3.1 CTDP4 Impact, Outcome and Outputs

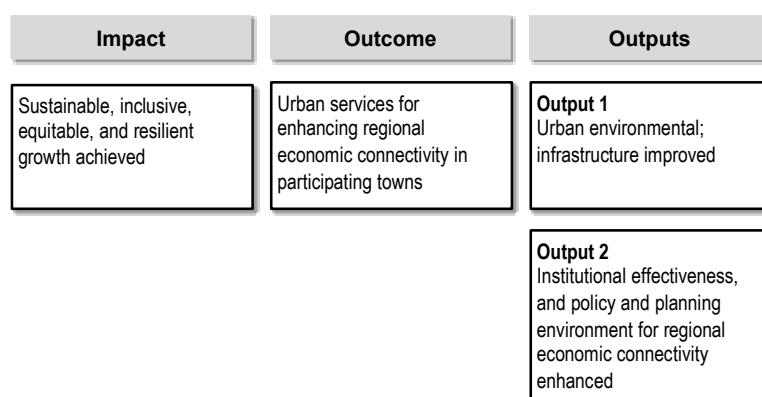

- 9 Currently no major changes to the Project scope or arrangements are envisaged and the Project should meet its original purpose.

3.2 Sub-Projects

- 10 The sub-projects are summarised in Table 3.1. This shows the scope as proposed in the RRP, which were based on the PPTA reports, as well as the latest estimates by PMC. The review and verification of the scope of some of the sub-projects is still ongoing at the time of this Quarterly Report.

Table 3.1 Proposed Civil Works Sub-Projects

Town	Sub-Projects	Scope of Sub-Projects	Latest PMC Estimates
Kampong Cham	Wastewater	▪ 5,000 m ³ /day WWTP, 137km sewers, 4.3km drains	▪ 5,000m ³ /day, 120km sewers, 4.2km drains
	Solid waste management	▪ 900,000m ³ landfill *	▪ Third site location approved, design preparations in progress.
Kratie	Wastewater	▪ 4,900 m ³ /day WWTP, 143km sewers, 12km drains	▪ 2,400m ³ /day, 41.1km sewers, drainage /stormwater under review
	Solid waste management	▪ 433,500m ³ landfill	▪ 2030: 150,000m ³
	Town centre improvements	▪ Footways, streetlights etc. – scope to be determined	▪ Under review
Stung Treng	Wastewater	▪ 3,650 m ³ /day WWTP, 147km sewers, 12km drains	▪ 2,900m ³ /day, 75.1km sewers, drainage included.
	Solid waste management	▪ 291,000m ³ landfill	▪ 2030: 70,000m ³
	Town centre improvements	▪ Footways, streetlights etc. – scope to be determined	▪ Under review

* Note: The PPTA figure of 900,000m³ for Kampong Cham landfill is not justified or explained in the PPTA reports.

3.3 Safeguards

3.3.1 Resettlement

- 11 The position regarding resettlement data/ documentation and the next steps are shown in Table 3.2. The overall status of resettlement safeguards is summarised in Table 3.3 on the next page.
- 12 The General Department of Resettlement (GDR) is preparing detailed resettlement plans (DRPs) for (i) Kratie and Stung Treng SWM subprojects (comments received from ADB to the draft version, comments being addressed by GDR), (ii) Kampong Cham WWTP subproject and (iii) Stung Treng WWTP subproject. None of the DRPs have been finalized to date, and hence ADB clearance for these is expected in year 2022. PMC has prepared corridor-of-impact (COI) maps, involuntary resettlement (IR) impact screening reports and field demarcation of the COI for GDR to use as basis for detailed measurement survey (DMS) for all of these subprojects. PMC is also on stand-by to assist in the preparation of the DRP documents if needed by GDR. Preparation for Kratie WWTP subproject DRP is anticipated to begin in the next reporting period.
- 13 No due diligence reports (DDRs) are expected at this stage, as all subprojects so far are IR category B. IR impact screening forms have been prepared for Stung Treng WWTP and Kampong Cham SWM subprojects, and will be prepared for Kratie WWTP subproject once DED is approved. There has been no progress in town centre improvement designs. Details of resettlement and social safeguards implementation progress is given in PMU semi-annual social safeguards construction monitoring reports.

Table 3.2 Resettlement Documentation and Next Steps.

Town	Sub-Projects	Pending data / documentation	Next steps in following quarter	Timeframe
Kampong Cham	Wastewater	<ul style="list-style-type: none"> ▪ Draft DRP from GDR 	<ul style="list-style-type: none"> ▪ Agree on temporary market sites (GDR, PIU and market management) ▪ Complete DRP (GDR)* 	<ul style="list-style-type: none"> ▪ 28/02/22* ▪ 30/06/22*
	Solid waste management	<ul style="list-style-type: none"> ▪ Access road COI, map and cross-section for latest SWM site option 	<ul style="list-style-type: none"> ▪ Prepare draft DRP (GDR)* 	<ul style="list-style-type: none"> ▪ 30/06/22*
Kratie	Wastewater & Drainage	<ul style="list-style-type: none"> ▪ WWTP site acquisition ▪ Draft DRP from GDR 	<ul style="list-style-type: none"> ▪ Prepare IR impact screening report ▪ Prepare draft DRP (GDR)* 	<ul style="list-style-type: none"> ▪ 30/04/22 ▪ 30/06/22*
	Solid waste management	<ul style="list-style-type: none"> ▪ Final DRP from GDR 	<ul style="list-style-type: none"> ▪ Complete DRP (GDR) (combined with STR)* 	<ul style="list-style-type: none"> ▪ 10/01/22*
	Town centre improvements	<ul style="list-style-type: none"> ▪ Outline design from town planners 	<ul style="list-style-type: none"> ▪ Review design and mitigate impact ▪ Prepare IR impact screening report 	<ul style="list-style-type: none"> ▪ 30/06/22
Stung Treng	Wastewater	<ul style="list-style-type: none"> ▪ Draft DRP from GDR 	<ul style="list-style-type: none"> ▪ Prepare draft DRP (GDR)* 	<ul style="list-style-type: none"> ▪ 30/06/22*
	Solid waste management	<ul style="list-style-type: none"> ▪ Final DRP from GDR 	<ul style="list-style-type: none"> ▪ Complete DRP (GDR) (combined with KRT)* 	<ul style="list-style-type: none"> ▪ 10/01/22*
	Town centre improvements	<ul style="list-style-type: none"> ▪ Outline design from town planners 	<ul style="list-style-type: none"> ▪ Review design and mitigate impact ▪ Prepare IR impact screening report 	<ul style="list-style-type: none"> ▪ 30/06/22

* Timing of deliverables depending on GDR

3.3.2 Environment

- 14 The overall status of environmental safeguards is summarised in Tables 3.4 and 3.5 on the next pages.
- 15 Initial Environmental Examinations (IEEs) were prepared for all the subprojects during the PPTA activities. PMC tasks regarding IEE and EMPs as per TOR are the following:
- Update/redraft IEEs based on the detailed engineering design and domestic IESIAs
 - Conduct additional analysis and data collection to ensure the final IEEs comply with ADB Safeguards Policy (SPS, 2009);
 - Prepare contract specific EMPs and assist MPWT/PMU to attach to the bidding documents or submit to the potential contractors.

Table 3.3 Status of Resettlement Safeguards.

CTDP4	Subproject / IR category	Site selection	Land ownership	Cadastre data	Demarcation	Consultations / PIB	Pre-screening report	Land acquired (ha)	DED submitted to GDR	Consultation	DMS/SES & RCS	DRP / DDR	Comments
Kampong Cham	Landfill / B	Yes	State	Yes			Nov.21	n/a	DED on-going, expected in Feb.22	Jan.22	Feb.22	Mar.22	COI for access road location to be finalized as preparation for DRP. Impact at SWM site also
	Wastewater / B	Yes	State	Not available	Yes	Updated PIB submitted Mar.21	Updated version submitted	n/a	Yes, including adjusted COI	Sep 21	Sep-Oct 21	Draft DRP Jan.22	DMS/SES and consultations completed. DRP being prepared by GDR (scope of works chapter provided to GDR)
Kratie	Landfill / B	Yes	State	Yes	Yes	July 2021	Submitted	n/a	Yes, including adjusted COI for access road	Jul-Aug 21	Jul-Aug 21	Final DRP/IRP Jan.22	ADB comments on combined DRP with STR landfill draft being addressed by GDR (scope of works chapter provided to GDR)
	Wastewater / B	Yes	Private	Yes	WWTP site	21.12.2017	Draft	On-going for 10.5 ha (1 AH)	Draft DED submitted in Dec.21	Feb.22	Feb.22	Draft DRP Apr.22	WWTP site preliminary impact screening started. WWTP site acquisition can proceed (one owner)
	Town center / C	TBC	State				Draft	n/a	On-hold, pending WWTP designs				As per design process, no IR impacts will be entertained in the design. IR impact screening of designs will be required
Stueng Treng	Landfill / B	Yes	State	Yes	Yes	July 2021	Submitted	n/a	Yes, including adjusted COI for access road	Jun-Jul 21	Jun-Aug 21	Final DRP/IRP Jan.22	ADB comments on combined DRP with STR landfill draft being addressed by GDR (scope of works chapter provided to GDR)
	Wastewater / B	Yes	Private	Yes	Yes	20.12.2017	Final in Oct.21	Through DRP (3-5 AHs)	DED submitted Nov.21, including adjusted COI	Dec.21	Dec.21	Draft DRP Feb.22	Final COI submitted to GDR in Nov.21, DMS/SES on-going by GDR
	Town center / C	TBC	State				Draft	n/a	On-hold, pending WWTP designs				As per design process, no IR impacts will be entertained in the design. IR impact screening of designs will be required

Table 3.4 Status of IESIA Preparation.

Documents	Submitted to MoE	Approved By MoE:	Comments
IESIA CW06 – Kampong Cham: Wastewater and drainage	Final draft 12 Jan 2021	02 March 2021	
IESIA CW07 – Kratie: Wastewater and drainage	Final draft 19 Feb 2021	06 April 2021	
IESIA CW08 – Stung Treng: Wastewater and drainage	Final draft 25 February 2021	20 May 2021	
IESIA CW03 – Kampong Cham: Solid waste management			MoE did not approve the initially proposed site. In September 2021, PMU/PMC decided on an alternative site. PMU has commissioned an IESIA which is waiting for information from design.
IESIA CW04 – Kratie: Solid waste management	Final draft 11 March 2021	20 May 2021	
IESIA CW05 – Stung Treng: Solid waste management	Final draft 22 June 2021	30 June 2021	

Municipality	Sub-project	Preparing draft ToR and submit to MoE for review	Discussion meeting with MoE and revise the ToR	Approval from MoE for conducting field survey on Physical, Natural and Social Resources	Preparing draft IEIA report	Submit the draft IEIA to MPWT for comments	Revised the first draft IEIA and submit to MoE	MoE conducting field visit	Discussion meeting on the draft	Revised 1st draft base on comments from MoE	Submission 2nd draft for Inter-Ministry meeting	Inter-Ministry meeting on 2nd draft	Prepare final draft based on comments from Inter-Ministry meeting	Minutes preparation for approval report	Document preparation for issuing license
Kampong Cham	Wastewater	June 2020	June 2020	July 2020	June-Aug 2020	11 Aug 2020	14 Aug 2020	01 Sept 2020	15 Sept 2020	Sept 2020	23 Oct 2020	01 Dec 2020	12 Jan 2021	Feb 2021	02-Mar-2021
	Landfill	April 2020								Oct 2021 New site					
Kratie	Wastewater	June 2020	July 2020	July 2020	July-Sept 2020	11 Sept 2020	15 Sept 2020	22 Sept 2020	06 Oct 2020	Oct 2020	13 Nov 2020	12 Jan 2021	19 Feb 2021	29 Mar 2021	06-Apr-2021
	Landfill	April 2020	June 2020	June 2020	July-Aug 2020	14 Aug 20	21 Aug 2020	02 Sept 2020	21 Sept 2020	Nov-Dec 2020	Feb 2021	23 Feb 2021	Mar 2021		20-May-2021
	Town Centre														
Stung Treng	Wastewater	June 2020	July 2020	July 2020	July-Sept 2020	23 Sept 2020	29 Sept 2020	8-9 Oct 2020	22 Oct 2020	Oct 2020	19 Nov 2020	11 Jan 2021	25 Feb 2021	April 2021	20-May-2021
	Landfill	April 2020	June 2020	June 2020	July-Aug 2020	14 Aug 2020	24 Aug 2020	03 Sept 20	21 Sept 20	is revising	Feb 2021	19 April 21	June 21	22 June 21	30-June-2021
	Town Centre														

Table 3.5 Status of IEEs and EMPs.

	Subproject	Site agreed	Land ownership	MOE approval	IEE Update			EMP Update			Notes
					Draft	Submitted to PMU	Submitted to ADB	Draft	Submitted to PMU	Submitted to ADB	
Kampong Cham	Landfill	Yes	State	In progress							The initially proposed site was not approved by MoE. PMU/PMC decided on an alternative site in September 2021
	WWTP	Yes	State	Yes	Jul-2020	04-Jun-2021	07-Jun-2021	Jul-2020	04-Jun-2021	07-Jun-2021	IEE/EMP available on https://www.adb.org/projects/50099-002/main#project-documents
Kratie	Landfill	Yes	State	Yes 02-May-19	Mar-2021	13-Jul-2021	13-Jul-2021	Mar-2021	13-Jul-2021	13-Jul-2021	IEE/EMP including ECA of 2 dumpsites cleared by ADB on 14-Jul-2021
	WWTP	Yes	Private	Yes	Dec-2021			Dec-2021			IEE/EMP: Draft prepared
	Town centre	TBC	State								
Stung Treng	Landfill	Yes	State	Yes 02-May-19	Dec-2020	16-Sep-2021	17-Sep-2021	Dec-2020	16-Sep-2021	17-Sep-2021	Final IEE/EMP and dumpsite ECA cleared by ADB on 17-Sep-2021
	WWTP	Yes	Private	20-May-2021		05-Oct-2021	05-Oct-2021	05-Oct-2021	05-Oct-2021	05-Oct-2021	IEE/EMP cleared by ADB on 23-Oct-2021
	Town centre	TBC	State								

3.4 Gender Action Plan

- 16 The CTDP4 Project is classified as Effective Gender Mainstreaming (EGM) and Gender Action Plan monitoring tables are shown in Annex F. Identified gender issues include insufficient solid waste collection services, limited sanitation and sewerage systems resulting in poor environmental sanitation, decrease in local business and income during flooding, limited participation in decision-making and representation in the water and sanitation sector of female staff; and limited opportunities to strengthen and expand job opportunities for women.

4 Implementation Progress

4.1 Project Organisation and Management

- 17 The contract for PMC (Contract No. PMU/MPWT/TS-2&CTP-4/CS01) was signed on 26 June 2019 between the Ministry of Public Works and Transport (MPWT) (The Client) and Ramboll Danmark A/S in Joint Venture with Oriental Consultant Global Co., Ltd. and SCE in association with Tancons (Cambodia) Co., Ltd (The Consultant).
- 18 The PMC was mobilized on 15 July 2019. The kick-off meeting took place at MPWT in Phnom Penh on 17th of July 2019 attended by key stakeholders.
- 19 The Ministry of Public Works and Transport (MPWT) is the Project's executing agency (EA) and will manage the implementation of the Project's outputs through a Project Management Unit (PMU) based in MPWT's main office in Phnom Penh.
- 20 Project Implementation Units (PIUs) have been established in each of the Project towns. These are embedded within the provincial Departments of Public Works and Transport (DPWT) for the different provinces.
- 21 As the available office space available in MPWT is insufficient to accommodate the large consultant team, the PMC have rented an office space on the corner of Street 51 and Street 228.

4.1.1 Contract Variations

- 22 Contract Variation No. 6 was approved during this quarter; VO 7 is under preparation and discussion at the time of preparing this Report. The history and status of contract variations is shown in Table 4.1.

Table 4.1 Contract Variations, Current and Previous Quarters

Period	Variation No.	Key Dates:		No Objection from ADB	Main Items in Variation
		Submitted	Approved by MPWT		
	1		22 Oct 2019	18 Oct 2019	Replacement International TL and National Deputy TL 1
	2		Feb 2020	March 2020	Change of scope – separate sewers, not combined and traditional procurement not D&B in CTDP4, removal of procurement tasks from PMC, change in scope of urban and provincial plan preparation
<i>Previous Quarters</i>	3	29 June 2020	29 June 2020		Change in payment schedule for urban and provincial planning Agreement for PMU to pay sub-contractors for preparation of IEIAs
	4	11 September 2020	11 September 2020		Replacement of National Deputy Team Leader 2
	5	May 2021		29 June 2021	Reallocation to home input due to Covid19 restrictions, Additional time spent by PMC due to site changes, COI and scope changes, replacement of solid waste engineers (Intl. and Nat.) and Resettlement specialist (Nat).
	6	June 2021	1 July 2021	30 July 2021	Replacement of International TL

This Quarter 4:	7	December 2021	In progress	Old Landfills Remediation (TS2 nos.3 and CTDP4 nos. 3) Additional input and reallocation to home inputs experts Additional Supervision support Serei Saophoan Landfill additional surveys Kampong Cham Controlled landfill additional inputs; Master Plans LUMP and PSP translations.
--------------------	---	------------------	-------------	--

4.2 Progress Monitoring

- 23 A Project Performance Monitoring System (PPMS) is being used to record the progress of the project. Summaries of progress by sub-project are shown in Annex C.
- 24 The current status of all project activities is summarised in Table 4.2

Table 4.2 Status of Sub-projects and other Project Activities.

CIVIL WORKS AND EQUIPMENT.

Contract No.	Town	Site Approval	Topo Survey	Geo Survey	Status	Action Required	Action By
CTDP4							
CW06 Wastewater WWTP, sewers, drains	Kampong Cham	▪ MOE site approval not required	▪ Yes	▪ Yes	▪ On-going bidding process ▪ DMS completed	▪ Follow up and assist for DRP preparation report	▪ PMC, GDR
CW07 Wastewater WWTP, sewers, drains	Kratie	▪ MOE site approval not required	▪ Yes	▪ Yes	▪ Draft DED submitted ▪ COI preparing	▪ Need to response to ADB and PMU comment ▪ COI to be prepared and submitted	▪ PMC
CW08 Wastewater WWTP, sewers, drains	Stung Treng	▪ MOE site approval not required	▪ Yes	▪ Yes	▪ DED completed ▪ Invitation for bidding	▪ Need to response clarification of bidder	▪ PMC ▪ PMU
CW03 Landfill	Kampong Cham	▪ Not for new site	▪ Completed	▪ Completed	▪ DED on-going	▪ Concept layout drawing to be presented	▪ PMC
CW04 Landfill	Kratie	▪ MOE 2.5.19	▪ Yes	▪ Yes	▪ Evaluation Bids finished	▪ Kick-off meeting ▪ Mobilization Staff for inspection	▪ PMC ▪ Contractor
CW05 Landfill	Stung Treng	▪ MOE 2.5.19	▪ Yes	▪ Yes	▪ Evaluation Bids finished	▪ Kick-off meeting ▪ Mobilization Staff for inspection	▪ PMC ▪ Contractor
CW01 Town centre improvements	Kratie	▪ MOE approval not needed	▪ Within area surveyed already	▪ N/A	▪ Revised proposals received from PIU ▪ Footpath proposals to be reviewed/revised	▪ To be reviewed and cost estimated	▪ PIU
CW02 Town centre improvements	Stung Treng	▪ MOE approval not needed	▪ Within area surveyed already	▪ N/A	▪ Revised proposals received from PIU – 2 urban parks agreed, riverbank park and bank protection beyond scope	▪ Additional schemes needed	▪ PIU

Contract No.	Town	Site Approval	Topo Survey	Geo Survey	Status	Action Required	Action By
G02 SWM equipment	Kampong Cham, Kratie Stung Treng	▪ N.a.	▪ N.a.	▪ N.a.	▪ Not started	▪ Preparation of Equipment report	▪ PMC

PROVINCIAL PLANS AND LAND USE MASTER PLANS

Output/Activity	Location/Coverage	Status	Next Steps	Action By
CTDP4				
Provincial spatial plan	Kampong Cham	<ul style="list-style-type: none"> ▪ Workshop on November 30, 2020 ▪ Vision Seminar held on December 25, 2020 ▪ Final Workshop on Draft PSP on December 1, 2021 	<ul style="list-style-type: none"> ▪ Draft PSP (English) submission 	<ul style="list-style-type: none"> ▪ PMC
Provincial spatial plan	Kratie	<ul style="list-style-type: none"> ▪ Workshop on January 18, 2021 ▪ Situation Report submitted ▪ Vision Seminar held on July 15, 2021 	<ul style="list-style-type: none"> ▪ Second workshop (February 2022) ▪ Draft PSP (English) submission 	<ul style="list-style-type: none"> ▪ PMC
Provincial spatial plan	Stung Treng	<ul style="list-style-type: none"> ▪ Workshop on January 20, 2021 ▪ Situation Report submitted ▪ Vision Seminar on July 15, 2021 	<ul style="list-style-type: none"> ▪ Second workshop (February 2022) ▪ Draft PSP (English) submission 	<ul style="list-style-type: none"> ▪ PMC
LUMP Review	Kampong Cham	<ul style="list-style-type: none"> ▪ Review submitted 	<ul style="list-style-type: none"> ▪ 	<ul style="list-style-type: none"> ▪
LUMP Review	Kratie	<ul style="list-style-type: none"> ▪ Review submitted 	<ul style="list-style-type: none"> ▪ 	<ul style="list-style-type: none"> ▪

OTHER ACTIVITIES

Item	Status	Action Required	Action By
IEC	<ul style="list-style-type: none"> ▪ First request for proposals rejected by NGOs due to much too low available budget: no responses. Second round with no budget limit: 4 NGOs submitted a proposal 17 December 2021. January 2022 these proposals are under evaluation. 	<ul style="list-style-type: none"> ▪ Selection of NGO, approval and contracting expected February 2022. 	<ul style="list-style-type: none"> ▪ PMC and PMU
Capacity Building	<ul style="list-style-type: none"> ▪ Training needs assessment done ▪ First training planned in February/ March 2022 – depending on Covid-19 situation 	<ul style="list-style-type: none"> ▪ Training planned. 	<ul style="list-style-type: none"> ▪ PMC

4.3 Implementation Activities

4.3.1 Consultant Team

25 The PMC team members mobilised during this quarter are shown in Table 4.3.

Table 4.3 International and National Consultants Active during the Quarter

Position	Name
<i>International</i>	
Team Leader	René van Doorn
Deputy Team Leader	Lars Orio
Wastewater / Civil Engineer	Michael Odgaard Nielsen
Social Safeguards and Resettlement Specialist	Teemu Jantunen
Finance and Institutional Specialist	Alice Thauvin
Urban Development Specialist	Howard Trett
Urban and Regional Planner	Hisako Kobayashi
Urban and Regional Economist	Manabu Fujikawa
Urban Planner	Tomoki Fukunaga
Solid Waste Expert	Steven Long
Social and Gender Expert	Alexander Timmermann
Senior Design Engineer	Dhanesh Prasad
Environmental Safeguards Expert	Peter Gammelgaard Jensen
<i>National</i>	
National Deputy Team Leader	Ho Ratha
National Deputy Team Leader	Ly Nara
Environmental Safeguard Specialist	Yim Chamnan
Sanitation Engineer	Va Vandith
Sanitation Engineer	Sarit Chung
Social Safeguards & Resettlement Specialist CTDP4	Chan Narith
Solid Waste Engineer	Yin Somean
Urban Planner	Seng Touch
Urban Planner	Sim Bovisal
Land Use Management Specialist	David Chandavin
CAD Operator	Lon Saoveasna
CAD Operator	Phe Samnang

(Not including engineering design teams REC and Archineer)

4.3.2 General Activities

26 Activities during this quarter have included meetings with stakeholders, topographical and geotechnical surveys, initial and Detailed Design works and Preparing Bidding documents.

4.3.3 Activities by Output

27 The key activities undertaken during this quarter are summarised in Table 4.4 below.

Table 4.4 Key Implementation Activities by Output During the Reporting Period

Outputs	Summary of Activities Undertaken
Output 1: Urban Environmental Infrastructure Improved	<i>Kampong Cham – Wastewater:</i>
	<ul style="list-style-type: none"> Invitations for Bid published and contractor's bids received. Evaluation ongoing PMU
	<i>Kampong Cham – Solid Waste Management:</i>
	<ul style="list-style-type: none"> Site soil investigations, groundwater level monitoring and geotechnical survey of new third site completed in December 2021.
	<i>Kratie – Wastewater:</i>
	<ul style="list-style-type: none"> Draft DED design and draft tender documents submitted 10 December 2021.
	<i>Kratie – Solid Waste Management:</i>
	<ul style="list-style-type: none"> Invitations for Bid published and contractor's bids received. Evaluation ongoing PMU
	<i>Kratie – Town Centre Improvements:</i>
	<ul style="list-style-type: none"> Potential projects will be reviewed.
Output 2: Institutional effectiveness, and policy and planning environment Urban Environmental Infrastructure Improved	<i>Stung Treng – Wastewater and Drainage</i>
	<ul style="list-style-type: none"> Invitations for Bidding published Responses to Contractor's request for clarifications submitted
	<i>Stung Treng – Solid Waste Management:</i>
	<ul style="list-style-type: none"> Invitations for Bid published and contractor's bids received. Evaluation ongoing PMU
	<i>Stung Treng – Town Centre Improvements:</i>
	<ul style="list-style-type: none"> Potential projects will be reviewed.
	<i>Kampong Cham, Kratie, Stung Treng</i>
	<ul style="list-style-type: none"> Formulation of development strategies and action plans presented in Vision Seminar in Kratie and Stung Treng province; Second workshops planned Feb 2022. Draft Provincial Spatial Plans (PSP) nearly completed (Feb 2022) for Kampong Cham, Kratie and Stung Treng provinces.

4.3.4 Meetings

28 The key meetings held during this quarter are listed in Annex B.

4.4 Project Costs

29 Estimates of sub-project costs are shown in Table 4.5. The cost estimates have been updated where the DED engineers have preliminary, draft estimates or based on the BOQs.

Table 4.5 Current Estimates of Sub-project Costs

Contract No.	Sub-Project	Estimate US\$m	Source of Estimate	Procurement Plan (14 Aug 2020)	Difference
CW01	Kratie town enhancements	0.75	Procurement Plan	0.75	0.0
CW02	Stung Treng town enhancements	0.75	Procurement Plan	0.75	0.0
CW03	Kampong Cham landfill	6.25	estimate based on average. DED Designs in progress.	6.18	0.07
CW04	Kratie landfill	6.28	DED engineer's estimate based on BOQ	5.57	0.71
CW05	Stung Treng landfill	6.24	DED engineer's estimate based on BOQ	5.92	0.32
CW06	Kampong Cham wastewater	30.59	DED engineer's estimate based on BOQ	17.26	13.33

CW07	Kratie wastewater (Reduced Phase 1)	23.50	DED engineer's preliminary estimate on draft DED	14.14	9.36
CW08	Stung Treng wastewater (Reduced Phase 1)	21.37	DED engineer's Final Cost Estimate	14.45	6.92
G02	Kampong Cham, Kratie, Stung Treng Landfill equipment	1.35	Procurement Plan	1.35	0.0
Total for civil works and equipment		\$97.08		\$66.37	+\$30.71

- 30 As can be seen in Table 4.5 above, the current total estimate for civil works and equipment is around **\$30.71m above** the amount in the latest procurement plan.
- 31 In Stung Treng and Kratie town, the cost estimates are based for wastewater subprojects for Reduced Phase 1 areas compared to the PPTA Phase 1 areas. This was decided by PMU to lower the investment costs.
- 32 Kampong Cham wastewater cost estimate is based on the cost estimate submitted final DED. This is the largest town in CTDP4.
- 33 Kampong Cham landfill: a new location(3rd) has been allocated. Soil investigations and topographical surveys has been executed December 2021. A first site assessment has been executed related to Environmental and Social Resettlement issues. So far, no major concerns were noticed.
- 34 Stung Treng sewerage layout is designed with a reduced area Phase 1 that covers the main central parts of the urban area. This reduction initiated the cost estimate down to around \$21m.
- 35 Kratie sewerage layout will be designed with a reduced area Phase 1 that covers the main central parts of the urban area. It is expected this reduction will bring the cost estimate down to around \$23.5m.

4.5 Procurement

4.5.1 Procurement Plan

- 36 The Procurement Plan for CTDP4 is shown in Annex G.

4.5.2 Procurement of Civil Works and Equipment

- 37 Invitations for Bid were published for Kratie Landfill (16 July 2021), Kampong Cham Wastewater (22 July 2021) and Stung Treng Landfill (22 September 2021). No contract has been signed in this Q4-2021 period. The status of procurement of civil works and equipment contracts is summarised in Table 4.6.

Table 4.6 Status of Civil Works and Equipment Contracts.

Package No.	Package Name	Estimated Value (\$m)	DED Cost estimate (USD)	Contract Signed (USD)	Method of Procurement	Type of Contract	Review	Submission of Proposed Bidding Documents to ADB	ADB Approval of Bid Docs	Invitation for Bid/ RFP Issued	Bid Opening / Receipt of Proposals	BER to ADB	ADB Approval of BER/ Issuance of NOL	Contract Signing
CW03	Kampong Cham Solid Waste Management	6.18			ICB	Works	Prior							
CW04	Kratie Solid Waste Management	5.57	6,282,937.00		ICB	Works	Prior	11-Jul-21	14-Jul-21	16-Jul-21	01-Sep-21	16-Sep-21	19-Oct-21	
CW05	Stung Treng Solid Waste Management	5.92	6,235,313.00		ICB	Works	Prior	31-May-21	02-Jun-21	22-Sep-21	03-Nov-21	10-Dec-21	11-Jan-22	
CW06	Kampong Cham Wastewater and Drainage	17.26	30,587,838.00		ICB	Works	Prior	02-Jun-21	20-Jul-21	22-Jul-21	09-Sep-21	27-Oct-21		
CW07	Kratie Wastewater and Drainage	14.14			ICB	Works	Prior							
CW08	Stung Treng Wastewater and Drainage	14.45	21,371,606.62		ICB	Works	Prior							
G02	SW Collection Vehicles and Landfill Equipment	1.35			NCB	Goods	Prior							
CW01	Town Center Environmental Enhancement for Kratie	0.75			NCB	Works	Prior							
CW02	Town Center Environmental Enhancement for Stung Treng	0.75			NCB	Works	Post							
CS02	ICT for Public Management	1.00			QCBS	Consultant	Prior							

4.6 Provincial Planning and Municipality Planning

4.6.1 General Activities

- 38 Activities during the quarter include the formulation of development strategies and action plan for Provincial Spatial Plans (PSPs), the visioning seminar, and meetings with relevant departments and organizations.

4.6.2 Activities by Output

- 39 The key planning activities undertaken during this quarter are summarised in Table 4.7 below.

Table 4.7 Key Implementation Activities by Output

Outputs	Summary of Activities Undertaken
Output 1: Formulation of Provincial Spatial Plan	<i>Kampong Cham:</i>
	<ul style="list-style-type: none"> ▪ Supplemental data and information have been collected to propose strategies and action plan ▪ The socio-economic framework was prepared. ▪ The formulation of development strategies and action plan is in progress. ▪ The spatial structure of the province in 2040 is under preparation.
	<i>Kratie:</i>
	<ul style="list-style-type: none"> ▪ Data and information related to population, economy, infrastructure, physical characteristics, land use, protected areas, disaster prone areas, on-going projects, etc. have been collected and analyzed. ▪ The formulation of development strategies and action plan is in progress. ▪ The spatial structure of the province in 2040 is under preparation.
	<i>Stung Treng:</i>
	<ul style="list-style-type: none"> ▪ Data and information related to population, economy, infrastructure, physical characteristics, land use, protected areas, disaster prone areas, on-going projects, etc. have been collected and analyzed. ▪ The formulation of development strategies and action plan is in progress. ▪ The spatial structure of the province in 2040 is under preparation.

5 Compliance with Covenants

- 40 The status of covenant compliance is shown in the tables in Annex H.

6 Project Implementation Issues.

6.1 Issues Affecting Project Implementation Progress

6.1.1 Covid 19

- 41 The Covid-19 pandemic has a significant impact on project operations and progress.
- 42 **Recommended Actions:** The Covid situation is being constantly monitored in Cambodia and overseas. Discussions will continue to be held with PMU in order to agree a safe and pragmatic approach to project progress.

6.1.2 Kampong Cham Landfill

- 43 PMC has finished the topographical -, soil surveys and geotechnical surveys. At the moment the survey reports are studied.

44 **Recommended Actions:** Preparation for detailed designs including environmental and resettlement aspects investigated.

45 The initial planning is to submit the draft DED end of February 2022.

6.1.3 Stung Treng Landfill

46 Bids have been received before the deadline of 4 November 2021. Evaluation of the bids is in progress.

47 **Recommended Actions:** It is expected the contractor's Contract will be signed in Q1 – 2022 and commencement of the Works can start after signing.

6.1.4 Kratie Landfill

48 Bids have been received before the deadline of 1st September 2021. Evaluation of the bids is in progress.

49 **Recommended Actions:** It is expected the contractor's Contract will be signed in Q1 – 2022 and commencement of the Works can start after signing.

6.1.5 Kampong Cham Wastewater.

50 Bids have been received with deadline submission 27 October 2021. Evaluation of the bids is in progress.

51 **Recommended Actions:** Contracting of the contractor is expected in Quarter 1 or Q2 - 2022.

6.1.6 Stung Treng Wastewater.

52 The Final DED Bid documents have been submitted to PMU and published for bidding. PMC has submitted responses to the Contractor's requests for clarifications on the tender documents.

53 **Recommended Actions:** Contracting of the contractor is expected in Quarter Q2 - 2022.

6.1.7 Kratie Wastewater

54 The draft DED of Kratie wastewater and drainage subproject was submitted 10 December 2021.

55 The difficulties of the wastewater treatment plant are challenging due to the location in the flood plain of the Natural Lake south-east of Kratie town. It is anticipated the total construction of Kratie wastewater subproject will take 5 years total.

56 The WWTP site and some parts of the access road is in private ownership. PMU and GDR are both acquainted with this issue.

57 The preliminary cost estimate for the sewerage scheme is around \$23.5m, including construction of five stormwater-return-valves to improve runoff drainage rain and stormwater from the city centre to the lake.

58 The Report of Revised Kratie Drainage and Stormwater subproject was discussed with PMU, other Ministries and the local Authorities in December 2021.

59 **Recommended Actions:** A period of contract time overstay for this sub-project is projected due to required setting of the land filling of 6.00 – 8.00m height of the whole WWTP area.

60 For the soil filling of the WWTP site, an advanced work contract could be considered.

6.1.8 Kratie Town Centre Enhancements

61 This contract package is intended for enhancements that would not involve land and property impacts and compensation.

62 **Recommended Actions:** It is proposed to revisit the options for this contract once the wastewater DED has been completed and agreed. This is in order to identify possible overlaps and avoid works and disruptions occurring twice in the same locations.

6.1.9 Stung Treng Town Centre Enhancements

63 The PIU submitted two schemes adjacent to the Sekong bridge involving small urban parks. These are acceptable. An additional scheme is expected in Q1-2022.

64 **Recommended Actions:** It is proposed to revisit one of the options for this contract once the wastewater DED has been completed and agreed. This is in order to identify possible overlaps and avoid works and disruptions occurring twice in the same locations.

6.2 Other Issues

6.2.1 IESIAs

65 PMU directly recruited and contracted Cambodian consultants to undertake the preparation of the required IESIAs. PMC is only coordinating the activities of the IESIA consultant.

66 During Q4 2021, the IESIA consultant was preparing the IESIA for the new landfill site in Kampong Cham.

7 Work Plan

67 The summary schedule is shown in Annex D.

68 The major activities planned for the next quarter are shown in Table 7.1 below.

Table 7.1 Key Activities Planned for Next Quarter

Civil Works and Equipment	Activities
Kampong Cham Wastewater	<ul style="list-style-type: none"> ▪ Contracting Contractor for works
Kratie Wastewater	<ul style="list-style-type: none"> ▪ Final DED following receipt of comments ▪ COI preparation and submission
Stung Treng Wastewater	<ul style="list-style-type: none"> ▪ Evaluation of Contractor 's Bids for Works
Kampong Cham Landfill	<ul style="list-style-type: none"> ▪ Preparation of Draft DED and Bid documents
Kratie Landfill	<ul style="list-style-type: none"> ▪ Contracting Contractor for works and start of Site supervision
Stung Treng Landfill	<ul style="list-style-type: none"> ▪ Contracting Contractor for works and start of Site supervision
Kratie Town Enhancements	<ul style="list-style-type: none"> ▪ Review and agreement on sub-project components
Stung Treng Town Enhancements	<ul style="list-style-type: none"> ▪ Review and agreement on sub-project components
Kampong Cham, Kratie, Stung Treng SWM Equipment	<ul style="list-style-type: none"> ▪ Assessment and discussions on equipment ▪ Agreement with PIUs and PMU and preparation of equipment specs for bidding (2022)
Institutional Effectiveness	
Semiautonomous Urban Service Units	<ul style="list-style-type: none"> ▪ Policy review ▪ Institutional assessment ▪ Financial assessment ▪ Development of organisational schemes
Urban Development Strategies and Master Plans	<ul style="list-style-type: none"> ▪ Completion and submission of final PSP for Kampong Cham ▪ Completion and submission of final PSP for Kratie ▪ Completion and submission of final PSP for Stung Treng
Training Government Staff	<ul style="list-style-type: none"> ▪ Delivery of initial phase of training programme

Annex A: Design and Monitoring Framework

CTDP4 Design and Monitoring Framework

Impact the Project is aligned with sustainable, inclusive, equitable, and resilient growth achieved (National Strategic Development Plan, 2014–2018) ^a			
Results Chain	Performance Indicators with Targets and Baselines	Data Sources and Reporting	Risks
Outcome Urban services for enhancing regional economic connectivity in participating towns improved	By 2026 a. 31% of the town population in Kampong Cham, Kratie, and Stung Treng (41,400 residents) serviced by new wastewater collection and treatment facilities (2017 baseline: 0 resident) b. 90% of the town population in Kampong Cham, Kratie, and Stung Treng (120,400 residents) residents served by improved solid waste management (2017 baseline: 48,000 residents) c. Incidence of flood and/or waterlogging reduced by 80% in the project service area (2017 baseline: six flood events per year in Kampong Cham, Kratie, and Stung Treng)	a–c. Annual reports by DPWTs and MPWT; project completion report	Lack of financial sustainability caused by limited cost recovery and/or low willingness of households to connect to sewerage network or pay for services. Poor O&M of project infrastructure given limited local capacity.
Outputs 1. Urban environmental infrastructure improved	By 2024 1a. Three new lagoon-based wastewater treatment plants with 13,750 m ³ /day capacity constructed (2017 baseline: 0) 1b. At least 420 km combined trunk and wastewater collection pipeline constructed (2017 baseline: 0) 1c. At least 9,000 households and commercial buildings connected to the wastewater treatment system (including 1,500 households headed by women) (2017 baseline: 0) 1d. Three controlled landfills with capacity of 1,624,500 m ³ constructed and operational (2017 baseline: 0) 1e. At least 16,000 m ² of pedestrian walk rehabilitated (2017 baseline: not available) 1f. 30% of staff employed in O&M are women (baseline 2017: 0)	1a–1f. Project progress reports	Construction delays caused by late approval and implementation of land acquisition and/or resettlement.
2. Institutional effectiveness, and policy and planning environment for regional economic connectivity enhanced	2a. Two ICT-based public management systems for improved work productivity and transparency in three provincial governments deployed (2017 baseline: not available)	2a–2c. Project progress reports	

	<p>2b. Provincial five-year development plans with regional cooperation and development strategy approved in Kampong Cham, Kratie, and Stung Treng (2017 baseline: not available)</p> <p>2c. At least 120 government staff (at least 50% women) in the provincial governments increased ICT skills to operate the ICT-based public services (2017 baseline: 0)</p>		
--	--	--	--

Key Activities with Milestones

1. Urban environmental infrastructure improved

- 1.1. Complete the bidding documents for solid waste management component by Q1 2019
 - 1.2. Complete the bidding document for solid waste management goods component by Q1 2020
 - 1.3. Complete the bidding documents for wastewater treatment component by Q3 2019
 - 1.4. Complete the bidding document for the town center enhancement component by Q3 2019
 - 1.5. Complete the engagement of solid waste management contractor(s) by Q4 2020
 - 1.6. Complete the engagement of wastewater treatment contractor(s) by Q1 2020
 - 1.7. Complete the engagement of the town center enhancement contractor(s) by Q1 2020
 - 1.8. Complete the land acquisition and resettlement activities in Kratie by Q1 2020
 - 1.9. Complete the land acquisition and resettlement activities in Stung Treng by Q1 2020
 - 1.10. Complete construction by Q4 2023
2. Institutional effectiveness, and policy and planning environment for regional economic connectivity enhanced
- 2.1. Complete procurement of the ICT consulting service by Q3 2019
 - 2.2. Ensure the completion of the ICT consulting service by Q4 2023

Project Management Activities

Complete the procurement of the project management consulting service by Q1 2019
 Ensure the completion of the project management consulting service by Q2 2024
 Complete environmental management plan key activities, resettlement plan key activities, gender action plan key activities, and communication strategy key activities by Q2 2024

Inputs

Asian Development Bank: \$78.5 million (concessional loan)
 Asian Development Fund Disaster Risk Reduction Fund: \$1.5 million (grant) Republic of Korea e-Asia and Knowledge Partnership Fund: \$0.5 million (grant) Government: \$8.0 million

Assumption for Partner Financing

Not applicable

DPWT = Department of Public Works and Transport, ICT = information and communication technology, km = kilometer, m² = square meter, m³ = cubic meter, m³/day = cubic meter per day, MPWT = Ministry of Public Works and Transport, O&M = operation and maintenance, Q = quarter.

^a Government of Cambodia, Ministry of Planning. 2014. National Strategic Development Plan, 2014–2018. Phnom Penh.

Source: Asian Development Bank

Annex B: List of Key Meetings Held During this Quarter.

Date	
1 October 2021	National DTL, National Social Safeguards and Resettlement Specialist, and Solid Waste Expert to have a site visit and conducted Site Impact Assessment of Kampong Cham landfill. The experts checked existing access road to new landfill and meeting with Chief of Sangkat and Owner of effected house at two pumping stations.
1 October 2021	Sanitation Engineer and PMU's CTDP4 Project Manager to visit affected households' owners (AHs) at Kampong Cham subprojects
4 October 2021	International DTL to have site visit at Stung Treng landfill and WWTP
8 October 2021	International DTL to have site visit at Kratie landfill and WWTP
13 October 2021	Management Meeting PMC, PMU, and MEF through video conference. Discussions of: Contract management, communication channel, Civil work progress Stung Saen landfill, Battambang landfill progress, Stung Treng landfill bidding, Kampong Cham wastewater subproject.
28 October 2021	PMC to have a presentation and discussion through video conference with PMU and PIU of Kratie on the Revised Kratie Stormwater Drainage Assessment for Kratie Wastewater and Drainage Sub-project
30 November 2021	Urban Planning Team to travel and have a venue check for Provincial Spatial Plan (PSP) and Land Use Master Plan (LUMP) Workshop for Kampong Cham which is taking place the next day
1 December 2021	Provincial Spatial Plan (PSP) and Land Use Master Plan (LUMP) Workshop for Kampong Cham
3 December 2021	National Solid Waste Engineer to have site visit in order to assist the Geotechnical & Hydrogeological team and prepared site survey report for Kampong Cham landfill
16 December 2021	National DTL, National Social Safeguards and Resettlement Specialist and PMU's CTDP4 Project Manager to conduct the public consultation meeting at the Stung Treng city hall with GDR/MEF, PMU/PIU, PMC, city hall, provincial authorities
17-19 December 2021	National Social Safeguards and Resettlement Specialist to conduct Site impact assessment for Stung Treng with GDR and project stakeholder, and facilitated the COI and impact with GDR/DMS team
21 December 2021	National DTL, National Solid Waste Engineer, and National Social Safeguards and Resettlement Specialist to have field visit the new access road to new landfill site at Kampong Cham
24 December 2021	National DTL and Sanitation Engineer to have video conference with PMU, PIU, Governor of Kratie and concerned departments in order to present project information for Kratie Landfill as well as Wastewater and Drainage Subproject.

Annex C: Project Progress by Output.

Activities	Weighting	Plan/Progress (%)	
Overall		Plan cumulative %	75.00%
		Progress to date	46.49%
Output 1: Urban environmental infrastructure improved	85%	Plan cumulative %	76.44%
		Progress to date	47.47%
Wastewater Treatment Plants, Sewerage and Drainage		Plan cumulative %	76.50%
		Progress to date	58.88%
i. Kampong Cham WWTP, Sewerage and Drainage		Plan cumulative %	79.90%
		Progress to date	67.85%
ii. Kratie WWTP, Sewerage and Drainage		Plan cumulative %	74.80%
		Progress to date	48.65%
iii. Stung Treng WWTP, Sewerage and Drainage		Plan cumulative %	74.80%
		Progress to date	60.13%
Wastewater Treatment Plants	20%	Plan cumulative %	76.50%
		Progress to date	61.25%
i. Kampong Cham WWTP	33%	Plan cumulative %	79.90%
		Progress to date	68.85%
Site Selection, Surveys and Approval	10%	Cumulative %	100.00%
Preparation of Resettlement Plan/Due Diligence Review	5%	Cumulative %	99.00%
Preparation/Updating and Approval of IEE & EMP	10%	Cumulative %	99.00%
Preparation and Approval of IEIA	10%	Cumulative %	100.00%
Implementation of Land Acquisition and Resettlement/Site Purchase	3%	Cumulative %	100.00%
Monitoring of Social and Environmental Safeguards	5%	Cumulative %	0.00%
Implementation of GAP and Communication Plan	5%	Cumulative %	0.00%
Preparation of Detailed Engineering Design	15%	Cumulative %	100.00%
Preparation of BOQ and specs	10%	Cumulative %	100.00%
Preparation of Bidding Documents	2%	Cumulative %	100.00%
Bidding process/Award of contract	5%	Cumulative %	80.00%
Construction and Installation	20%	Cumulative %	0.00%

ii. Kratie WWTP	33%	Plan cumulative % Progress to date	74.80% 54.40%
Site Selection, Surveys and Approval	10%	Cumulative %	100.00%
Preparation of Resettlement Plan/Due Diligence Review	5%	Cumulative %	69.00%
Preparation/Updating and Approval of IEE & EMP	10%	Cumulative %	79.00%
Preparation and Approval of IEIA	10%	Cumulative %	99.00%
Implementation of Land Acquisition and Resettlement/Site Purchase	3%	Cumulative %	75.00%
Monitoring of Social and Environmental Safeguards	5%	Cumulative %	0.00%
Implementation of GAP and Communication Plan	5%	Cumulative %	0.00%
Preparation of Detailed Engineering Design	15%	Cumulative %	92.00%
Preparation of BOQ and specs	10%	Cumulative %	65.00%
Preparation of Bidding Documents	2%	Cumulative %	30.00%
Bidding process/Award of contract	5%	Cumulative %	0.00%
Construction and Installation	20%	Cumulative %	0.00%
iii. Stung Treng WWTP	33%	Plan cumulative % Progress to date	74.80% 60.50%
Site Selection, Surveys and Approval	10%	Cumulative %	100.00%
Preparation of Resettlement Plan/Due Diligence Review	5%	Cumulative %	70.00%
Preparation/Updating and Approval of IEE & EMP	10%	Cumulative %	80.00%
Preparation and Approval of IEIA	10%	Cumulative %	99.00%
Implementation of Land Acquisition and Resettlement/Site Purchase	3%	Cumulative %	45.00%
Monitoring of Social and Environmental Safeguards	5%	Cumulative %	0.00%
Implementation of GAP and Communication Plan	5%	Cumulative %	0.00%
Preparation of Detailed Engineering Design	15%	Cumulative %	100.00%
Preparation of BOQ and specs	10%	Cumulative %	100.00%
Preparation of Bidding Documents	2%	Cumulative %	100.00%
Bidding process/Award of contract	5%	Cumulative %	15.00%
Construction and Installation	20%	Cumulative %	0.00%

Sewers, Drainage & Households and Commercial buildings Connections	30%	Plan cumulative % Progress to date	76.50% 56.50%
i. Kampong Cham Sewerage & Drainage	33%	Plan cumulative % Progress to date	79.90% 66.85%
Site Selection, Surveys and Approval	10%	Cumulative %	100.00%
Preparation of Resettlement Plan/Due Diligence Review	5%	Cumulative %	98.00%
Preparation/Updating and Approval of IEE & EMP	10%	Cumulative %	98.00%
Preparation and Approval of IEIA	10%	Cumulative %	100.00%
Implementation of Land Acquisition and Resettlement/Site Purchase	3%	Cumulative %	30.00%
Monitoring of Social and Environmental Safeguards	5%	Cumulative %	0.00%
Implementation of GAP and Communication Plan	5%	Cumulative %	0.00%
Preparation of Detailed Engineering Design	15%	Cumulative %	100.00%
Preparation of BOQ and specs	10%	Cumulative %	100.00%
Preparation of Bidding Documents	2%	Cumulative %	100.00%
Bidding process/Award of contract	5%	Cumulative %	85.00%
Construction and Installation	20%	Cumulative %	0.00%
ii. Kratie Sewerage & Drainage	33%	Plan cumulative % Progress to date	74.80% 42.90%
Site Selection, Surveys and Approval	10%	Cumulative %	96.00%
Preparation of Resettlement Plan/Due Diligence Review	5%	Cumulative %	69.00%
Preparation/Updating and Approval of IEE & EMP	10%	Cumulative %	33.00%
Preparation and Approval of IEIA	10%	Cumulative %	99.00%
Implementation of Land Acquisition and Resettlement/Site Purchase	3%	Cumulative %	20.00%
Monitoring of Social and Environmental Safeguards	5%	Cumulative %	0.00%
Implementation of GAP and Communication Plan	5%	Cumulative %	0.00%
Preparation of Detailed Engineering Design	15%	Cumulative %	91.00%
Preparation of BOQ and specs	10%	Cumulative %	20.00%
Preparation of Bidding Documents	2%	Cumulative %	20.00%
Bidding process/Award of contract	5%	Cumulative %	0.00%
Construction and Installation	20%	Cumulative %	0.00%

iii. Stung Treng Sewerage & Drainage	33%	Plan cumulative % Progress to date	74.80% 59.75%
Site Selection, Surveys and Approval	10%	Cumulative %	100.00%
Preparation of Resettlement Plan/Due Diligence Review	5%	Cumulative %	80.00%
Preparation/Updating and Approval of IEE & EMP	10%	Cumulative %	85.00%
Preparation and Approval of IEIA	10%	Cumulative %	98.00%
Implementation of Land Acquisition and Resettlement/Site Purchase	3%	Cumulative %	15.00%
Monitoring of Social and Environmental Safeguards	5%	Cumulative %	0.00%
Implementation of GAP and Communication Plan	5%	Cumulative %	0.00%
Preparation of Detailed Engineering Design	15%	Cumulative %	100.00%
Preparation of BOQ and specs	10%	Cumulative %	100.00%
Preparation of Bidding Documents	2%	Cumulative %	100.00%
Bidding process/Award of contract	5%	Cumulative %	0.00%
Construction and Installation	20%	Cumulative %	0.00%
Landfills	20%	Plan cumulative % Progress to date	89.93% 51.00%
i. Kampong Cham Landfill	33%	Plan cumulative % Progress to date	91.86% 21.75%
Site Selection, Surveys and Approval	10%	Cumulative %	95.00%
Preparation/Updating and Approval of IEE & EMP	10%	Cumulative %	10.00%
Preparation and Approval of IEIA	10%	Cumulative %	90.00%
Monitoring of Social and Environmental Safeguards	6%	Cumulative %	0.00%
Implementation of GAP and Communication Plan	6%	Cumulative %	0.00%
Preparation of Detailed Engineering Design	15%	Cumulative %	15.00%
Preparation of BOQ and specs	10%	Cumulative %	0.00%
Preparation of Bidding Documents	2%	Cumulative %	0.00%
Bidding process/Award of contract	6%	Cumulative %	0.00%
Construction and Installation	25%	Cumulative %	0.00%

ii. Kratie Landfill	33%	Plan cumulative % Progress to date	87.52% 66.55%
Site Selection, Surveys and Approval	10%	Cumulative %	100.00%
Preparation of Resettlement Plan/Due Diligence Review	5%	Cumulative %	99.00%
Preparation/Updating and Approval of IEE & EMP	10%	Cumulative %	99.00%
Preparation and Approval of IEIA	10%	Cumulative %	99.00%
Monitoring of Social and Environmental Safeguards	6%	Cumulative %	0.00%
Implementation of GAP and Communication Plan	6%	Cumulative %	0.00%
Preparation of Detailed Engineering Design	15%	Cumulative %	100.00%
Preparation of BOQ and specs	10%	Cumulative %	100.00%
Preparation of Bidding Documents	2%	Cumulative %	100.00%
Bidding process/Award of contract	6%	Cumulative %	80.00%
Construction and Installation	20%	Cumulative %	0.00%
iii. Stung Treng Landfill	33%	Plan cumulative % Progress to date	90.40% 64.70%
Site Selection, Surveys and Approval	10%	Cumulative %	100.00%
Preparation of Resettlement Plan/Due Diligence Review	5%	Cumulative %	80.00%
Preparation/Updating and Approval of IEE & EMP	10%	Cumulative %	99.00%
Preparation and Approval of IEIA	10%	Cumulative %	99.00%
Monitoring of Social and Environmental Safeguards	6%	Cumulative %	0.00%
Implementation of GAP and Communication Plan	6%	Cumulative %	0.00%
Preparation of Detailed Engineering Design	15%	Cumulative %	100.00%
Preparation of BOQ and specs	10%	Cumulative %	100.00%
Preparation of Bidding Documents	2%	Cumulative %	100.00%
Bidding process/Award of contract	6%	Cumulative %	65.00%
Construction and Installation	20%	Cumulative %	0.00%

Town Centre Enhancements	10%	Plan cumulative % Progress to date	87.40% 9.50%
i. Kratie Town Centre Enhancements	50%	Plan cumulative % Progress to date	84.70% 11.00%
Site Selection, Surveys and Approval	10%	Cumulative %	80.00%
Preparation of Detailed Design	20%	Cumulative %	15.00%
Preparation and approval of Due Dilligence Report	10%	Cumulative %	0.00%
Monitoring of Social and Environmental Safeguards	5%	Cumulative %	0.00%
Implementation of GAP and Communication Plan	5%	Cumulative %	0.00%
Preparation of Bidding Documents	5%	Cumulative %	0.00%
Bidding process/Award of contract	10%	Cumulative %	0.00%
Construction and Installation	35%	Cumulative %	0.00%
ii. Stung Treng Town Centre Enhancements	50%	Plan cumulative % Progress to date	90.10% 8.00%
Site Selection, Surveys and Approval	10%	Cumulative %	50.00%
Preparation of Detailed Design	20%	Cumulative %	15.00%
Preparation and approval of Due Dilligence Report	10%	Cumulative %	0.00%
Monitoring of Social and Environmental Safeguards	5%	Cumulative %	0.00%
Implementation of GAP and Communication Plan	5%	Cumulative %	0.00%
Preparation of Biding Documents	5%	Cumulative %	0.00%
Bidding process/Award of contract	10%	Cumulative %	0.00%
Construction and Installation	35%	Cumulative %	0.00%

Staff employed in O&M are women	5%	Plan cumulative % Progress to date	0.00% 0.00%
i. Kampong Cham O & M Staff	33%	Plan cumulative % Progress to date	0.00% 0.00%
Staff employed in O&M are women	100%	Cumulative %	0.00%
ii. Kratie O & M Staff	33%	Plan cumulative % Progress to date	0.00% 0.00%
Staff employed in O&M are women	100%	Cumulative %	0.00%
iii. Stung Treng O & M Staff	33%	Plan cumulative % Progress to date	0.00% 0.00%
Staff employed in O&M are women	100%	Cumulative %	0.00%
Output 2: Institutional effectiveness, and policy and planning environment for regional economic connectivity enhancement	15%	Plan cumulative % Progress to date	66.86% 40.92%
i. ICT for Provincial Government	33%	Plan cumulative % Progress to date	35.00% 40.70%
Kampong Cham	33%	Cumulative %	0.00%
Kratie	33%	Cumulative %	0.00%
Stung Treng	33%	Cumulative %	0.00%
ii. Preparation of Provincial Spatial Plans	33%	Plan cumulative % Progress to date	100.00% 98.00%
Kampong Cham	33%	Cumulative %	98.00%
Kratie	33%	Cumulative %	98.00%
Stung Treng	33%	Cumulative %	98.00%
iii. Training	33%	Plan cumulative % Progress to date	66.25% 25.00%
Training Needs Assessment	25%	Cumulative %	100.00%
Training Delivery	75%	Cumulative %	0.00%


Output Progress Compared with Planned Progress*

*Based on work plans prepared in April 2020


Project Progress - Outputs from Project Performance Monitoring System

December 2021


CTDP4

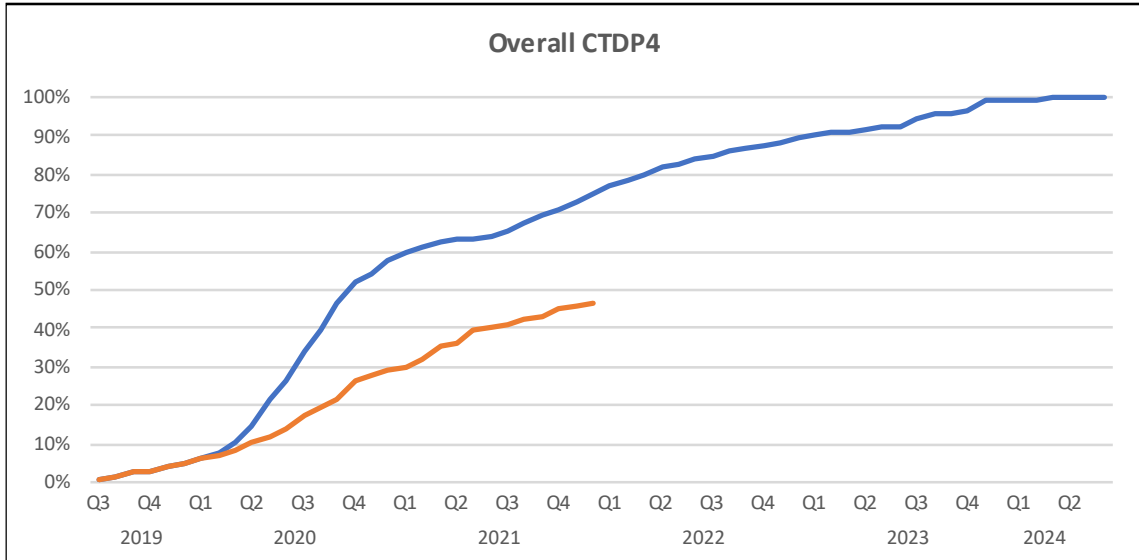


Plan 75.00% **Actual 46.49%**

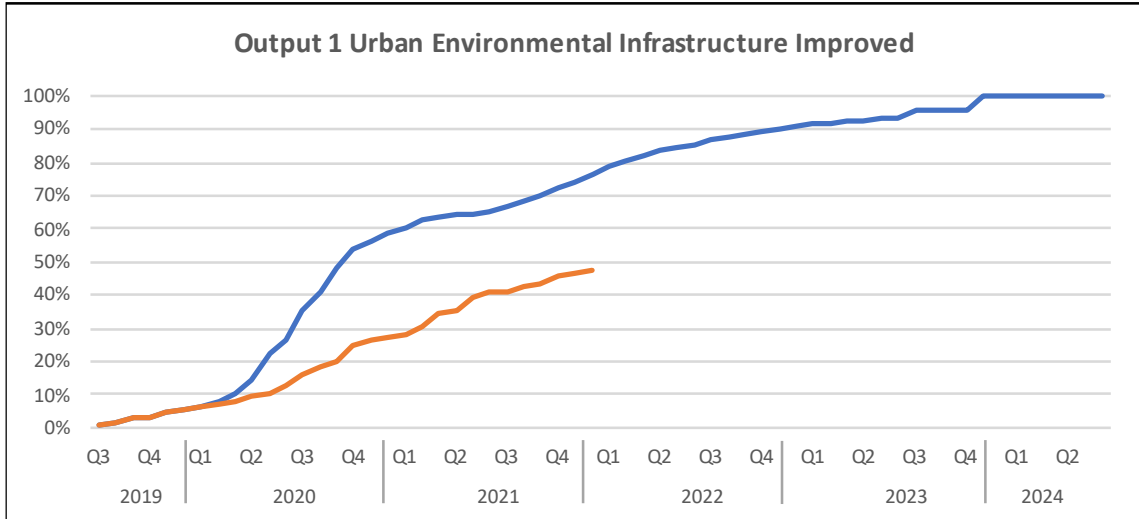


Plan 76.44% **Actual 47.47%**

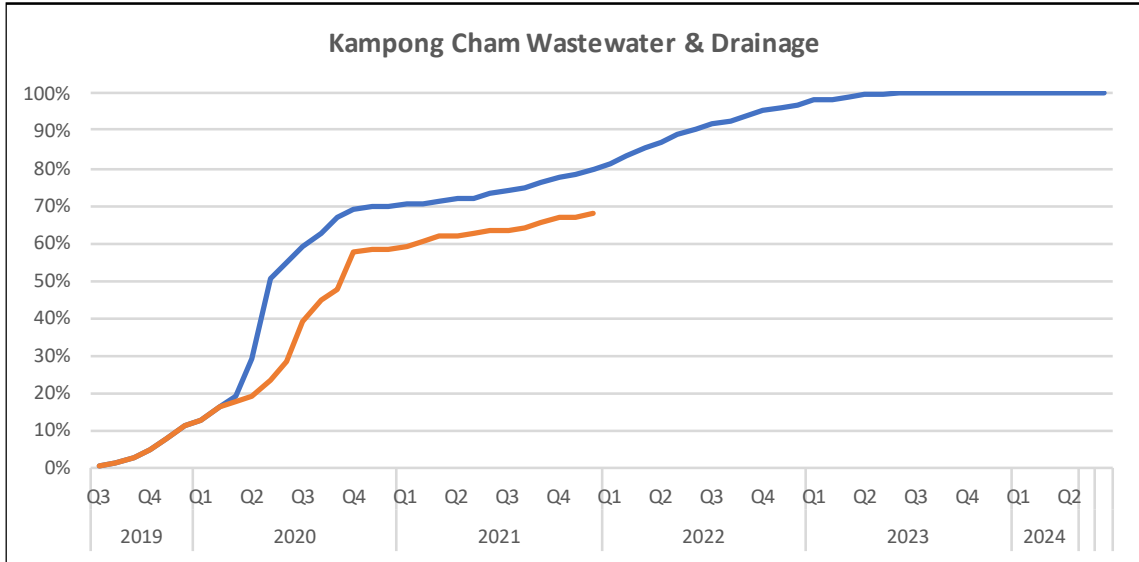


Plan 79.90% **Actual 67.85%**

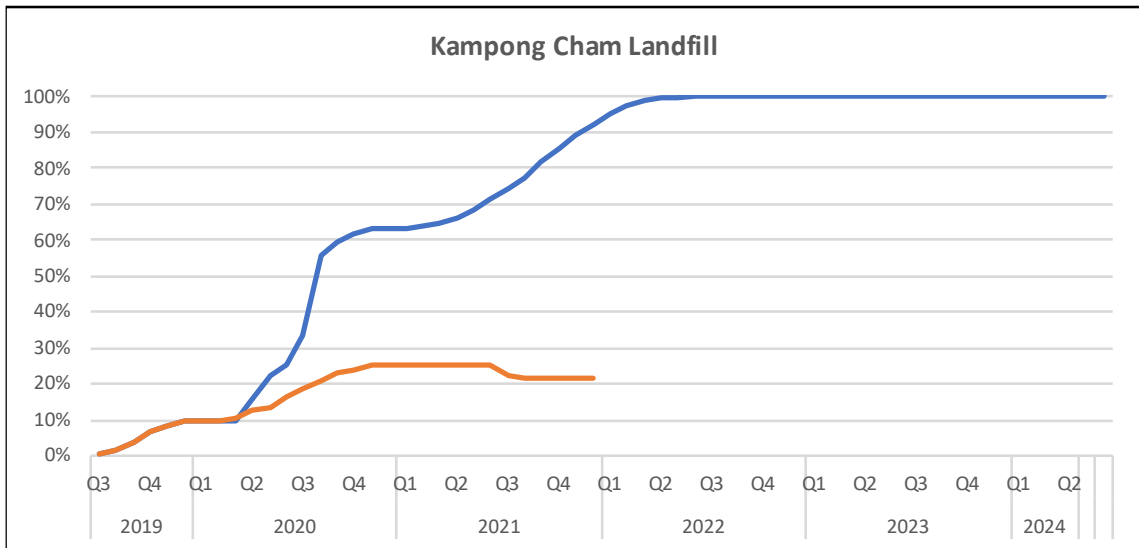


Plan 91.86% **Actual 21.75%**

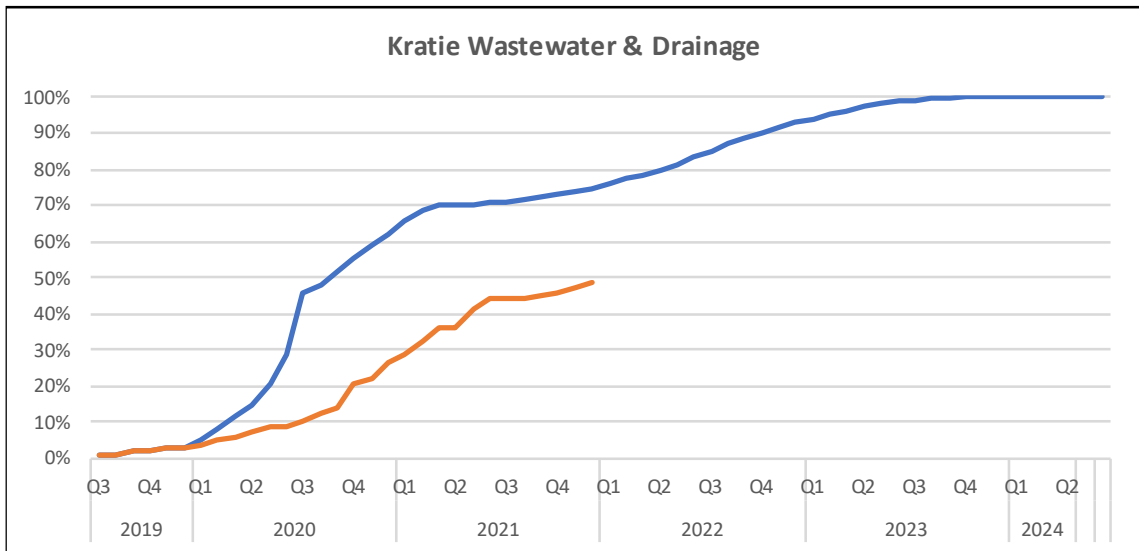


Plan 74.80% **Actual 48.65%**

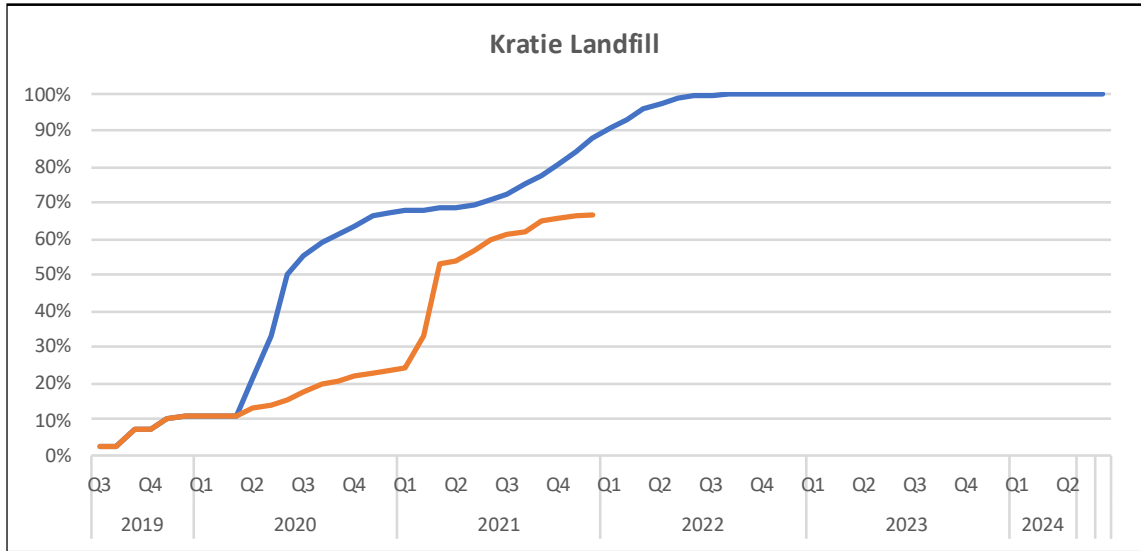


Plan 87.52% **Actual** 66.55%

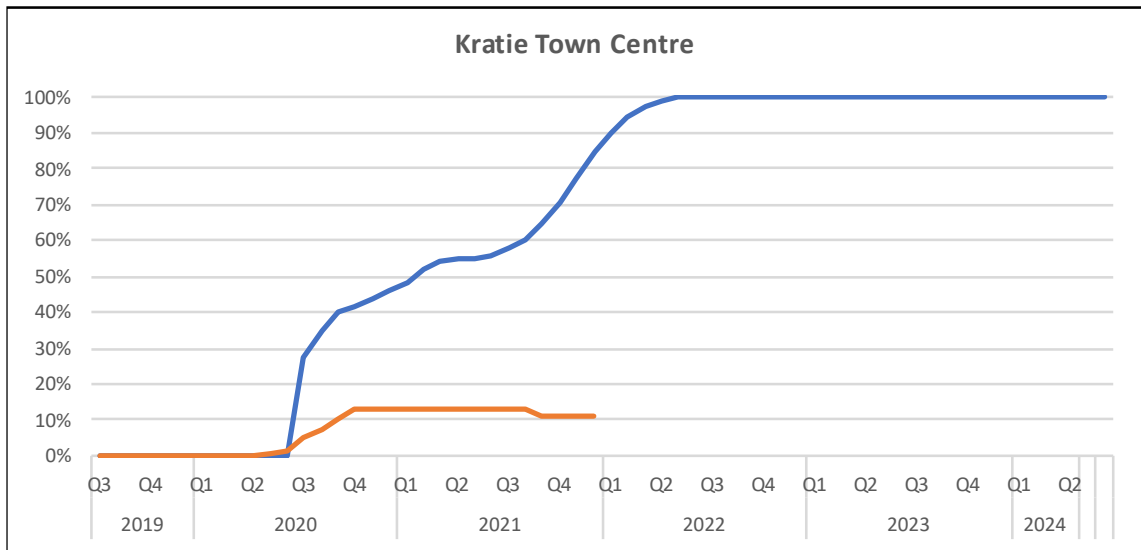


Plan 84.70% **Actual** 11.00%

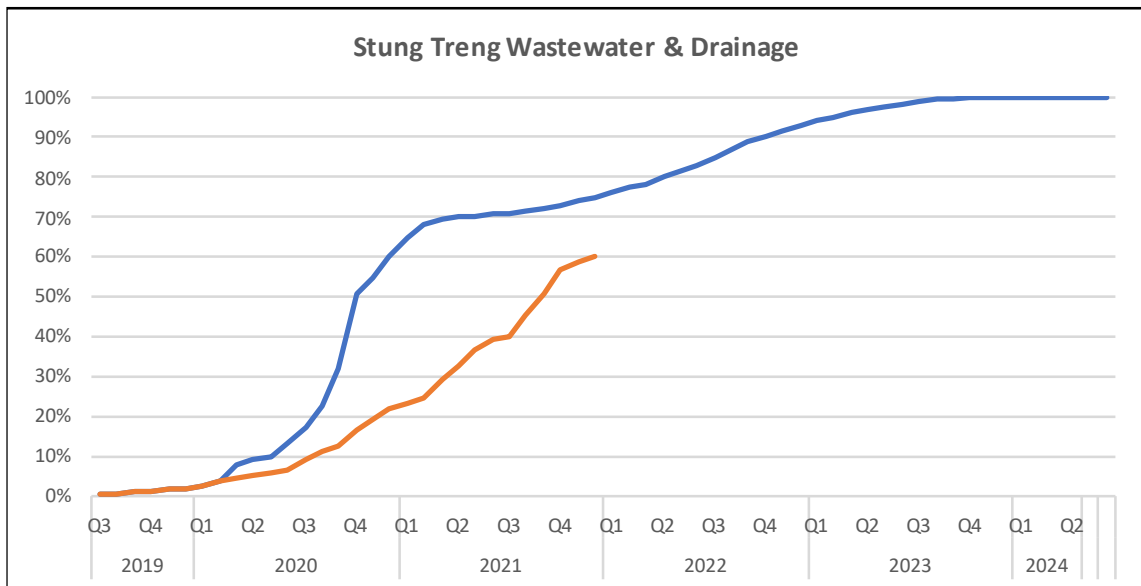


Plan 74.80% **Actual** 60.13%

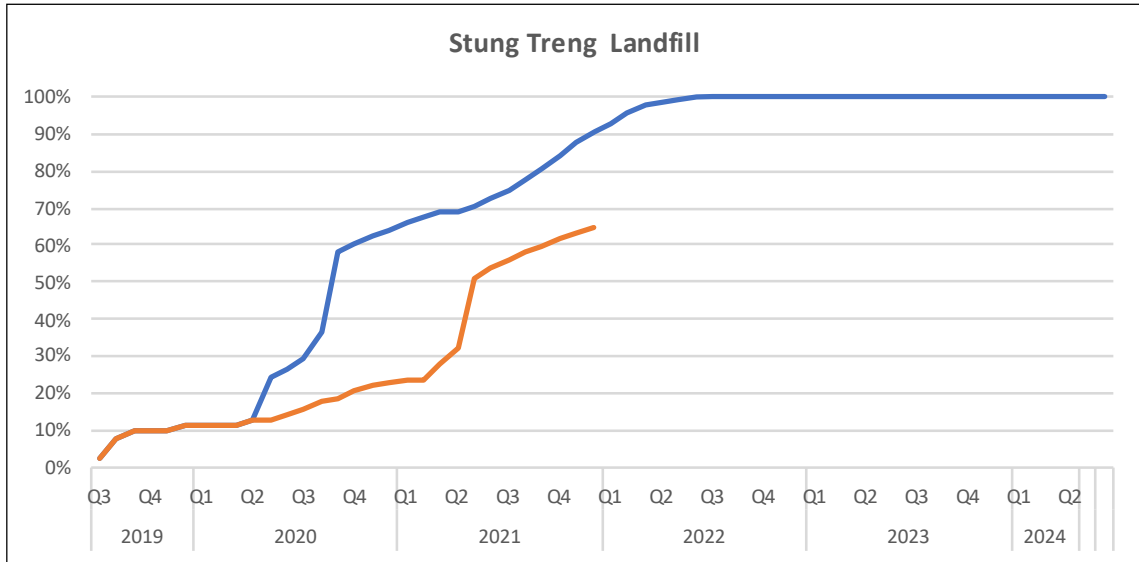

Plan 90.40% **Actual 64.70%**

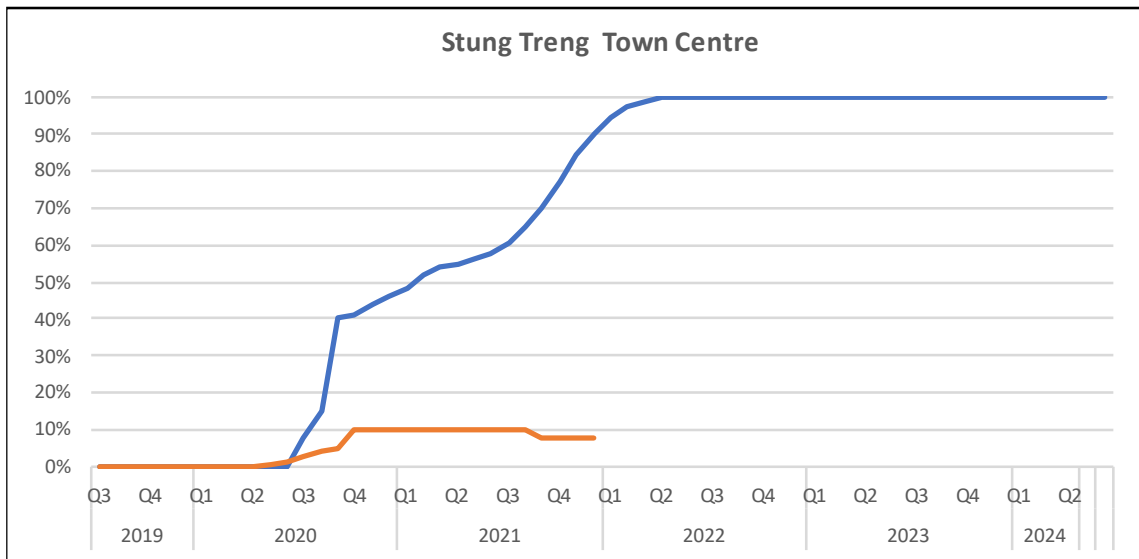

Plan 90.10% **Actual 8.00%**

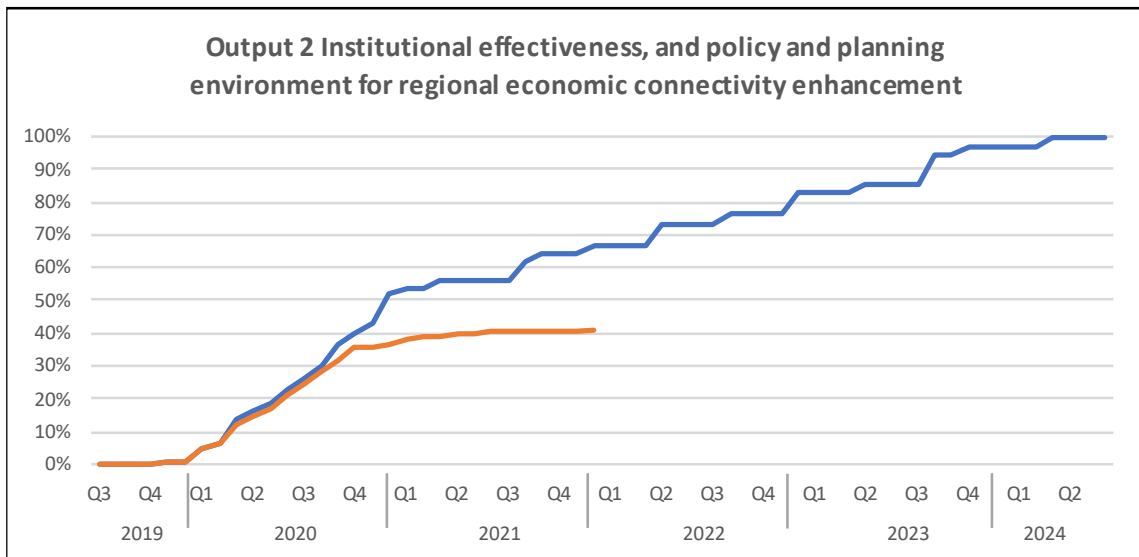

Plan 66.86% **Actual 40.92%**

Annex E: Consultant Inputs (Time-based only)

CTDP-4 Timesheet input								
Quarterly 4 (Oct - Dec 2021)								
Position Code	Name	Position	Contract Amount	Contract Amount after Variation Order No.6	Cumulative to Q3 Sep'21	Q4 Period Oct-Dec'21	Total	Balance
International Expert								
Int.KE-1	Mr. René van Doorn	Team Leader	27.00	19.20	10.75	0.66	11.41	7.79
Int.KE-2	Mr. Lars Orio	International Deputy Team Leader	16.29	16.29	3.41	0.29	3.70	12.59
Int.KE-5	Mr. Peter Peter Gammelgaard Jensen	Environmental Safeguard Specialist	8.00	8.00	4.14	0.60	4.74	3.26
Int.KE-6	Mr. Teemu Jantunen	Social Safeguard and Resettlement Specialist	6.00	6.00	4.20	0.29	4.49	1.51
Int. NKE-7	Ms. Alice Thauvin	Finance and Institutional Specialist	3.00	3.00	0.09	0.03	0.12	2.88
Int. NKE-8	Mr. Richard Pope	Capacity Development and Training Specialist	3.00	3.00	0.54		0.54	2.46
National Expert								
Nat.KE-1.2	Mr. Ly Nara	Deputy Team Leader (CTDP4)	55.00	55.00	23.83	3.00	26.83	28.17
Nat. KE-5.2	Mr. Yim Chamnan	Environment Safeguards Specialist-2	12.00	12.00	4.98	0.84	5.82	6.18
Nat.KE-6.2	Mr. Chan Narith	Social Safeguard and Resettlement Specialist	12.00	12.00	9.41	0.97	10.38	1.62
Nat. KE-7	Mr. Chheav Nak	Institutional Development Specialist	4.00	4.00	0.62		0.62	3.38

Annex F: Gender Action Plan Monitoring.

Gender Action Plan (GAP Activities, Indicators and Targets, Timeframe and Responsibility)	Progress to date (as of December 2021)	Issues, Challenges & Comments
Output 1: Urban environmental infrastructure improved		
Output 1.1: Urban environmental infrastructure in Kampong Cham improved		
<p>Target 1: Wastewater collection connections provided free-of charge to 4,676 HHs in Phase 1 service area of which 991 are FHH, 122 ID Poor 1 and 34 ID Poor 2 HHs.</p> <p>Responsibility: DPWTs/PIUs</p>	<p>Not yet due: Q4 2023</p> <p>Approximately 4,000 HH are included in the design (23 Feb 2021 presentation)</p> <p>Target is included in the TOR for the NGO to be subcontracted for IEC.</p>	<p>The WW services will be extended to the service area included in catchment 1, 2, & 3, which by the design team has an estimated 4,000 HH and thus about 14% lower than the HH target. The share of FHH and ID Poor HH will depend on the socio-economic situation of the service area. The service area covers 030502 Kampong Cham, 030504 Veal Vong, about 22% of the settled area of Boeng Kok, and 3% of the settled area of 030503 Sombuur Meas Sangkats.</p> <p>Targets in left column established in the PAM, Table 8.1 GAP. Targets in the standalone GAP, July 2018 are higher than those in the PAM for some variables (4,676 HHs in Phase 1 service area of which 1,153 are FHHs, 154 HHs are ID Poor 1, and 34 HHs are ID Poor 2).</p>
<p>Target 2: Expanded and improved solid waste collection services will cover 2,416 FHHs.</p> <p>Responsibility: Municipality</p>	<p>Not yet due: Q4 2023</p> <p>Targets are included in the TOR for the NGO to be subcontracted for IEC.</p>	<p>Indicator is not relevant in respect of the PMC TOR, which only includes services related to landfill construction and provision of equipment.</p> <p>According to the Commune Database 2018, 0305 Krong Kampong Cham had 2,311 FHH, i.e. less than the target.</p>
<p>Target 3: 30% of staff employed in operation and maintenance are women (baseline 2016: 0).</p> <p>Responsibility: PIUs/Cities/organizations, incl. Landfill operation, waste collection operation, and the urban service unit</p>	<p>Not yet due: Q4 2023</p>	<p>The employing organisations to be assigned responsibility for the target.</p> <p>PMC to obtain and review baseline in operating companies.</p> <p>Include 30% of women in the training invitation for O&M staff to ensure target can be met.</p>
<p>Action 1: Pilot project at Sangkat/Commune level on community management of flood resilience, gender equity in post-flood clean-up, and town beautification.</p> <p>Responsibility: DPWTs/PIUs, NGO</p>	<p>Not yet due: Q4 2022</p> <p>The Pilot projects are included in the TOR for the NGO to be subcontracted for IEC.</p>	<p>Indicator is not relevant in respect of the PMC TOR, which only includes services related to wastewater collection and landfill construction and provision of equipment.</p>

Output 1.2: Urban environmental infrastructure in Kratie improved		
<p>Target 4: Wastewater collection connections provided free-of charge to 2,688 HHs in Phase 1 service area of which 238 are FHH, 111 ID Poor 1 and 246 ID Poor 2 HHs.</p> <p>Responsibility: DPWTs/PIUs</p>	<p>Not yet due: Q4 2023</p> <p>Approximately 1,700-1,800 HH are included in the design (23 Feb 2021 presentation)</p> <p>Target is included in the TOR for the NGO to be subcontracted for IEC.</p>	<p>The WW services will be extended to the service area included in catchment 1, 2, & 3, which by the design team has an estimated 1,700-1,800 HH and thus about 33% lower than the HH target. The share of FHH and ID Poor HH will depend on the socio-economic situation of the service area. The service area covers an estimated 95% of the settled areas of 10029 Kracheh and 100211 Roka Kandal Sangkats.</p> <p>Targets in left column established in the PAM, Table 8.1 GAP and match those of the standalone GAP, July 2018.</p>
<p>Target 5: Expanded and improved solid waste collection services will cover 825 FHHs.</p> <p>Responsibility: Municipality</p>	<p>Not yet due: Q4 2023</p> <p>Targets are included in the draft TOR for the NGO to be subcontracted for IEC.</p>	<p>Indicator is not relevant in respect of the PMC TOR, which only includes services related to landfill construction and provision of equipment.</p> <p>According to the Commune Database 2018, 1002 Krong Kracheh had 888 FHH, so nearly all FHH should be covered by the services to meet the target.</p>
<p>Target 6: 30% of staff employed in operation and maintenance are women (baseline 2016: 0).</p> <p>Responsibility: PIUs/Cities/organizations, incl. Landfill operation, waste collection operation, and the urban service unit</p>	<p>Not yet due: Q4 2023</p>	<p>Refer above.</p>
<p>Action 2: Pilot project at Sangkat/Commune level on community management of flood resilience, gender equity in post-flood clean-up, and town beautification.</p> <p>Responsibility: DPWTs/PIUs, NGO</p>	<p>Not yet due: Q4 2022</p> <p>The Pilot projects are included in the TOR for the NGO to be subcontracted for IEC.</p>	<p>Refer above.</p>
Output 1.3: Urban environmental infrastructure in Stung Treng improved		
<p>Target 7: Wastewater collection connections provided free-of charge to 2,253 HHs in Phase 1 service area of which 163 are FHH, 122 ID Poor 1 and 6 ID Poor 2 HHs.</p> <p>Responsibility: DPWTs/PIUs</p>	<p>Not yet due: Q4 2023</p> <p>Preliminary estimate of 2,000 HH in the service area by the design team (23 Feb 2021 presentation)</p> <p>Target is included in the TOR for the NGO to be subcontracted for IEC.</p>	<p>The WW services will be extended to the proposed Phase 1 service area, which by the design team has an estimated 2,000 HH and thus about 11% lower than the HH target. The share of FHH and ID Poor HH will depend on the socio-economic situation of the service area. The service area covers parts of the 190402 Srah Ruessei, 190403 Preah Bat, and 190401 Stung Treng Sangkats.</p> <p>Targets in left column established in the PAM, Table 8.1 GAP. Targets differ in the standalone GAP, July 2018 for some variables (2,253 HHs in Phase 1 service area, of which 277 are FHHs, 14 are ID Poor 1, 44 are ID Poor 2).</p>

<p>Target 8: Expanded and improved solid waste collection services will cover 446 FHHs.</p> <p>Responsibility: Municipality</p>	<p>Not yet due: Q4 2023</p> <p>Targets are included in the TOR for the NGO to be subcontracted for IEC.</p>	<p>Indicator is not relevant in respect of the PMC TOR, which only includes services related to landfill construction and provision of equipment.</p> <p>According to the Commune Database 2018, 1904 Krong Stueng Traeng had 718 FHH of which 499 are in the more urbanised area south of the Sekong and 219 in the largely rural Sameakki Commune.</p>
<p>Target 9: 30% of staff employed in operation and maintenance are women (baseline 2016: 0).</p> <p>Responsibility: PIUs/Cities/organizations, incl. Landfill operation, waste collection operation, and the urban service unit</p>	<p>Not yet due: Q4 2023</p>	<p>Refer above.</p>
<p>Action 3: Pilot project at Sangkat/Commune level on community management of flood resilience, gender equity in post-flood clean-up, and town beautification.</p> <p>Responsibility: DPWTs/PIUs, NGO</p>	<p>Not yet due: Q4 2022</p> <p>The Pilot projects are included in the draft TOR for the NGO to be subcontracted for IEC.</p>	<p>Refer above.</p>
<p>Output 2: Institutional effectiveness, and policy and planning environment for regional economic connectivity enhanced</p>		
<p>Action 4: Provincial Development Strategies approved include social inclusion and gender equity components.</p> <p>Responsibility: MLMUPLC/PMC</p>	<p>Not yet due: Q4 2023</p> <p>Land Use Master Plan reviews for Kratie and Kampong Cham cover social inclusion and gender equity components.</p> <p>PSPs under development for Kampong Cham, Kratie, Stung Treng (and Banteay Meanchey TS-2).</p>	<p>Scope has changed to Provincial Spatial Plan (PSP). Therefore, action is proposed changed to: "Provincial Spatial Plan approved include social inclusion and gender equity components." Scope of the PSPs follows the Provincial Spatial Planning Handbook, MLMUPLC. Change of action may be considered at MTR.</p>
<p>Target 10: In development of Provincial Development Strategy and implementation of ICT initiatives 30% and 50%, respectively, of participants from government agencies will be female staff.</p> <p>Responsibility: DPWTs/PIUs</p>	<p>Not yet due: Q2 2022</p> <p>Gender of committee members and secretariat members involved in the PSPs are as follows:</p> <p>Kampong Cham</p> <ul style="list-style-type: none"> • Committee: 3 F of 22, 14% • Secretariat: 0 F of 13, 0% 	<p>Scope has changed to Provincial Spatial Plan. Therefore, target is proposed changed to: "In development of Provincial Spatial Plan and implementation of ICT initiatives 30% and 50%, respectively, of participants from government agencies will be female staff." Change of target may be considered at MTR.</p> <p>The Provincial Department of Land Management, Urban Planning, Construction, and Cadastre (PDLMUPCC) appoints the participants of the committee and secretariat from government agencies based on position, which make it difficult to achieve specific gender ratio.</p>

	<p>Kratie</p> <ul style="list-style-type: none"> • Committee: 1 F of 34, 3% • Secretariat: 0 F of 28, 0% <p>Stung Treng:</p> <ul style="list-style-type: none"> • Committee: 4 F of 35, 11% • Secretariat: 4 F of 22, 18% <p>Banteay Meanchey (TS-2)</p> <ul style="list-style-type: none"> • Committee: 3 F of 40, 8% • Secretariat: 3 F of 36, 8% 	<p>Female participation will be monitored but achieving the target is beyond the control of the PMC.</p>
<p>Target 11: In workshops related to Provincial Development Strategy and ICT initiatives 50% of participants will be women</p> <p>Responsibility: DPWTs/PIUs, PMC and ICTM Consultant</p>	<p>Overdue: Q4 2019</p> <p>Kampong Cham on 30-Nov 2020:</p> <p>Total participants: 3 F of 55, 5%</p> <p>Kratie & Stung Treng 15-Jul 2021:</p> <p>Total participants: 7F, 29M, 12 not reported of 48 participants.</p> <p>Banteay Meanchey, Serei Saophoan (TS-2) on 26-Nov 2020:</p> <p>Total participants: 6 F of 66, 9%</p> <p>Banteay Meanchey, Serei Saophoan (TS-2) on 9-Sep-2021:</p> <p>Total participants: 2 F of 27, 7%</p>	<p>Scope has changed to Provincial Spatial Plan. Therefore, target is proposed changed to: "In workshops related to Provincial Spatial Plan and ICT initiatives 50% of participants will be women." Change of target may be considered at MTR. The scope change led to some delays of workshops.</p> <p>The Provincial Department of Land Management, Urban Planning, Construction, and Cadastre (PDLMUPCC) determines the participants of stakeholder meetings based on their positions as government officials. The PDLMUPCC has been explained the targets of the GAP and suggested to increase female participants by inviting NGOs and CSOs, including women's groups and private sector. The PDLMUPCC has stated that they will try to increase the number of female participants.</p> <p>ICT initiatives have not commenced yet and are not under PMC scope.</p> <p>Female participation will be monitored but achieving the target is beyond the control of the PMC.</p>
<p>Action 5: Existing staff responsible for financial management and administration (majority women) to be trained in ICTM</p> <p>Responsibility: DPWTs/PIUs, ICTM Consultant</p>	<p>Not yet due: Q4 2022</p>	<p>ICT initiatives have not commenced yet and are not under PMC scope. ICTM Consultant to conduct training in ICTM.</p>

<p>Target 12: At least 120 government staff (at least 50% women) in the provincial governments trained in ICT skills to operate the ICTM services (2017 baseline: 0)</p> <p>Responsibility: MPWT/PMU, ICTM Consultant</p>	<p>Not yet due: Q4 2023</p>	<p>ICT initiatives have not commenced yet and are not under PMC scope.</p> <p>ICTM Consultant to review baseline data and conduct training.</p>
<p>Target 13: At least 60 government staff (at least 25% women) in the implementing agencies gained new technical, operational and maintenance knowledge and skills on wastewater treatment facility, drainage systems and controlled landfill (2017 baseline: 0)</p> <p>Responsibility: MPWT/PMU</p>	<p>Not yet due: Q4 2023</p>	<p>Pre- and post-training questionnaires will be distributed in coordination with the Capacity Development and Training Specialist.</p> <p>At least 25% women participating in training or workshop related to those skills will be included in the workshop/training invitation letter.</p> <p>Target to be discussed at GAP orientation.</p>
<p>Target 14: Women's representation in PMU/PIU decision making and technical positions 20% (PMU and PIU Steung Treng) and 25% (PIUs Kampong Cham and Kratie). (Baseline (2011-2015) for PMU: MPWT 17%; PDPWT cumulative 14.85% women in managerial positions, PIU: PDPWT percentage of managerial positions occupied by women: Kampong Cham: 25% Kratie 22%; Stung Treng 18%)</p> <p>Responsibility: Steering Committee responsible for ensuring % of women in Committee PMU and PIU</p>	<p>Staff lists and gender lists have been collected by the PMC from the PMU and PIUs. Women representation are as follows:</p> <p>PMU: 0 of 10 (0% versus a target of 20%)</p> <p>PIU Steung Treng: 0 of 9 (0% versus a target of 20%)</p> <p>PIU Kampong Cham: 1 of 9 (11% versus a target of 25%)</p> <p>PIU Kratie: 0 of 9 (0% versus a target of 20%)</p>	<p>PMU and PIUs are already established. PIUs are composed of members from PDPWT, municipalities, and provincial local administration staff. Gender ratio of members reflects those of the organizations these are appointed from.</p> <p>Targets to be discussed at GAP orientation.</p>
<p>Action 6: Orientation on GAP implementation, monitoring, and reporting provided to PMU/PIU staff, and local implementation partners.</p> <p>Responsibility: MPWT/PMU, DPWTs/PIUs</p>	<p>Overdue: Q1 2019</p>	<p>National Gender Consultant has mobilised with the PMC, while Gender Focal Point in the PMU (EA) is yet to mobilise.</p>
<p>Action 7: GAP integrated in overall work plan, budget and PPMS.</p> <p>Responsibility: MPWT/PMU, DPWTs/PIUs, PMC</p>	<p>GAP has been integrated in overall workplan, budget and PPMS</p>	

Action 8: Collection and monitoring of sex-disaggregated data with gender sensitive indicators incorporated in the PPMS and reflected in quarterly reports and GAP monitoring reports using ADBs template.

Responsibility: MPWT/PMU/PMC

GAP Monitoring Template received and annexed the quarterly reports.

Annex G: Procurement Plan

CTDP4 PROCUREMENT PLAN

Basic Data

Project Name: Fourth Greater Mekong Subregion Corridor Towns Development Project	
Project Number: 50099-002	Approval Number: 3686/0593/0592
Country: Cambodia	Executing Agency: Ministry of Public Works and Transport
Project Procurement Risk: Medium	Implementing Agency: N/A
Project Financing Amount: US\$ 88,500,000 ADB Financing: US\$ 80,000,000 Cofinancing (ADB Administered): US\$ 500,000 Non-ADB Financing: US\$ 8,000,000	Project Closing Date: 30 June 2024
Date of First Procurement Plan: 1 August 2018	Date of this Procurement Plan: 14 August 2020 Version 3
Advance Contracting: No	e-GP: No

A. Methods, Thresholds, Review and 18-Month Procurement Plan

1. Procurement and Consulting Methods and Thresholds

Except as the Asian Development Bank (ADB) may otherwise agree, the following process thresholds shall apply to procurement of goods and works.

Procurement of Goods and Works		
Method	Threshold	Comments
International Competitive Bidding for Goods	US\$ 1,000,000 and Above	
National Competitive Bidding for Goods	Between US\$ 100,000 and US\$ 999,999	The first NCB is subject to prior review, thereafter post review.
Shopping for Goods	Up to US\$ 99,999	
International Competitive Bidding for Works	US\$ 3,000,000 and Above	
National Competitive Bidding for Works	Between US\$ 100,000 and US\$ 2,999,999	The first NCB is subject to prior review, thereafter post review.
Shopping for Works	Up to US\$ 99,999	

Consulting Services	
Method	Comments
Quality- and Cost-Based Selection for Consulting Firm	80:20 and 90:10; FTP
Quality-Based Selection for Consulting Firm	
Individual Consultant Selection for Individual Consultant	

2. Goods and Works Contracts Estimated to Cost \$1 Million or More

The following table lists goods and works contracts for which the procurement activity is either ongoing or expected to commence within the next 18 months.

Package Number	General Description	Estimated Value	Procurement Method	Review (Prior/Post)	Bidding Procedure	Advertisement Date (quarter/year)	Comments
CW03	Kampong Cham Solid Waste Management Subproject	6,180,000.00	ICB	Prior	1S1E	Q4 / 2020	Prequalification of Bidders: N Domestic Preference Applicable: N Bidding Document: Small Works
CW04	Kratie Solid Waste Management Subproject	5,570,000.00	ICB	Prior	1S1E	Q4 / 2020	Prequalification of Bidders: N Domestic Preference Applicable: N Bidding Document: Small Works
CW05	Stung Treng Solid Waste Management Subproject	5,920,000.00	ICB	Prior	1S1E	Q4 / 2020	Prequalification of Bidders: N Domestic Preference Applicable: N Bidding Document: Small Works
CW06	Kampong Cham Wastewater and Drainage Subproject	17,260,000.00	ICB	Prior	1S1E	Q3 / 2020	Prequalification of Bidders: N Domestic Preference Applicable: N Bidding Document: Large Works
CW07	Kratie Wastewater and Drainage Subproject	14,140,000.00	ICB	Prior	1S1E	Q4 / 2020	Prequalification of Bidders: N Domestic Preference Applicable: N Bidding Document: Large Works

CW08	Stung Treng Wastewater and Drainage Subproject	14,450,000.00	ICB	Prior	1S1E	Q4 / 2020	Prequalification of Bidders: N Domestic Preference Applicable: N Bidding Document: Large Works
G02	Solid Waste Collection Vehicles and Landfill Equipment	1,350,000.00	ICB	Prior	1S1E	Q4 / 2021	Prequalification of Bidders: N Domestic Preference Applicable: N Bidding Document: Goods

3. Consulting Services Contracts Estimated to Cost \$100,000 or More

The following table lists consulting services contracts for which the recruitment activity is either ongoing or expected to commence within the next 18 months.

Package Number	General Description	Estimated Value	Recruitment Method	Review (Prior/Post)	Advertisement Date (quarter/year)	Type of Proposal	Comments
CS02	ICT for Public Management	1,000,000.00	QCBS	Prior	Q4 / 2020	FTP	Assignment: International Quality-Cost Ratio: 80:20

4. Goods and Works Contracts Estimated to Cost Less than \$1 Million and Consulting Services Contracts Less than \$100,000 (Smaller Value Contracts)

The following table lists smaller-value goods, works and consulting services contracts for which the activity is either ongoing or expected to commence within the next 18 months.

Goods and Works								
Package Number	General Description	Estimated Value	Number of Contracts	Procurement Method	Review (Prior/Post)	Bidding Procedure	Advertisement Date (quarter/year)	Comments
CW01	Kratie Town Centre Environmental Enhancement	750,000.00	1	NCB	Prior	1S1E	Q4 / 2020	Prequalification of Bidders: N Domestic Preference Applicable: N Bidding Document: Small Works

CW02	Stung Treng Town Centre Environmental Enhancement	750,000.00	1	NCB	Post	1S1E	Q4 / 2020	Prequalification of Bidders: N Domestic Preference Applicable: N Bidding Document: Small Works
------	---	------------	---	-----	------	------	-----------	--

Consulting Services								
Package Number	General Description	Estimated Value	Number of Contracts	Recruitment Method	Review (Prior/Post)	Advertisement Date (quarter/year)	Type of Proposal	Comments
ICS02	Financial Management Specialist	80,000.00	1	ICS	Prior	Q4 / 2020		Assignment : National Expertise: Financial management
ICS03	Procurement Specialist	80,000.00	1	ICS	Prior	Q4 / 2020		Assignment : National Expertise: Procurement

B. Indicative List of Packages Required Under the Project

The following table provides an indicative list of goods, works and consulting services contracts over the life of the project, other than those mentioned in previous sections (i.e., those expected beyond the current period).

Goods and Works							
Package Number	General Description	Estimated Value (cumulative)	Estimated Number of Contracts	Procurement Method	Review (Prior/Post)	Bidding Procedure	Comments
None							

Consulting Services							
Package Number	General Description	Estimated Value	Number of Contracts	Recruitment Method	Review (Prior/Post)	Type of Proposal	Comments
None							

C. List of Awarded and On-going, and Completed Contracts

The following tables list the awarded and on-going contracts, and completed contracts.

1. Awarded and Ongoing Contracts

Goods and Works							
Package Number	General Description	Estimated Value	Awarded Contract Value	Procurement Method	Advertisement Date (quarter/year)	Date of ADB Approval of Contract Award	Comments
G01	Vehicles (5 units)	190,000.00	160,000.00	NCB	Q1 / 2020	22-JUN-20	

Consulting Services							
Package Number	General Description	Estimated Value	Awarded Contract Value	Recruitment Method	Advertisement Date (quarter/year)	Date of ADB Approval of Contract Award	Comments
PMCS-CS01	Project Management, Detailed Engineering Design, Construction Supervision, Provincial Development Strategy and Capacity Building	6,100,000.00	5,834,010.83	QCBS	Q2 / 2018	20-JUN-19	The contract is both under CAM; TS and CAM: GMS4
ICS01	Project Implementation Specialist	250,000.00	280,000.00	ICS	Q3 / 2019	25-MAR-20	Mr. Greesh Kumar Sharma

D. National Competitive Bidding

A. Regulation and Reference Documents

1. The procedures to be followed for national competitive bidding shall be those set forth for the “National Competitive Bidding” method in the Government’s Procurement Manual issued under Sub-Decree Number 74 ANKR.BK, updated version dated 22 May 2012 with the clarifications and modifications described in the following paragraphs. These clarifications and modifications are required for compliance with the provisions of the Procurement Guidelines.

2. For the procurement of ADB financed contracts under National Competitive Bidding (NCB) procedures, the use of harmonized national bidding documents (NCB and National Shopping) developed in consultation with development partners including ADB, is mandatory except where the Government and ADB have agreed to amendments to any part of the documents. The Procurement Manual also advises users to check the ADB website from time to time for any update on ADB documents, which form the basis, among others, of the existing harmonized national bidding documents.

B. Procurement Procedures

1. Application

3. Contract packages subject to National Competitive Bidding procedures will be those

identified as such in the project Procurement Plan. Any change to the mode of procurement of any procurement package in the Procurement Plan shall be made through updating of the Procurement Plan, and only with prior approval of ADB.

2. Sanctioning

4. Bidders shall not be declared ineligible or prohibited from bidding on the basis of barring procedures or sanction lists, except individuals and firms sanctioned by ADB, without prior approval of ADB.

3. Rejection of all Bids and Rebidding

5. The Borrower shall not reject all bids and solicit new bids without ADB's prior concurrence. Even when only one or a few bids is/are submitted, the bidding process may still be considered valid if the bid was satisfactorily advertised and prices are reasonable in comparison to market values.

4. Advertising

6. Bidding of NCB contracts shall be advertised on the ADB website via the posting of the Procurement Plan. Borrowers have the option of requesting ADB to post specific notices in the ADB website.

C. Bidding Documents

5. Use of Bidding Documents

7. The Standard National Competitive Bidding Documents provided with the Government's Procurement Manual shall be used to the extent possible both for the master bidding documents and the contract-specific bidding documents. The English language version of the procurement documents shall be submitted for ADB review and approval in accordance with agreed review procedures (post and prior review) as indicated in the Procurement Plan. The ADB-approved procurement documents will then be used as a model for all procurement financed by ADB for the project.

6. Bid Evaluation

8. Bidders shall not be eliminated from detailed evaluation on the basis of minor, non-substantial deviations.

9. A bidder shall not be required, as a condition for award of contract, to undertake obligations not specified in the bidding documents or otherwise to modify the bid as originally submitted.

7. Employer's Right to Accept or Reject Any or All Bids

10. The decision of the Employer to accept or reject any or all bids shall be made in a transparent manner and involve an obligation to inform of the grounds for the decision through the bid evaluation report.

8. ADB Policy Clauses

11. A provision shall be included in all NCB works and goods contracts financed by ADB requiring suppliers and contractors to permit ADB to inspect their accounts and records and

other documents relating to the bid submission and the performance of the contract, and to have them audited by auditors appointed by ADB.

12. A provision shall be included in all bidding documents for NCB works and goods contracts financed by ADB stating that the Borrower shall reject a proposal for award if it determines that the bidder recommended for award has, directly or through an agent, engaged in corrupt, fraudulent, collusive, or coercive practices in competing for the contract in question.

13. A provision shall be included in all bidding documents for NCB works and goods contracts financed by ADB stating that ADB will declare a firm or individual ineligible, either indefinitely or for a stated period, to be awarded a contract financed by ADB, if it at any time determines that the firm or individual has, directly or through an agent, engaged in corrupt, fraudulent, collusive, coercive or obstructive practices or any integrity violation in competing for, or in executing, ADB-financed contract.

Annex H: Compliance with Loan and Grant Covenants

No.	Covenant	Reference	Status of Compliance
	CTDP4 Loan 3686		
1	In the carrying out of the project and operation of the project facilities, the Borrower shall perform, or cause to be performed, all obligations set forth in Schedule 5 to this Loan Agreement.	Section 4.01	Ongoing
2	The Borrower shall cause the Project Executing Agency to (i) maintain separate accounts and records for the projects; (ii) prepare annual financial statements for the project in accordance with financial reporting standard acceptable to ADB; (iii) have such financial statements audited annually by independent auditors whose qualifications, experience, and terms of reference are acceptable to ADB, in accordance with auditing standards, acceptable to ADB; (iv) as part of each such audit, have the auditors prepare a report, which includes the auditors' opinion(s) on the financial statements and the use of the Loan proceeds, and a management letter (which sets out the deficiencies in the internal control of the project that were identified in the course of the audit, if any); and (v) furnish to ADB, no later than 6 months after the end of each related fiscal year, copies of such audited financial statements, audit report, and management letter, all in the English language, and such other information concerning these documents and the audit thereof as ADB shall from time to time reasonably request.	Section 4.02 (a)	Ongoing
3	ADB shall disclose the annual audited financial statements for the project and the opinion of the auditors on the financial statements within 14 days of the date of ADB's confirmation of their acceptability by posting them on ADB's website.	Section 4.02 (b)	Ongoing
4	The Borrower shall enable ADB, upon ADB's request, to discuss the financial statements for the project and the Borrower's financial affairs where they relate to the Project with the auditors appointed pursuant to subsection (a)(iii) hereinabove and shall authorize and require any representative of such auditors to participate in any such discussions requested by ADB. This is provided that such discussions shall be conducted only in the presence of an authorized officer of the Borrower, unless the Borrower shall otherwise agree.	Section 4.02 (c)	Ongoing
5	The Borrower shall enable ADB's representatives to inspect the Project, the Goods and Works, and any relevant records and documents.	Section 4.03	Ongoing
	CTDP4 Grant 0592		
6	In the carrying out of the project and operation of the project facilities, the Recipient shall perform, or cause to be performed, all obligations set forth in Schedule 5 to the ADB Loan Agreement.	Section 4.01	Ongoing
7	The Recipient shall cause the Project Executing Agency to (i) maintain separate accounts and records for the projects; (ii) prepare annual financial statements for the project in accordance with financial reporting standard acceptable to ADB; (iii) have such financial statements audited annually by independent auditors whose qualifications, experience, and terms of reference are acceptable to ADB, in accordance with auditing standards, acceptable to ADB; (iv) as part of each such audit, have the auditors prepare a report, which includes the auditors' opinion(s) on the financial statements and the use of the Grant proceeds, and management letter (which sets out the deficiencies in the internal control of the project that were identified in the course of the audit, if any); and (v) furnish to ADB, no later than 6 months after the end of each related fiscal year, copies of such audited financial statements, audit report, and management letter, all in the English language, and such other information concerning these documents and the audit thereof as ADB shall from time to time reasonably request.	Section 4.02 (a)	Ongoing
8	ADB shall disclose the annual audited financial statements for the project and the opinion of the auditors on the financial statements within 14 days of the date of ADB's confirmation of their acceptability by posting them on ADB's website.	Section 4.02 (b)	Ongoing
9	The Recipient shall enable ADB, upon ADB's request, to discuss the financial statements for the project and the Borrower's financial affairs where they relate to the Project with the auditors appointed pursuant to subsection (a)(iii) hereinabove and shall authorize and require any representative of such auditors to participate in any such discussions requested by ADB. This is provided that such discussions shall be conducted only in the presence of an authorized officer of the Recipient, unless the Recipient shall otherwise agree.	Section 4.02 (c)	Ongoing

No.	Covenant	Reference	Status of Compliance
10	The Recipient shall enable ADB's representatives to inspect the Project, the Goods and Works, and any relevant records and documents.	Section 4.03	Ongoing
CTDP4 Grant 0593			
11	In the carrying out of the project and operation of the project facilities, the Recipient shall perform, or cause to be performed, all obligations set forth in Schedule 5 to the ADB Loan Agreement.	Section 4.01	Ongoing
12	The Recipient shall cause the Project Executing Agency to (i) maintain separate accounts and records for the projects; (ii) prepare annual financial statements for the project in accordance with financial reporting standard acceptable to ADB; (iii) have such financial statements audited annually by independent auditors whose qualifications, experience, and terms of reference are acceptable to ADB, in accordance with auditing standards, acceptable to ADB; (iv) as part of each such audit, have the auditors prepare a report, which includes the auditors' opinion(s) on the financial statements and the use of the Grant proceeds, and management letter (which sets out the deficiencies in the internal control of the project that were identified in the course of the audit, if any); and (v) furnish to ADB, no later than 6 months after the end of each related fiscal year, copies of such audited financial statements, audit report, and management letter, all in the English language, and such other information concerning these documents and the audit thereof as ADB shall from time to time reasonably request.	Section 4.02 (a)	Ongoing
13	ADB shall disclose the annual audited financial statements for the project and the opinion of the auditors on the financial statements within 14 days of the date of ADB's confirmation of their acceptability by posting them on ADB's website.	Section 4.02 (b)	Ongoing
14	The Recipient shall enable ADB, upon ADB's request, to discuss the financial statements for the project and the Recipient's financial affairs where they relate to the Project with the auditors appointed pursuant to subsection (a)(iii) hereinabove and shall authorize and require any representative of such auditors to participate in any such discussions requested by ADB. This is provided that such discussions shall be conducted only in the presence of an authorized officer of the Recipient, unless the Recipient shall otherwise agree.	Section 4.02 (c)	Ongoing
15	The Recipient shall enable ADB's representatives to inspect the Project, the Goods and Works, and any relevant records and documents.	Section 4.03	Ongoing
16	The Recipient acknowledges and agrees that this Grant Agreement is entered into by ADB, not in its individual capacity, but as trustee of the Republic of Korea e-Asia and Knowledge Partnership Fund. Accordingly, the Recipient agrees that (a) it may only withdraw Grant proceeds to the extent that ADB has received proceeds for the Grant from the Republic of Korea e-Asia and Knowledge Partnership Fund and such proceeds has not been suspended or cancelled in whole or in part by the Republic of Korea e-Asia and Knowledge Partnership Fund pursuant to the Cofinancing Agreement, and (b) that ADB does not assume any obligations or responsibilities of the Republic of Korea e-Asia and Knowledge Partnership Fund in respect of the Project or the Grant other than those set out in this Grant Agreement.	Section 4.04	Ongoing

nnex I: Financial Management Action Plan

Risk description	Impact	likelihood	Overall Risk Assessment	Mitigation measures/ Responsibility	Timeline	Responsibility	Actions Taken/ Status	Next Steps
Inherent Risk								
The Standard Operating Procedure for externally financed projects in Cambodia (May 2012) stipulates that assets must be subject to careful asset management, but in practice there is no regular monitoring/ inventory. There is a risk of loss of asset due to poor maintenance.	High	Unlikely	Substantial	<ul style="list-style-type: none"> - Update Fixed Asset Book every year during and after project implementation. - Project will develop ICT-based public asset management and deploy them in three provinces with capacity development training. - Train government staff in fixed asset management including linkage to asset preventive maintenance activities. 	<ul style="list-style-type: none"> - Throughout the project duration - Q4 2022 and Q4 2023 (related to the DMF milestone 2.4) - Q4 2022 and Q4 2023 (related to the DMF milestone 2.4) 	<p>MPWT/PMU</p> <p>MPWT/PMU</p>	<p>The government staff were trained on the updated FMM (2019) including asset management in various groups by MEF in later 2019 and early 2020.</p> <p>The government staff were trained on the updated FMM (2019) including asset management in various groups by MEF in later 2019 and early 2020.</p>	The record and asset management is stated in the Financial Management (FMM) issued by MEF, RGC in Dec 2019
Control Risk								
Internal audit–Lack of internal audit system in the provincial governments/DPWTs	Low	Likely	Moderate	<ul style="list-style-type: none"> - No transaction and fund flow of ADB loan and grant proceeds to the DPWTs/PIUs 	<ul style="list-style-type: none"> - Throughout the project 	MPWT/PMU	This is to confirm that no fund of ADB has transferred to DPWT/IPUS	

Information systems—Improper record keeping or mistakes because of the excel-based financial management system in the provincial governments/DPWTs	Low	Likely	Moderate	<ul style="list-style-type: none"> - PMU and PIUs will undertake regular backups of all financial, accounting and project related data and appropriate security measures over backed-up data shall be in place. - MEF and MPWT/PMU ensure to engage the qualified audit company under the project 	<ul style="list-style-type: none"> - Throughout the project -Q2 2020 (related to the DMF Project Management Activities) 	<p>MPWT/P MU/PIUs</p> <p>MEF and MPWT/ PMU</p>	<ul style="list-style-type: none"> - PMU undertakes regular backups of all financial, accounting and project related data and appropriate security measures over backed-up data in external HD which is kept in the safe. - Complied with; engaged a qualified audit company under the project 	
Total Control Risk			Moderate					
